


# EPDP Phase 2A - Summary Timeline

30 Jun 2021

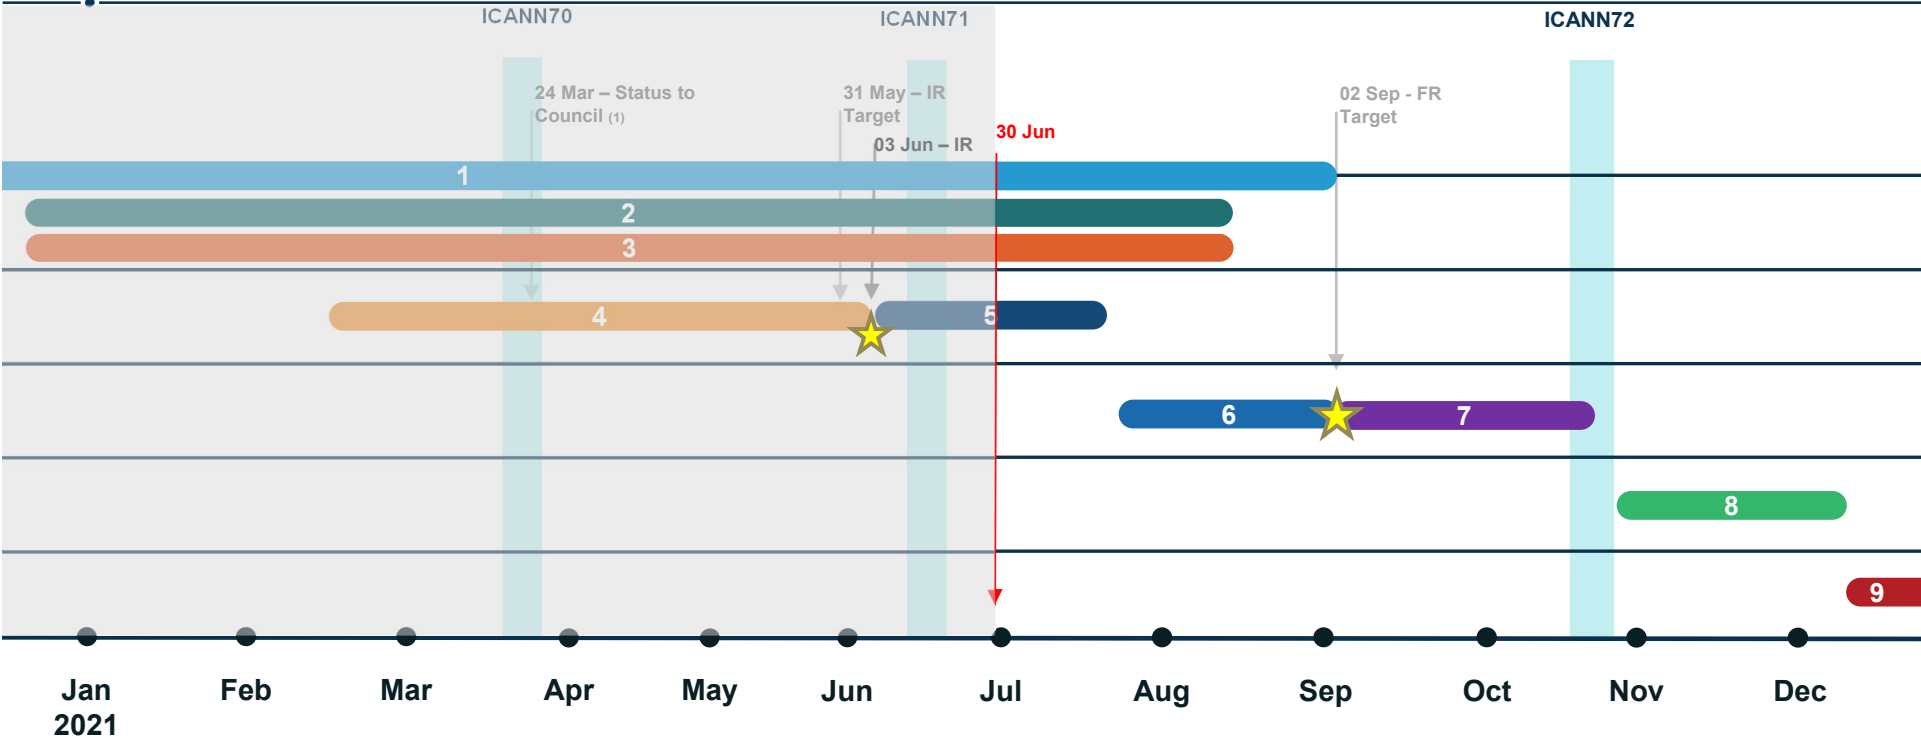

1 Project Management, Workplan, & Factsheet

2 EPDP-P2A Legal vs. Natural Deliberations

3 EPDP-P2A Unique Contacts Deliberations

4 Construct Initial Report

5 Public Comment on Initial Report

6 Review of Public Comment & Submission of Final Report

7 Council Consideration of Final Report

8 Public Comment during Board Consideration

9 Board Consideration

Complete: 78%   Status: ●   Health: ■




1) Updated GNSO Council on probability to achieve consensus recommendations



EPDP-P2A - Plenary			
Represented Group / Member & Alternate	Invited	Attended	% Attendance
<b>At-Large Advisory Committee (ALAC)</b>	<b>50</b>	<b>49</b>	<b>98.0%</b>
Alan Greenberg	25	24	96.0%
Hadia Elminiawi	25	25	100.0%
<b>Commercial Business Users Constituency (BC)</b>	<b>70</b>	<b>66</b>	<b>94.3%</b>
Margie Milam	24	22	91.7%
Mark Svancarek	25	24	96.0%
Steve DelBianco	21	20	95.2%
<b>GNSO Council</b>	<b>63</b>	<b>56</b>	<b>88.9%</b>
Brian Beckham	18	14	77.8%
Keith Drazek	24	24	100.0%
Philippe Fouquart	21	18	85.7%
<b>Governmental Advisory Committee (GAC)</b>	<b>87</b>	<b>75</b>	<b>86.2%</b>
Christopher Lewis-Evans	25	23	92.0%
Laureen Kapin	25	22	88.0%
Melina Stroungi	24	17	70.8%
Ryan Carroll	9	9	100.0%
Velimira Nemiguentcheva-Grau	4	4	100.0%
<b>ICANN Board</b>	<b>60</b>	<b>52</b>	<b>86.7%</b>
Becky Burr	25	20	80.0%
León Felipe Sánchez Ambia	11	11	100.0%
Matthew Shears	24	21	87.5%
<b>Intellectual Property Constituency (IPC)</b>	<b>50</b>	<b>46</b>	<b>92.0%</b>
Brian King	25	24	96.0%
Jan Janssen	25	22	88.0%
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>	<b>50</b>	<b>48</b>	<b>96.0%</b>
Amy Bivins	25	23	92.0%
Brian Gutterman	25	25	100.0%
<b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>	<b>51</b>	<b>47</b>	<b>92.2%</b>
Christian Dawson	25	23	92.0%
Suman Lal Pradhan	1	1	100.0%
Thomas Rickert	25	23	92.0%
<b>Non-Commercial Stakeholder Group (NCSG)</b>	<b>131</b>	<b>96</b>	<b>73.3%</b>
Bruna Santos	7	7	100.0%
David Cake	25	22	88.0%
Manju Chen	25	24	96.0%
Milton Mueller	24	16	66.7%
Stefan Filipovic	25	5	20.0%
Stephanie Perrin	25	22	88.0%
<b>Registrar Stakeholder Group (RrSG)</b>	<b>122</b>	<b>106</b>	<b>86.9%</b>
James Bladel	23	9	39.1%
Matt Serlin	21	21	100.0%
Owen Smigelski	23	23	100.0%
Sarah Wyld	25	24	96.0%
Theo Geurts	5	5	100.0%
Volker Greimann	25	24	96.0%
<b>Registry Stakeholder Group (RySG)</b>	<b>133</b>	<b>130</b>	<b>97.7%</b>
Alan Woods	25	24	96.0%
Amr Elsadr	18	18	100.0%
Beth Bacon	18	18	100.0%
Marc Anderson	25	25	100.0%
Matthew Crossman	25	23	92.0%
Sean Baseri	22	22	100.0%
<b>Security and Stability Advisory Committee (SSAC)</b>	<b>48</b>	<b>47</b>	<b>97.9%</b>
Ben Butler	2	1	50.0%
Greg Aaron	2	2	100.0%
Steve Crocker	19	19	100.0%
Tara Whalen	25	25	100.0%
<b>Grand Total</b>	<b>915</b>	<b>818</b>	<b>89.4%</b>


EPDP-P2A - Legal Committee			
Represented Group / Member & Alternate	Invited	Attended	% Attendance
<b>At-Large Advisory Committee (ALAC)</b>	<b>11</b>	<b>9</b>	<b>81.8%</b>
Hadia Elminiawi	11	9	81.8%
<b>Commercial Business Users Constituency (BC)</b>	<b>11</b>	<b>11</b>	<b>100.0%</b>
Margie Milam	11	11	100.0%
<b>GNSO Council</b>	<b>30</b>	<b>23</b>	<b>76.7%</b>
Brian Beckham	8	8	100.0%
Keith Drazek	11	10	90.9%
Philippe Fouquart	11	5	45.5%
<b>Governmental Advisory Committee (GAC)</b>	<b>14</b>	<b>13</b>	<b>92.9%</b>
Laureen Kapin	11	10	90.9%
Melina Asimina Stroungi	3	3	100.0%
<b>ICANN Board</b>	<b>11</b>	<b>11</b>	<b>100.0%</b>
Becky Burr	11	11	100.0%
<b>Intellectual Property Constituency (IPC)</b>	<b>12</b>	<b>10</b>	<b>83.3%</b>
Brian King	1	0	0.0%
Jan Janssen	11	10	90.9%
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>	<b>11</b>	<b>11</b>	<b>100.0%</b>
Amy Bivins	11	11	100.0%
<b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>	<b>11</b>	<b>11</b>	<b>100.0%</b>
Thomas Rickert	11	11	100.0%
<b>Non-Commercial Stakeholder Group (NCSG)</b>	<b>12</b>	<b>8</b>	<b>66.7%</b>
Stefan Filipovic	1	1	100.0%
Stephanie Perrin	11	7	63.6%
<b>Registrar Stakeholder Group (RrSG)</b>	<b>11</b>	<b>11</b>	<b>100.0%</b>
Volker Greimann	11	11	100.0%
<b>Registry Stakeholder Group (RySG)</b>	<b>12</b>	<b>11</b>	<b>91.7%</b>
Alan Woods	1	1	100.0%
Matthew Crossman	11	10	90.9%
<b>Security and Stability Advisory Committee (SSAC)</b>	<b>11</b>	<b>11</b>	<b>100.0%</b>
Tara Whalen	11	11	100.0%
<b>Grand Total</b>	<b>157</b>	<b>140</b>	<b>89.2%</b>

### Meeting Activities

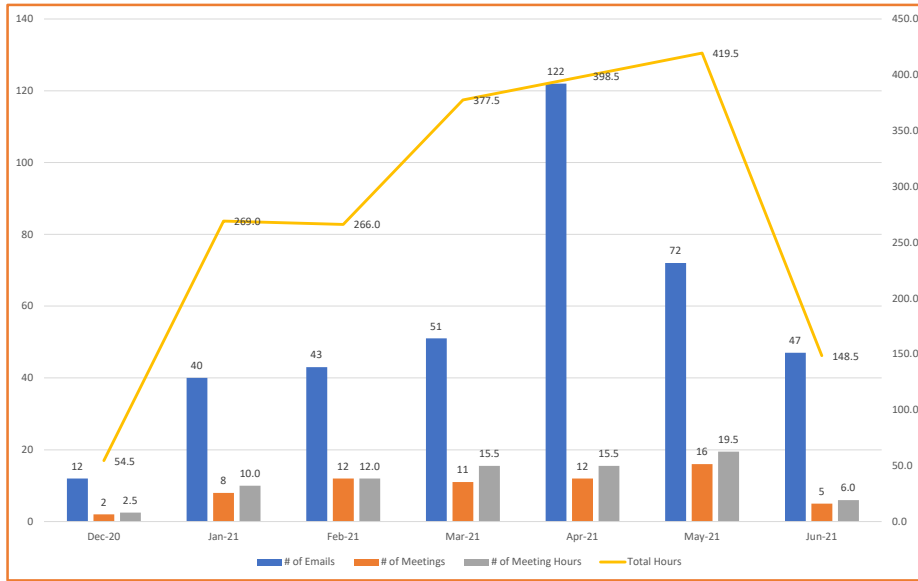

Date	# of Emails	# of Meetings	# of Meeting Hours	Total Hours
Dec-20	12	2	2.5	54.5
Jan-21	40	8	10.0	269.0
Feb-21	43	12	12.0	266.0
Mar-21	51	11	15.5	377.5
Apr-21	122	12	15.5	398.5
May-21	72	16	19.5	419.5
Jun-21	47	5	6.0	148.5
				1933.5


### Work Based Metrics

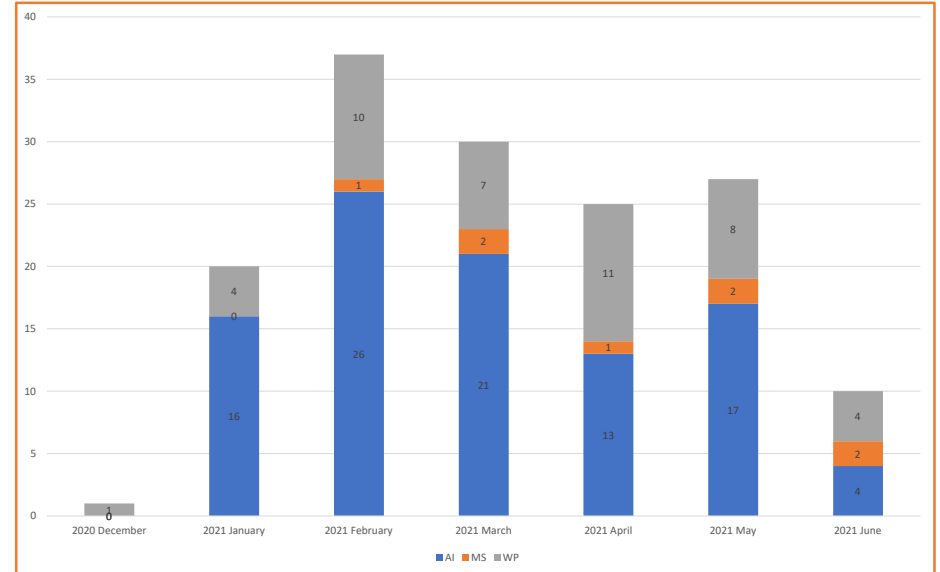

AI = Action Item  
 MS = Milestone  
 WP = Work Plan

WBS	Closed Qty
1.1.1.7	7
1.1.4	1
1.1.5	1
1.1.6	1
1.2.1	1
1.2.3	1
1.2.4	1
1.2.5.1	5
1.2.5.2	1
1.2.5.3	5
1.2.5.4	49
1.2.6	8
1.2.6.1	3
1.2.8.1	1
1.2.8.2	2
1.2.8.3	46
1.3.4	11
1.3.8	1
1.4.1	5

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	% Complete	Baseline1 Duration	Baseline1 Start	Baseline1 Finish	Qtr 4, 2020	Qtr 1, 2021	Qtr 2, 2021	Qtr 3, 2021	Qtr 4, 2021	Qtr 1, 2022
1	1	<b>EPDP-P2A Policy Development</b>	<b>372 days</b>	<b>Wed 10/21/20</b>	<b>Thu 3/24/22</b>		<b>78% 369 days</b>		<b>Wed 10/21/20</b>	<b>Mon 3/21/22</b>						
2	1.1	<b>PROJECT MANAGEMENT</b>	<b>372 days</b>	<b>Wed 10/21/20</b>	<b>Thu 3/24/22</b>		<b>73% 369 days</b>		<b>Wed 10/21/20</b>	<b>Mon 3/21/22</b>						
3	1.1.1	Project start confirmed	1 day	Wed 10/21/20	Wed 10/21/20		100% 1 day		Wed 10/21/20	Wed 10/21/20						
4	1.1.2	Adopt/Confirm charter	1 day	Thu 10/22/20	Thu 10/22/20	3	100% 1 day		Thu 10/22/20	Thu 10/22/20						
5	1.1.3	Confirmation of Team	35 days	Thu 10/22/20	Wed 12/9/20	3	100% 35 days		Thu 10/22/20	Wed 12/9/20						
6	1.1.4	Appointment of Team Chair	35 days	Thu 10/22/20	Wed 12/9/20	3	100% 35 days		Thu 10/22/20	Wed 12/9/20						
7	1.1.5	Appointment of Liaison to GNSO Council	70 days	Thu 10/22/20	Wed 1/27/21	3	100% 70 days		Thu 10/22/20	Wed 1/27/21						
8	1.1.6	Chair / Staff preparations	5 days	Thu 12/10/20	Wed 12/16/20	6	100% 5 days		Thu 12/10/20	Wed 12/16/20						
9	1.1.7	<b>Project Management</b>	<b>370 days</b>	<b>Thu 10/22/20</b>	<b>Thu 3/24/22</b>		<b>64% 367 days</b>		<b>Thu 10/22/20</b>	<b>Mon 3/21/22</b>						
10	1.1.7.1	Develop and confirm Project Plan	30 days	Thu 12/10/20	Wed 1/20/21	6	100% 30 days		Thu 12/10/20	Wed 1/20/21						
11	1.1.7.2	Obtain project plan approval from GNSO Council	25 days	Thu 1/21/21	Wed 2/24/21	10	100% 25 days		Thu 1/21/21	Wed 2/24/21						
12	1.1.7.3	Adopt iterative work plan(s)	1 day	Thu 2/25/21	Thu 2/25/21	11	100% 1 day		Thu 2/25/21	Thu 2/25/21						
13	1.1.7.4	Develop Project status work products and communications	140 days	Thu 2/4/21	Wed 9/1/21	11	43% 140 days		Thu 2/4/21	Wed 9/1/21						
14	1.1.7.5	<b>Leadership Sub team</b>	<b>190 days</b>	<b>Thu 12/10/20</b>	<b>Wed 9/1/21</b>		<b>75% 190 days</b>		<b>Thu 12/10/20</b>	<b>Wed 9/1/21</b>						
15	1.1.7.5.1	On-going preparation and planning of group activities	190 days	Thu 12/10/20	Wed 9/1/21	6	75% 190 days		Thu 12/10/20	Wed 9/1/21						
16	1.1.7.6	<b>Project Cost Support Team Sub team (Not applicable)</b>	<b>0 days</b>	<b>Thu 10/22/20</b>	<b>Thu 10/22/20</b>		<b>0% 0 days</b>		<b>Thu 10/22/20</b>	<b>Thu 10/22/20</b>						
20	1.1.7.7	Close project plan, Factsheet, and transition project to IPT	20 days	Fri 2/25/22	Thu 3/24/22	19,15,105	0% 20 days		Tue 2/22/22	Mon 3/21/22						
21	1.2	<b>EPDP-P2A DELIBERATIONS</b>	<b>116 days</b>	<b>Thu 12/17/20</b>	<b>Thu 5/27/21</b>		<b>100% 116 days</b>		<b>Thu 12/17/20</b>	<b>Thu 5/27/21</b>						
22	1.2.1	First meeting of EPDP Team	1 day	Thu 12/17/20	Thu 12/17/20	8	100% 1 day		Thu 12/17/20	Thu 12/17/20						
23	1.2.2	Understand Charter, organize materials and develop initial approach	21 days	Thu 12/17/20	Thu 1/14/21	8	100% 21 days		Thu 12/17/20	Thu 1/14/21						
24	1.2.3	Develop definitions and terminology	7 days	Fri 1/15/21	Mon 1/25/21	23	100% 7 days		Fri 1/15/21	Mon 1/25/21						
25	1.2.4	<b>Input from other SOIACs &amp; GNSO SG/Cs</b>	<b>26 days</b>	<b>Fri 1/15/21</b>	<b>Fri 2/19/21</b>		<b>100% 26 days</b>		<b>Fri 1/15/21</b>	<b>Fri 2/19/21</b>						
30	1.2.5	<b>Topic 1 Deliberations - Legal vs. Natural</b>	<b>85 days</b>	<b>Fri 1/15/21</b>	<b>Thu 5/13/21</b>		<b>100% 85 days</b>		<b>Fri 1/15/21</b>	<b>Thu 5/13/21</b>						
31	1.2.5.1	Understand topic and determine need to deliberate	5 days	Fri 1/15/21	Thu 1/21/21	23	100% 5 days		Fri 1/15/21	Thu 1/21/21						
32	1.2.5.2	Deliberate policy considerations and determine approach	5 days	Fri 1/15/21	Thu 1/21/21	23	100% 5 days		Fri 1/15/21	Thu 1/21/21						
33	1.2.5.3	Webinar on Legal vs. Natural Study	1 day	Fri 1/15/21	Fri 1/15/21	23	100% 1 day		Fri 1/15/21	Fri 1/15/21						
34	1.2.5.4	Develop Proposals and deliberate policy issues	60 days	Fri 1/22/21	Thu 4/15/21	32	100% 60 days		Fri 1/22/21	Thu 4/15/21						
35	1.2.5.5	Develop draft work product	60 days	Fri 1/22/21	Thu 4/15/21	32	100% 60 days		Fri 1/22/21	Thu 4/15/21						
36	1.2.5.6	Conduct First Reading + verbal and email response	10 days	Fri 4/16/21	Thu 4/29/21	35	100% 10 days		Fri 4/16/21	Thu 4/29/21						
37	1.2.5.7	Conduct Second Reading + verbal response + adoption or discard	10 days	Fri 4/30/21	Thu 5/13/21	35,36	100% 10 days		Fri 4/30/21	Thu 5/13/21						
38	1.2.5.8	Confirm draft as stable	0 days	Thu 5/13/21	Thu 5/13/21	37	100% 0 days		Thu 5/13/21	Thu 5/13/21						
39	1.2.6	<b>Topic 2 Deliberations - Feasibility of unique contacts to have a uniform anonymized email address</b>	<b>85 days</b>	<b>Fri 1/15/21</b>	<b>Thu 5/13/21</b>		<b>100% 85 days</b>		<b>Fri 1/15/21</b>	<b>Thu 5/13/21</b>						
40	1.2.6.1	Understand topic and determine need to deliberate	5 days	Fri 1/15/21	Thu 1/21/21	23	100% 5 days		Fri 1/15/21	Thu 1/21/21						
41	1.2.6.2	Deliberate policy considerations and determine approach	5 days	Fri 1/15/21	Thu 1/21/21	23	100% 5 days		Fri 1/15/21	Thu 1/21/21						
42	1.2.6.3	Deliberate policy issues	60 days	Fri 1/22/21	Thu 4/15/21	41	100% 60 days		Fri 1/22/21	Thu 4/15/21						
43	1.2.6.4	Develop draft work product	60 days	Fri 1/22/21	Thu 4/15/21	41	100% 60 days		Fri 1/22/21	Thu 4/15/21						
44	1.2.6.5	Conduct First Reading + verbal and email response	10 days	Fri 4/16/21	Thu 4/29/21	43	100% 10 days		Fri 4/16/21	Thu 4/29/21						
45	1.2.6.6	Conduct Second Reading + verbal response + adoption or discard	10 days	Fri 4/30/21	Thu 5/13/21	43,44	100% 10 days		Fri 4/30/21	Thu 5/13/21						
46	1.2.6.7	Confirm draft as stable	0 days	Thu 5/13/21	Thu 5/13/21	45	100% 0 days		Thu 5/13/21	Thu 5/13/21						
47	1.2.7	<b>Unplanned Issues &amp; Tasks (Not applicable)</b>	<b>0 days</b>	<b>Thu 1/14/21</b>	<b>Thu 1/14/21</b>		<b>100% 0 days</b>		<b>Thu 1/14/21</b>	<b>Thu 1/14/21</b>						
64	1.2.8	<b>Legal Sub team</b>	<b>95 days</b>	<b>Fri 1/15/21</b>	<b>Thu 5/27/21</b>		<b>100% 95 days</b>		<b>Fri 1/15/21</b>	<b>Thu 5/27/21</b>						
68	1.2.9	<b>Key Events (Not applicable)</b>	<b>0 days</b>	<b>Thu 1/14/21</b>	<b>Thu 1/14/21</b>		<b>100% 0 days</b>		<b>Thu 1/14/21</b>	<b>Thu 1/14/21</b>						
84	1.3	<b>INITIAL REPORT</b>	<b>128 days</b>	<b>Tue 1/26/21</b>	<b>Thu 7/22/21</b>		<b>95% 125 days</b>		<b>Tue 1/26/21</b>	<b>Mon 7/19/21</b>						
85	1.3.1	Assemble initial conclusions	60 days	Tue 1/26/21	Mon 4/19/21	24	100% 60 days		Tue 1/26/21	Mon 4/19/21						
86	1.3.2	Populate discussion papers with findings and potential recommendations	60 days	Tue 1/26/21	Mon 4/19/21	24	100% 60 days		Tue 1/26/21	Mon 4/19/21						
87	1.3.3	Consolidate interim recommendations and findings	85 days	Tue 1/26/21	Mon 5/24/21	24	100% 85 days		Tue 1/26/21	Mon 5/24/21						
88	1.3.4	Build Draft Report for public comment	89 days	Tue 1/26/21	Fri 5/28/21	24	100% 85 days		Tue 1/26/21	Mon 5/24/21						
89	1.3.5	Approve Draft Report for public comment	4 days	Mon 5/31/21	Thu 6/3/21	88	100% 5 days		Tue 5/25/21	Mon 5/31/21						
90	1.3.6	Publish Initial Report	0 days	Fri 6/4/21	Fri 6/4/21	89	100% 0 days		Mon 5/31/21	Mon 5/31/21						
91	1.3.7	Communicate Initial Report	5 days	Fri 6/4/21	Thu 6/10/21	89	100% 5 days		Tue 6/1/21	Mon 6/7/21						
92	1.3.8	Public comment forum on the Initial Report (45 days)	35 days	Fri 6/4/21	Thu 7/22/21	89	55% 35 days		Tue 6/1/21	Mon 7/19/21						
93	1.4	<b>FINAL REPORT</b>	<b>30 days</b>	<b>Fri 7/23/21</b>	<b>Thu 9/2/21</b>		<b>0% 30 days</b>		<b>Tue 7/20/21</b>	<b>Mon 8/30/21</b>						
94	1.4.1	Review of public comments	20 days	Fri 7/23/21	Thu 8/19/21	84	0% 20 days		Tue 7/20/21	Mon 8/16/21						
95	1.4.2	Continue deliberations of policy topics towards a Final Report	20 days	Fri 7/23/21	Thu 8/19/21	84	0% 20 days		Tue 7/20/21	Mon 8/16/21						
96	1.4.3	Build Final Report & Final Deliberations	5 days	Fri 8/20/21	Thu 8/26/21	95	0% 5 days		Tue 8/17/21	Mon 8/23/21						
97	1.4.4	Determine consensus levels on interim recommendations	5 days	Fri 8/27/21	Thu 9/2/21	96	0% 5 days		Tue 8/24/21	Mon 8/30/21						
98	1.4.5	Adopt final recommendations and report	5 days	Fri 8/27/21	Thu 9/2/21	96	0% 5 days		Tue 8/24/21	Mon 8/30/21						
99	1.4.6	Submission of Final Report to the GNSO Council	0 days	Thu 9/2/21	Thu 9/2/21	98	0% 0 days		Mon 8/30/21	Mon 8/30/21						
100	1.5	<b>POST EPDP ACTIVITIES</b>	<b>125 days</b>	<b>Fri 9/3/21</b>	<b>Thu 2/24/22</b>		<b>0% 125 days</b>		<b>Tue 8/31/21</b>	<b>Mon 2/21/22</b>						

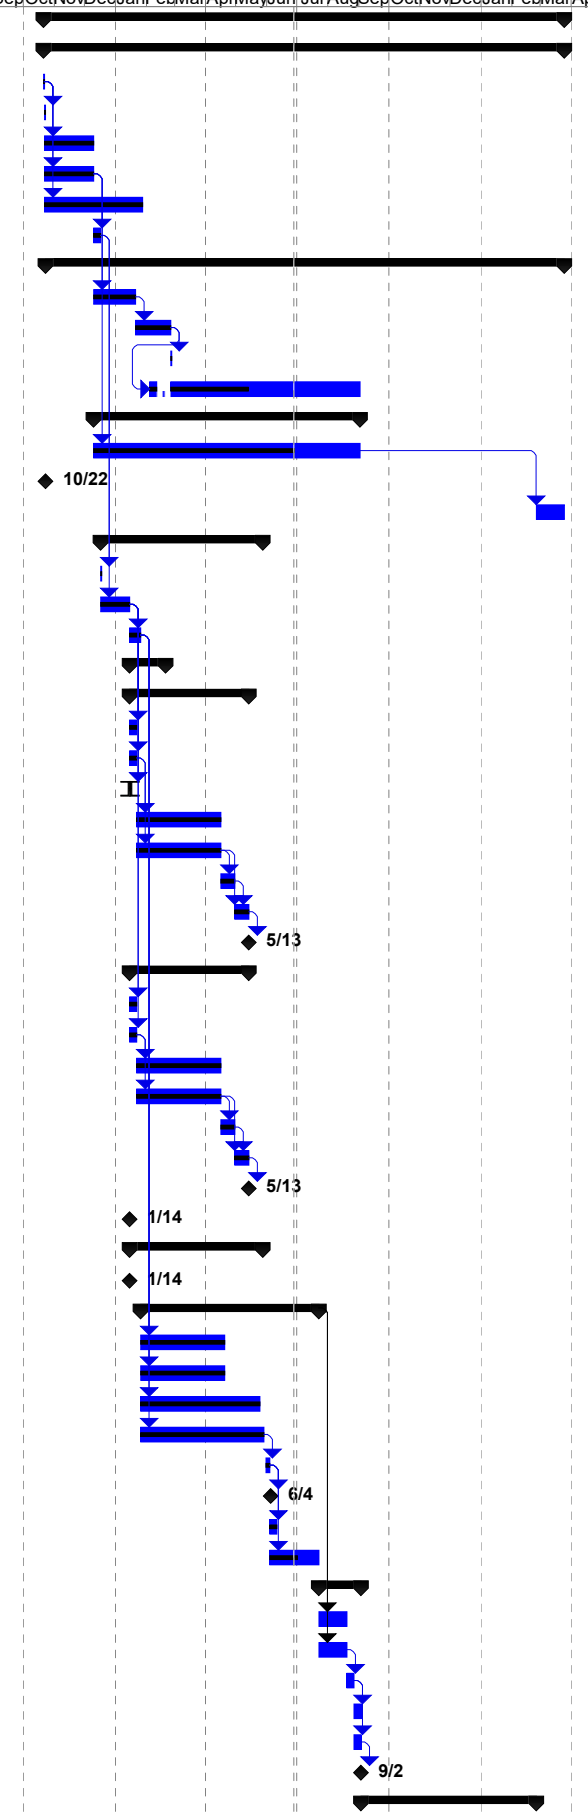

Project: EPDP-P2A\_Project\_Plan\_202  
Date: Mon 6/28/21

Task		Summary		External Milestone		Manual Task		Duration-only		Manual Summary		Start-only		External Milestone		Deadline	
Split		Project Summary		Inactive Milestone		Manual Summary Rollup		Finish-only		Progress							
Milestone		External Tasks		Inactive Summary													

Program	Project Code	Type	Action Item	WBS	Status	Date Assigned	Due Date	Responsible Member	Responsible Staff	Additional Notes - Action Taken
RDDS	EPDP_P2A	WP	Meeting #28 (03-Jun-2021) - Cancelled	1.4.1	Closed	18-May-2021	3-Jun-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Submit Initial Report for Public Comment - Changed from 40 to 45 days	1.3.8	Closed	29-Jan-2021	3-Jun-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Submit Monthly Project Package - May	1.1.1.7	Closed	14-Jan-2021	4-Jun-2021	EPDP-P2A Team	Berry C.	
RDDS	EPDP_P2A	WP	Meeting #29 (10-Jun-2021) - Prepare for ICANN71 & discuss possible actions during public comment	1.4.1	Closed	1-Jun-2021	10-Jun-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Session at ICANN71 (17-Jun-2021) - Community Outreach on Initial Report	1.4.1	Closed	1-Jun-2021	17-Jun-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Submit Monthly Project Package - June	1.1.1.7	Open	18-May-2021	6-Jul-2021	EPDP-P2A Team	Berry C.	
RDDS	EPDP_P2A	WP	Meeting #30 (15-Jul-2021) - Tentative - Review of Public Comment submissions	1.4.1	Open	1-Jun-2021	15-Jul-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Public Comment Closes	1.3.8	Open	18-May-2021	19-Jul-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #31 (27-Jul-2021) - Review of Public Comment submissions	1.4.1	Open	1-Jun-2021	27-Jul-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #32 (29-Jul-2021) - Review of Public Comment submissions	1.4.1	Open	1-Jun-2021	29-Jul-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #33 (03-Aug-2021) - Review of Public Comment submissions	1.4.1	Open	1-Jun-2021	3-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #34 (05-Aug-2021) - Review of Public Comment submissions	1.4.1	Open	1-Jun-2021	5-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Submit Monthly Project Package - July	1.1.1.7	Open	18-May-2021	6-Aug-2021	EPDP-P2A Team	Berry C.	
RDDS	EPDP_P2A	WP	Meeting #35 (10-Aug-2021) - TBD		Open	1-Jun-2021	10-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #36 (12-Aug-2021) - TBD		Open	1-Jun-2021	12-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #37 (17-Aug-2021) - TBD		Open	1-Jun-2021	17-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #38 (19-Aug-2021) - TBD		Open	1-Jun-2021	19-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #39 (24-Aug-2021) - TBD		Open	1-Jun-2021	24-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #40 (26-Aug-2021) - TBD		Open	1-Jun-2021	26-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	WP	Meeting #41 (31-Aug-2021) - TBD		Open	1-Jun-2021	31-Aug-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Submit Final Report to GNSO Council	1.4.6	Open	18-May-2021	2-Sep-2021	EPDP-P2A Team	Staff	
RDDS	EPDP_P2A	MS	Submit Monthly Project Package - August	1.1.1.7	Open	18-May-2021	3-Sep-2021	EPDP-P2A Team	Berry C.	
