

Project Tracking & Rollup DASHBOARD


Project Name PDP: Transfer Policy Review - Phase 1 **Program** Transfers **Project Sponsor** GNSO Council

Project Information **Tasks by Status** **Project Contacts** **Participant Summary**

42%
% Complete

02/18/21
Actual Start

12/28/23
Planned Finish




Roger Carney
Chair

n/a
Vice_Chair

Greg DiBiase
Liaison

Emily Barabas
Staff_Lead

Berry Cobb
Project_Manager

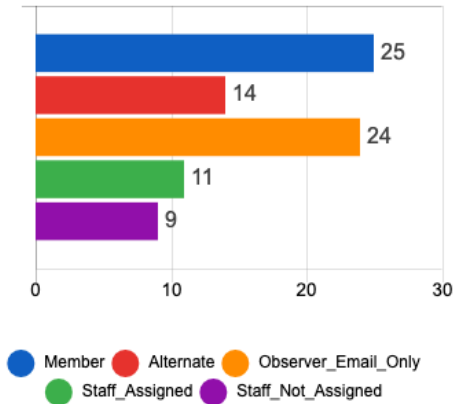

Project Status & Health

Project_Status	Project_Health
On-Schedule	On-Target

● Not_Started ● Complete ● In_Progress

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Timeline (2021-2023)											
						2021 Q1	2021 Q2	2021 Q3	2021 Q4	2022 Q1	2022 Q2	2022 Q3	2022 Q4	2023 Q1	2023 Q2	2023 Q3	2023 Q4
	PDP: Transfer Policy Review - Phase 1	02/18/21	12/28/23	42%	In Progress	PDP: Transfer Policy Review - Phase 1											
	PROJECT CONTROL	02/18/21	12/28/23	53%	In Progress	PROJECT CONTROL											
	GROUP DELIBERATIONS	05/13/21	02/22/23	64%	In Progress	GROUP DELIBERATIONS											
	Phase 1A Policy Topics	06/03/21	05/11/22	89%	In Progress	Phase 1A Policy Topics											
	Phase 1B Policy Topics	06/15/22	02/22/23			Phase 1B Policy Topics											
	INITIAL REPORT	06/24/21	05/17/23	36%	In Progress	INITIAL REPORT											
	Publish Initial Report	06/15/22	06/15/22			Publish Initial Report											
	Publish Initial Report	03/29/23	03/29/23			Publish Initial Report											
	FINAL REPORT	08/04/22	08/16/23		Not Started	FINAL REPORT											
	Review of public comments - Phase 1A	08/04/22	09/14/22			Review of public comments - Phase 1A											
	Review of public comments - Phase 1B	05/18/23	06/28/23			Review of public comments - Phase 1B											
	Submission of Final Report to the GNSO Council	08/16/23	08/16/23			Submission of Final Report to the GNSO Council											

4 - Working Group

Title: PDP: Transfer Policy Review - Phase 1 (TPR_P1)

Description & Scope: On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

Composition:

Chair(s):	Roger Carney
Council Liaison:	Greg Dibiase
Policy Staff:	E. Barabas, J. Hedlund, C. Tubergen, B. Cobb
GDS Staff:	I. Colas-Adeshina
# Participants:	39 Participants (link)
# Observers:	33
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	18 Feb 2021	18 Feb 2021	420	28 Dec 2023	TBD

Program	Progress	Status	Health
Transfers	42%	●	■

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan ([link](#)):

Milestone/Task	Date	
Final Issue Report to Council	Jan-21	✓
Project Start	Feb-21	✓
Charter Approved	Mar-21	✓
Chair appointment	Apr-21	✓
1st Plenary meeting	May-21	✓
Project Plan and Work plan Adoption	Jul-21	✓
SO/AC & SG/C Input to PDP	Aug-21	✓
Phase 1A Issue Deliberations	Aug-22	■
Populate stable draft papers w/ potential recs.	May-22	■
Discuss/approve findings and interim recs.	May-22	■
Consolidate interim recommendations and findings	Jun-22	
Issue Phase 1A Initial Report for public comment	Jun-22	
Review public comment input	Sep-22	
Phase 1B Issue Deliberations	Mar-23	
Populate stable draft papers w/ potential recs.	Feb-23	
Discuss/approve findings and interim recs.	Mar-23	
Consolidate interim recommendations and findings	Mar-23	
Issue Phase 1B Initial Report for public comment	Mar-23	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Jul-23	
Determine consensus levels on recommendations	Jun-23	
Adopt final recommendations and report (Phase 1A+1B)	Jul-23	
Send final report to GNSO Council	Aug-23	
GNSO Council adoption of consensus recs.	Oct-23	
Issue public comment for Board consideration	Oct-23	
ICANN Board adoption of consensus recs.	Jan-24	
Prior period % Complete	39%	■

Status/Health Rationale:

- The project schedule is confirmed by the GNSO Council and Status is “On-Schedule” and the Health is “On-Target”.

Current Activities:

- Complete deliberations on Additional Security Measures (post create locks and post transfer locks).
- Complete deliberations on Denial (NACK) of Transfers.
- Continue deliberations on Bulk Transfers of Domains.

Planned Activities:

- Transfer policy package: review of preliminary recommendations for Transfer Authorization Codes (formerly AuthInfo codes), Losing Form of Authorization, Gaining Form of Authorization, Denial (NACK) of Transfers, and Additional Security Measures.
- Prepare Initial Report for public comment.

Open Issues, Risks & Mitigation Plan:

- None at this time.

Completed in prior period(s):

- Completed and distributed [Project Package](#) for March.

Project Tracking & Rollup DASHBOARD



Project Roster

Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Nanghaka Daniel Khauka	Member		05/04/21		https://community.icann.org
Steinar Grøtterød	Member		05/05/21		https://community.icann.org
Raymond Mamattah	Alternate		05/04/21		https://community.icann.org
Lutz Donnerhacke	Alternate		05/08/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Zak Muscovitch	Member		04/23/21		https://community.icann.org
Arinola Akinyemi	Alternate		08/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Gregory DiBiase	Member	Liaison	06/04/21		https://community.icann.org
Roger Carney	Member	Chair	04/23/21		https://community.icann.org
Group Selected / Nominated By: Group Name Independent					
Steve Crocker	Member	Subject Matter Expert	04/26/21		https://community.icann.org
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Mike Rodenbaugh	Member		04/21/21		https://community.icann.org
Salvador Camacho Hernandez	Member		04/26/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Isabelle Colas	Staff - Assigned	Liaison	06/10/21		
Devan Reed	Staff - Assigned		11/16/21		
Berry Cobb	Staff - Assigned		02/18/21		
Emily Barabas	Staff - Assigned		02/18/21		
Michelle DeSmyter	Staff - Assigned		02/18/21		
Terri Agnew	Staff - Assigned		02/18/21		
Caitlin Tubergen	Staff - Assigned		02/18/21		
Julie Bisland	Staff - Assigned		02/18/21		
Julie Hedlund	Staff - Assigned		02/18/21		
Nathalie Peregrine	Staff - Assigned		02/18/21		
Holida Yanik	Staff - Assigned		04/30/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
John Woodworth	Member		04/14/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Wisdom Donkor	Member		06/01/21		https://community.icann.org
Farzaneh Badiei	Member		06/01/21		https://community.icann.org
Akinremi Peter Taiwo	Alternate		06/02/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Keiron Tobin	Member		06/07/21		https://community.icann.org
Thomas Keller	Member		04/26/21	09/27/21	https://community.icann.org
Eric Rokobauer	Member		04/26/21		https://community.icann.org
Theo Geurts	Member		04/23/21		https://community.icann.org
Kristian Ørmen	Member		04/23/21		https://community.icann.org
Crystal Ondo	Member		04/23/21		https://community.icann.org
Sarah Wyld	Member		04/23/21		https://community.icann.org
Prudence Malinki	Member		04/27/21		https://community.icann.org
Catherine Merdinger	Member		04/27/21		https://community.icann.org
Owen Smigelski	Member		04/27/21		https://community.icann.org
Richard Merdinger	Member		05/05/21	06/07/21	https://community.icann.org
Antonia Nan Chu	Member		05/06/21		https://community.icann.org
Volker Greimann	Alternate		04/24/21		https://community.icann.org
Jothan Frakes	Alternate		04/23/21		https://community.icann.org
Essie Musailov	Alternate		04/23/21		https://community.icann.org
Pam Little	Alternate		04/26/21		https://community.icann.org
Richard Brown	Alternate		04/26/21		https://community.icann.org
Min Feng	Alternate		04/26/21		https://community.icann.org
Jacques Blanc	Alternate		04/29/21		https://community.icann.org
Arnaud Wittersheim	Alternate		05/05/21		https://community.icann.org
Jody Kolker	Alternate		05/07/21		https://community.icann.org
Group Selected / Nominated By: Group Name					


Registry Stakeholder Group (RySG)

Richard Wilhelm	Member		03/04/22		https://community.icann.org
James Galvin	Member		04/27/21		https://community.icann.org
Beth Bacon	Alternate		05/04/21		https://community.icann.org


Project Tracking & Rollup

DASHBOARD


Work-Plan Activity Metrics

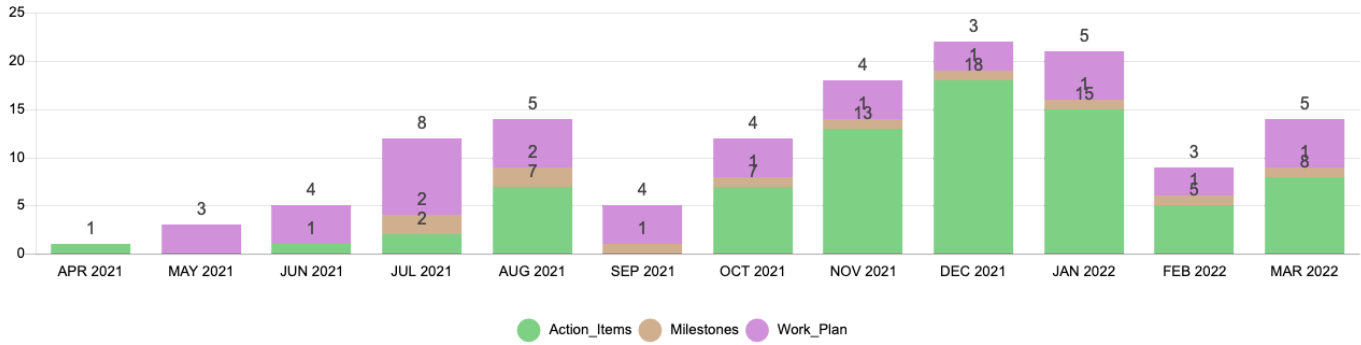

Mailman Activity

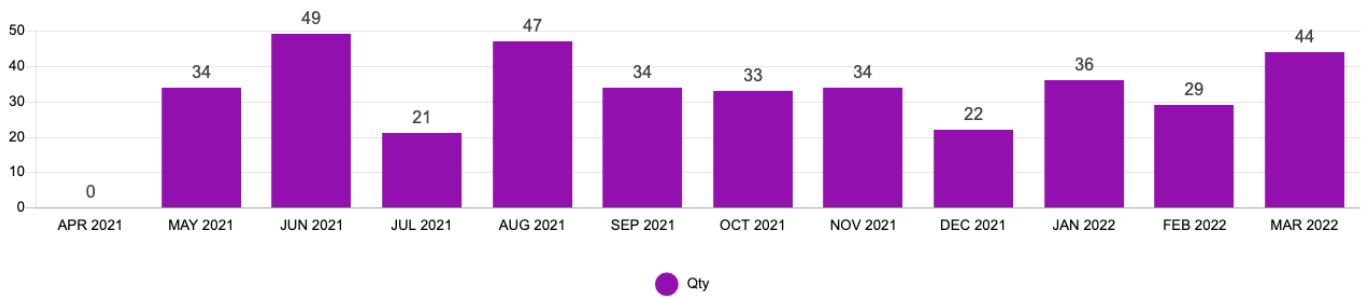

Meeting Activity

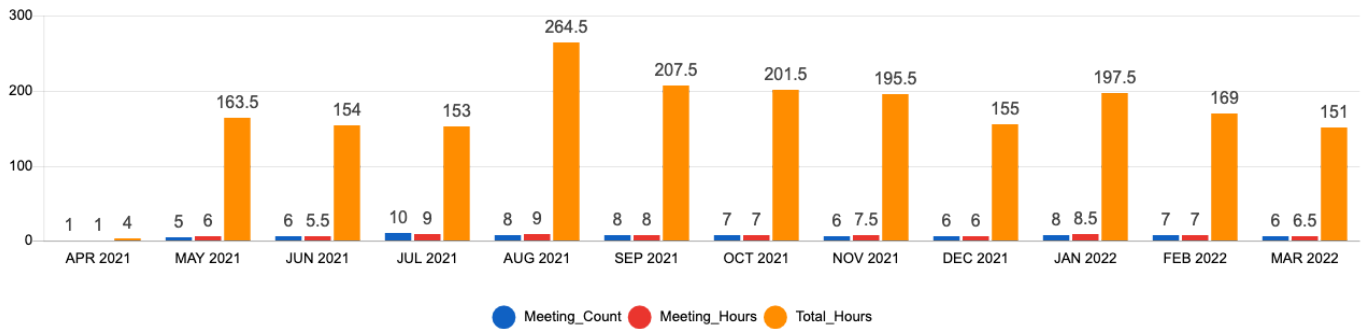

Project Tracking & Rollup DASHBOARD



Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 1185	Sum 980	Avg 82.7%
Primary At-Large Advisory Committee (ALAC)	Sum 122	Sum 103	Avg 84.4%
Attendee Name Lutz Donnerhacke	Sum 24	Sum 22	Avg 91.7%
Attendee Name Nanghaka Daniel Khauka	Sum 38	Sum 30	Avg 78.9%
Attendee Name Raymond Mamattah	Sum 22	Sum 20	Avg 90.9%
Attendee Name Steinar Grøtterød	Sum 38	Sum 31	Avg 81.6%
Primary Commercial Business Users Constituency (BC)	Sum 63	Sum 60	Avg 95.2%
Attendee Name Arinola Akinyemi	Sum 25	Sum 25	Avg 100.0%
Attendee Name Zak Muscovitch	Sum 38	Sum 35	Avg 92.1%
Primary GNSO Council	Sum 72	Sum 62	Avg 86.1%
Attendee Name Gregory DiBiase	Sum 34	Sum 24	Avg 70.6%
Attendee Name Roger Carney	Sum 38	Sum 38	Avg 100.0%
Primary Independent	Sum 38	Sum 11	Avg 28.9%
Attendee Name Steve Crocker	Sum 38	Sum 11	Avg 28.9%
Primary Intellectual Property Constituency (IPC)	Sum 76	Sum 25	Avg 32.9%
Attendee Name Mike Rodenbaugh	Sum 38	Sum 17	Avg 44.7%
Attendee Name Salvador Camacho Hernandez	Sum 38	Sum 8	Avg 21.1%
Primary Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Sum 38	Sum 33	Avg 86.8%
Attendee Name John Woodworth	Sum 38	Sum 33	Avg 86.8%
Primary Non-Commercial Stakeholder Group (NCSG)	Sum 76	Sum 43	Avg 56.6%
Attendee Name Akinremi Peter Taiwo	Sum 6	Sum 5	Avg 83.3%
Attendee Name Farzaneh Badiei	Sum 35	Sum 16	Avg 45.7%
Attendee Name Wisdom Donkor	Sum 35	Sum 22	Avg 62.9%
Primary Registrar Stakeholder Group (RrSG)	Sum 596	Sum 549	Avg 92.1%
Attendee Name Antonia Nan Chu	Sum 38	Sum 37	Avg 97.4%
Attendee Name Arnaud Wittersheim	Sum 23	Sum 23	Avg 100.0%
Attendee Name Catherine Merdinger	Sum 38	Sum 30	Avg 78.9%
Attendee Name Crystal Ondo	Sum 38	Sum 29	Avg 76.3%
Attendee Name Eric Rokobauer	Sum 37	Sum 36	Avg 97.3%
Attendee Name Essie Musailov	Sum 35	Sum 35	Avg 100.0%
Attendee Name Jacques Blanc	Sum 5	Sum 4	Avg 80.0%
Attendee Name Jody Kolker	Sum 36	Sum 36	Avg 100.0%
Attendee Name Jothan Frakes	Sum 36	Sum 36	Avg 100.0%

Attendee Name Keiron Tobin	Sum 34	Sum 30	Avg 88.2%
Attendee Name Kristian Ørmen	Sum 38	Sum 36	Avg 94.7%
Attendee Name Min Feng	Sum 3	Sum 2	Avg 66.7%
Attendee Name Owen Smigelski	Sum 38	Sum 33	Avg 86.8%
Attendee Name Pam Little	Sum 1	Sum 1	Avg 100.0%
Attendee Name Prudence Malinki	Sum 38	Sum 38	Avg 100.0%
Attendee Name Richard Brown	Sum 31	Sum 31	Avg 100.0%
Attendee Name Richard Merdinger	Sum 4	Sum 4	Avg 100.0%
Attendee Name Sarah Wyld	Sum 38	Sum 33	Avg 86.8%
Attendee Name Theo Geurts	Sum 38	Sum 35	Avg 92.1%
Attendee Name Thomas Keller	Sum 16	Sum 9	Avg 56.3%
Attendee Name Volker Greimann	Sum 31	Sum 31	Avg 100.0%
Primary Registry Stakeholder Group (RySG)	Sum 104	Sum 94	Avg 90.4%
Attendee Name Barbara Knight	Sum 36	Sum 33	Avg 91.7%
Attendee Name Beth Bacon	Sum 28	Sum 28	Avg 100.0%
Attendee Name James Galvin	Sum 38	Sum 31	Avg 81.6%
Attendee Name Richard Wilhelm	Sum 2	Sum 2	Avg 100.0%

Plenary - Alternates Replacing Members Log



<https://community.icann.org/x/V4aUCQ>

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	Q1		Q2		Q3		Q4		Q1		Q2		Q3		Q4		Q1		Q2		Q3							
											Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
		PDP: Transfer Policy Review - Phase 1	746d	02/18/21	12/28/23		42%	In Progress	02/18/21	12/28/23																												
		PROJECT CONTROL	746d	02/18/21	12/28/23		53%	In Progress	02/18/21	12/28/23																												
	1.1	Project start confirmed	0	02/18/21	02/18/21		100%	Complete	02/18/21	02/18/21																												
	1.2	Adopt/Confirm charter	25d	02/18/21	03/24/21	3	100%	Complete	02/18/21	03/24/21																												
	1.3	Confirmation of Team	50d	02/18/21	04/28/21	3	100%	Complete	02/18/21	04/28/21																												
	1.4	Appointment of Team Chair	50d	02/18/21	04/28/21	3	100%	Complete	02/18/21	04/28/21																												
	1.5	Appointment of Liaison to GNSO Council	50d	02/18/21	04/28/21	3	100%	Complete	02/18/21	04/28/21																												
	1.6	Chair / Staff preparations	10d	04/29/21	05/12/21	6	100%	Complete	04/29/21	05/12/21																												
	1.7	Project Management	696d	04/29/21	12/28/23		41%	In Progress	04/29/21	12/28/23																												
	1.7.1	Develop and confirm Project Plan	30d	04/29/21	06/09/21	6	100%	Complete	04/29/21	06/09/21																												
	1.7.2	Obtain project plan approval from GNSO Council	30d	06/10/21	07/21/21	10	100%	Complete	06/10/21	07/21/21																												
	1.7.3	Develop monthly Project Packages and deliver to Group & Council	540d	07/22/21	08/16/23	11	34%	In Progress	07/22/21	08/16/23																												
	1.7.4	Leadership Sub team	600d	04/29/21	08/16/23		41%	In Progress	04/29/21	08/16/23																												
	1.7.4.1	On-going preparation and planning of group activities	600d	04/29/21	08/16/23	6	41%	In Progress	04/29/21	08/16/23																												
	1.7.5	Close project and transition project to implementation	1d	12/28/23	12/28/23	14, 215																																
		GROUP DELIBERATIONS	465d	05/13/21	02/22/23		64%	In Progress	05/13/21	02/22/23																												
	2.1	First meeting of Team	1d	05/13/21	05/13/21	8	100%	Complete	05/13/21	05/13/21																												
	2.2	Understand Charter, organize materials and develop initial approach	10d	05/13/21	05/26/21	8	100%	Complete	05/13/21	05/26/21																												
	2.3	Overview & initial discussion of all Policy Topics	15d	05/13/21	06/02/21	8	100%	Complete	05/13/21	06/02/21																												
	2.4	Develop definitions and terminology	30d	05/13/21	06/23/21	8	100%	Complete	05/13/21	06/23/21																												
	2.5	Input from other SO/ACs & GNSO SG/Cs	91d	05/27/21	09/30/21		100%	Complete	05/27/21	09/30/21																												
	2.6	Phase 1A Policy Topics	245d	06/03/21	05/11/22		89%	In Progress	06/03/21	05/11/22																												
	2.6.1	Topic 1 Deliberations - Gaining FOA	40d	12/02/21	01/26/22		100%	Complete	12/02/21	01/26/22																												
	2.6.2	Topic 2 Deliberations - Losing FOA	40d	10/07/21	12/01/21		100%	Complete	10/07/21	12/01/21																												
	2.6.3	Topic 3 Deliberations - Additional Security Measures	40d	08/12/21	10/06/21		100%	Complete	08/12/21	10/06/21																												
	2.6.4	Topic 4 Deliberations - Auth-Info Code Management	180d	06/03/21	02/09/22		100%	Complete	06/03/21	02/09/22																												
	2.6.5	Topic 5 Deliberations - Bulk Use of Auth-Info Codes	40d	02/10/22	04/06/22		50%	In Progress	02/10/22	04/06/22																												
	2.6.6	Topic 6 Deliberations - Wave 1, Recommendation 27	25d	04/07/22	05/11/22		13%	In Progress	04/07/22	05/11/22																												
	2.6.7	Topic 7 Deliberations - Denying Transfers	35d	02/10/22	03/30/22		92%	In Progress	02/10/22	03/30/22																												
	2.7	Phase 1B Policy Topics	180d	06/15/22	02/22/23				06/15/22	02/22/23																												
		INITIAL REPORT	495d	06/24/21	05/17/23		36%	In Progress	06/24/21	05/17/23																												
	3.1	Phase 1A Initial Report	290d	06/24/21	08/03/22		66%	In Progress	06/24/21	08/03/22																												
	3.1.1	Populate stable drafts as required	230d	06/24/21	05/11/22	20	87%	In Progress	06/24/21	05/11/22																												
	3.1.2	Discuss/approve findings and interim recommendations	10d	05/12/22	05/25/22	27, 40, 51, 60, 72, 83			05/12/22	05/25/22																												
	3.1.3	Consolidate interim recommendations and findings	10d	05/26/22	06/08/22	191			05/26/22	06/08/22																												
	3.1.4	Build Draft Report for public comment	10d	05/26/22	06/08/22	191			05/26/22	06/08/22																												
	3.1.5	Approve Draft Report for public comment	5d	06/09/22	06/15/22	193			06/09/22	06/15/22																												
	3.1.6	Publish Initial Report	0	06/15/22	06/15/22	194			06/15/22	06/15/22																												
	3.1.7	Communicate Initial Report	5d	06/16/22	06/22/22	194			06/16/22	06/22/22																												
	3.1.8	Public comment forum on the Initial Report (45 days)	35d	06/16/22	08/03/22	194			06/16/22	08/03/22																												
	3.2	Phase 1B Initial Report	240d	06/16/22	05/17/23				06/16/22	05/17/23																												
		FINAL REPORT	270d	08/04/22	08/16/23			Not Started	08/04/22	08/16/23																												
	4.1	Review of public comments - Phase 1A	30d	08/04/22	09/14/22	197			08/04/22	09/14/22																												
	4.2	Review of public comments - Phase 1B	30d	05/18/23	06/28/23	206			05/18/23	06/28/23																												
	4.3	Continue deliberations of policy topics towards a Final Report	50d	05/18/23	07/26/23	197, 206			05/18/23	07/26/23																												
	4.4	Build Final Report & Final Deliberations	5d	07/27/23	08/02/23	210			07/27/23	08/02/23																												
	4.5	Determine consensus levels on interim recommendations	10d	08/03/23	08/16/23	211			08/03/23	08/16/23																												
	4.6	Adopt final recommendations and report	10d	08/03/23	08/16/23	211			08/03/23	08/16/23																												
	4.7	Submission of Final Report to the GNSO Council	0	08/16/23	08/16/23	213			08/16/23	08/16/23																												
		POST GROUP TASKS	95d	08/17/23	12/27/23			Not Started	08/17/23	12/27/23																												
		PDP CHECKLIST	824d	06/20/20	08/16/23		0%																															

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #38 Continue NACK	↓	TPR WG	03/01/22	03/01/22	Complete	
	AI	3.7.3: ACTION ITEM: Staff to research to see if there is background as to why this sentence is included: "In all such cases, however, the domain name must be put into "Registrar Hold" status by the Registrar of Record prior to the denial of transfer."	—	TPR WG	03/04/22	03/04/22	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	03/04/22	03/03/22	Complete	
	WP	Meeting - ICANN73 Continue deliberations on NACK of transfers	↓	TPR WG	03/08/22	03/08/22	Complete	
	AI	3.7.1: If we want to expand beyond "fraud" or clarify. WG members should suggest new language.	—	TPR WG	03/18/22	03/17/22	Complete	
	AI	3.7.2: WG members to review and suggest language relating to clarify the dispute and requested by issue.	—	TPR WG	03/18/22	03/17/22	Complete	
	AI	3.8.1: Staff to add the suggestion to remove "pending" and to change "informed of" to "notify".	—	Policy Support Staff	03/14/22	03/17/22	Complete	
	AI	WG members to review the charter questions and consider whether they need to be modified or added to, particularly, b5 which is about bulk use of Auth Info Codes, and whether the other two charter questions that relate to ICANN approved transfers need to be addressed in Phase 1A.	—	TPR WG	03/18/22	03/18/22	Complete	Changed from 7 March to 18 March in prep for Meeting #39
	AI	3.9.3: Add language to be more explicit on the order of applicability and reorder the list as MUST, MAY, MAY NOT. WG members are requested to suggest edits to make it more clear.	—	TPR WG	03/18/22	03/18/22	Complete	
	AI	3.9.3: Staff to research where the language of 3.9.5 was developed and the context/rationale. In general staff to review the entire list (MAY, MUST, MAY/MUST NOT) as a package and see which might be combined/eliminated/changed.	—	Policy Support Staff	03/14/22	03/17/22	Complete	
	WP	Meeting #39 Cancelled	↓	TPR WG	03/15/22	03/15/22	Complete	
	WP	Meeting #40 Start discussion on bulk use cases	↓	TPR WG	03/22/22	03/22/22	Complete	
	WP	Meeting #41 Continue discussion on bulk use cases	↓	TPR WG	03/29/22	03/29/22	Complete	
	AI	WG members to reply to the WG email distribution list if they are interested in joining a small team to review the NACKing/reasons for denial working document to finalize draft language for review by the full WG. https://docs.google.com/document/d/1L2bZnhJUY3VxyAjVCrkyVqdtOPn2EaqBARRRnEPd0Q/edit?usp=sharing_!!PtGJab4!r-dC9uVH1x8XlQfHwRmMmCvWstlPG8FPgvF8i5PWxpVDVnCWJjz52Psaon37IjsznQk3ws	—	TPR WG	03/31/22	03/31/22	Complete	
	WP	Meeting #42 Bulk use of TAC; Fast Undo	↓	TPR WG	04/05/22		In Progress	
	WP	Small Team Meeting #06 Review NACK options	↓	TPR WG	04/06/22		In Progress	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	04/08/22		In Progress	
	WP	Meeting #43 Post-creation and post-transfer locks	↓	TPR WG	04/12/22		Not Started	
	WP	Meeting #44 NACK; TAC	↓	TPR WG	04/19/22		Not Started	
	MS	Assemble Updated Swimlane and Single Document with All Draft Recommendations for WG Review	—	Policy Support Staff	04/25/22		In Progress	
	WP	Meeting #45 TAC	↓	TPR WG	04/26/22		Not Started	
	MS	Assemble Full Draft of Initial Report	—	Policy Support Staff	05/01/22		In Progress	
	WP	Meeting #46 Losing and Gaining FOA	↓	TPR WG	05/03/22		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	05/06/22		Not Started	
	WP	Meeting #47 Losing and Gaining FOA	↓	TPR WG	05/10/22		Not Started	
	WP	Meeting #48 Additional Security Measures	↓	TPR WG	05/17/22		Not Started	
	WP	Meeting #49 Review of Outstanding Items	↓	TPR WG	05/24/22		Not Started	
	WP	Meeting #50 Review of Outstanding Items	↓	TPR WG	05/31/22		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	06/03/22		Not Started	
	WP	Meeting #51 Review of Outstanding Items	↓	TPR WG	06/07/22		Not Started	
	MS	Submit Phase 1A Initial Report for Public Comment	!	TPR WG	06/15/22		Not Started	
