

Project Tracking & Rollup

DASHBOARD


Project Name PDP: Transfer Policy Review - Phase 1 **Program** Transfers **Project Sponsor** GNSO Council

Project Information **Tasks by Status** **Project Contacts** **Participant Summary**

25%
% Complete

02/18/21
Actual Start

12/28/23
Planned Finish




Roger Carney
Chair

n/a
Vice_Chair

Greg DiBiase
Liaison

Emily Barabas
Staff_Lead

Berry Cobb
Project_Manager

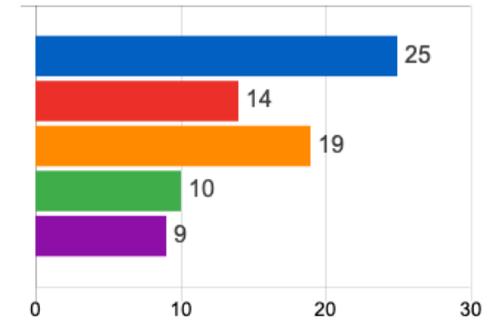

Project Status & Health

Project Status: On-Schedule

Project Health: On-Target

● Not_Started ● Complete ● In_Progress ● On_Hold

● Member ● Alternate ● Observer_Email_Only ● Staff_Assigned ● Staff_Not_Assigned

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021 2022 2023											
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	PDP: Transfer Policy Review - Phase 1	02/18/21	12/28/23	25%	In Progress	PDP: Transfer Policy Review - Phase 1											
	PROJECT CONTROL	02/18/21	12/28/23	35%	In Progress	PROJECT CONTROL											
	GROUP DELIBERATIONS	05/13/21	02/22/23	41%	In Progress	GROUP DELIBERATIONS											
	Phase 1A Policy Topics	06/02/21	05/11/22	36%	In Progress	Phase 1A Policy Topics											
	Phase 1B Policy Topics	06/15/22	02/22/23			Phase 1B Policy Topics											
	INITIAL REPORT	06/24/21	05/17/23	13%	In Progress	INITIAL REPORT											
	Publish Initial Report	06/15/22	06/15/22			Publish Initial Report											
	Publish Initial Report	03/29/23	03/29/23			Publish Initial Report											
	FINAL REPORT	08/04/22	08/16/23		Not Started	FINAL REPORT											
	Review of public comments - Phase 1A	08/04/22	09/14/22			Review of public comments - Phase 1A											
	Review of public comments - Phase 1B	05/18/23	06/28/23			Review of public comments - Phase 1B											
	Submission of Final Report to the GNSO Council	08/16/23	08/16/23			Submission of Final Report to the GNSO Council											

4 - Working Group

Title: PDP: Transfer Policy Review - Phase 1 (TPR_P1)

Description & Scope: On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

Composition:

Chair(s):	Roger Carney
Council Liaison:	Greg Dibiase
Staff:	E. Barabas, J. Hedlund, C. Tubergen
# Participants:	37 Participants (link)
# Observers:	19
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	Charter

Project Management:

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	18 Feb 2021	18 Feb 2021	224	28 Dec 2023	TBD

Program	Progress	Status	Health
Transfers	25%	●	■

STATUS: ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold

HEALTH: ■ On-Target ■ At-Risk ■ In-Trouble

Milestones/Work plan ([link](#)):

Milestone/Task	Date	
Final Issue Report to Council	Jan-21	✓
Project Start	Feb-21	✓
Charter Approved	Mar-21	✓
Chair appointment	Apr-21	✓
1st Plenary meeting	May-21	✓
Project Plan and Work plan Adoption	Jul-21	✓
SO/AC & SG/C Input to PDP	Aug-21	✓
Phase 1A Issue Deliberations	Aug-22	■
Populate stable draft papers w/ potential recs.	May-22	■
Discuss/approve findings and interim recs.	May-22	
Consolidate interim recommendations and findings	Jun-22	
Issue Phase 1A Initial Report for public comment	Jun-22	
Review public comment input	Sep-22	
Phase 1B Issue Deliberations	Mar-23	
Populate stable draft papers w/ potential recs.	Feb-23	
Discuss/approve findings and interim recs.	Mar-23	
Consolidate interim recommendations and findings	Mar-23	
Issue Phase 1B Initial Report for public comment	Mar-23	
Review public comment input & prepare final report	Mar-23	
Finalize Report	Jul-23	
Determine consensus levels on recommendations	Jun-23	
Adopt final recommendations and report (Phase 1A+1B)	Jul-23	
Send final report to GNSO Council	Aug-23	
GNSO Council adoption of consensus recs.	Oct-23	
Issue public comment for Board consideration	Oct-23	
ICANN Board adoption of consensus recs.	Jan-24	
Prior period % Complete	23%	■

Status/Health Rationale:

- The project schedule is confirmed by the GNSO Council and Status is “On-schedule” and the Health is “On-Target”.

Current Activities:

- Continue deliberations on Auth-Info Code Management; review of candidate recommendations on the Transfer Authorization Code.
- Continue deliberations on Losing & Gaining FOA.

Planned Activities:

- Deliberate AuthCode Additional Security Measures as noted in the charter.
- Transfer policy package: review of TAC, Losing FOA and Gaining FOA candidate recommendations

Open Issues, Risks & Mitigation Plan:

- None at this time.

Completed in prior period(s):

- Completed and distributed Project Package for September.
- Thomas Keller of RrSG resigned from the PDP, 27 Sep 2021.

Project Tracking & Rollup

DASHBOARD



Project Roster


Participant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
Nanghaka Daniel Khauka	Member		05/04/21		https://community.icann.org
Steinar Grøtterød	Member		05/05/21		https://community.icann.org
Raymond Mamattah	Alternate		05/04/21		https://community.icann.org
Lutz Donnerhacke	Alternate		05/08/21		https://community.icann.org
Group Selected / Nominated By: Group Name Commercial Business Users Constituency (BC)					
Zak Muscovitch	Member		04/23/21		https://community.icann.org
Arinola Akinyemi	Alternate		08/12/21		https://community.icann.org
Group Selected / Nominated By: Group Name GNSO Council					
Gregory DiBiase	Member	Liaison	06/04/21		https://community.icann.org
Roger Carney	Member	Chair	04/23/21		https://community.icann.org
Group Selected / Nominated By: Group Name Independent					
Steve Crocker	Member	Subject Matter Expert	04/26/21		https://community.icann.org
Group Selected / Nominated By: Group Name Intellectual Property Constituency (IPC)					
Mike Rodenbaugh	Member		04/21/21		https://community.icann.org
Salvador Camacho Hernandez	Member		04/26/21		https://community.icann.org
Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)					
Isabelle Colas	Staff - Assigned	Liaison	06/10/21		
Berry Cobb	Staff - Assigned		02/18/21		
Emily Barabas	Staff - Assigned		02/18/21		
Michelle DeSmyter	Staff - Assigned		02/18/21		
Terri Agnew	Staff - Assigned		02/18/21		
Caitlin Tubergen	Staff - Assigned		02/18/21		
Julie Bisland	Staff - Assigned		02/18/21		
Julie Hedlund	Staff - Assigned		02/18/21		
Nathalie Peregrine	Staff - Assigned		02/18/21		
Holida Yanik	Staff - Assigned		04/30/21		
Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency (ISPCP)					
John Woodworth	Member		04/14/21		https://community.icann.org
Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)					
Wisdom Donkor	Member		06/01/21		https://community.icann.org
Farzaneh Badiei	Member		06/01/21		https://community.icann.org
Akinremi Peter Taiwo	Alternate		06/02/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)					
Keiron Tobin	Member		06/07/21		https://community.icann.org
Thomas Keller	Member		04/26/21	09/27/21	https://community.icann.org
Eric Rokobauer	Member		04/26/21		https://community.icann.org
Theo Geurts	Member		04/23/21		https://community.icann.org
Kristian Ørmen	Member		04/23/21		https://community.icann.org
Crystal Ondo	Member		04/23/21		https://community.icann.org
Sarah Wylid	Member		04/23/21		https://community.icann.org
Prudence Malinki	Member		04/27/21		https://community.icann.org
Catherine Merdinger	Member		04/27/21		https://community.icann.org
Owen Smigelski	Member		04/27/21		https://community.icann.org
Richard Merdinger	Member		05/05/21	06/07/21	https://community.icann.org
Antonia Nan Chu	Member		05/06/21		https://community.icann.org
Volker Greimann	Alternate		04/24/21		https://community.icann.org
Jothan Frakes	Alternate		04/23/21		https://community.icann.org
Essie Musailov	Alternate		04/23/21		https://community.icann.org
Pam Little	Alternate		04/26/21		https://community.icann.org
Richard Brown	Alternate		04/26/21		https://community.icann.org
Min Feng	Alternate		04/26/21		https://community.icann.org
Jacques Blanc	Alternate		04/29/21		https://community.icann.org
Arnaud Wittersheim	Alternate		05/05/21		https://community.icann.org
Jody Kolker	Alternate		05/07/21		https://community.icann.org
Group Selected / Nominated By: Group Name Registry Stakeholder Group (RySG)					

James Galvin	Member		04/27/21	https://community.icann.org
Barbara Knight	Member		05/04/21	https://community.icann.org
Beth Bacon	Alternate		05/04/21	https://community.icann.org


Project Tracking & Rollup

DASHBOARD


Work-Plan Activity Metrics

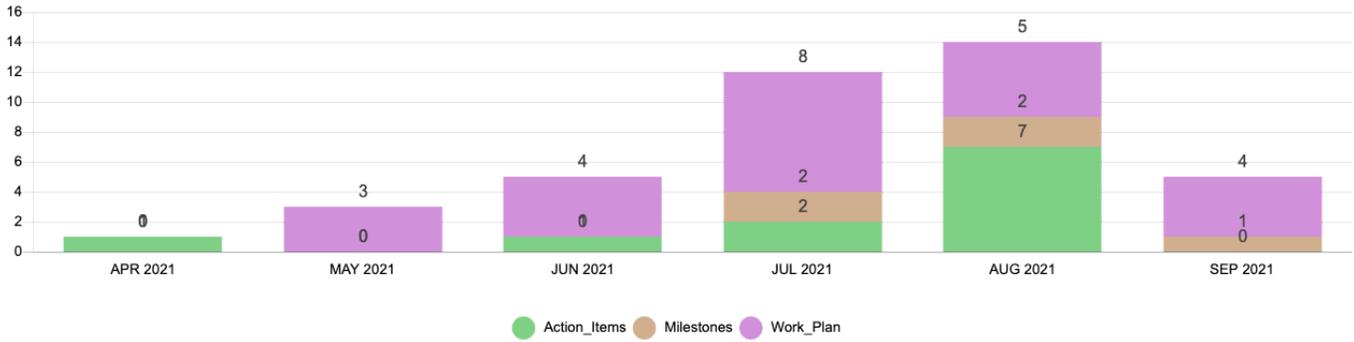

Mailman Activity



Meeting Activity



Project Tracking & Rollup

DASHBOARD



Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 530	Sum 466	Avg 87.9%
Primary At-Large Advisory Committee (ALAC)	Sum 55	Sum 52	Avg 94.5%
Attendee Name Lutz Donnerhacke	Sum 10	Sum 10	Avg 100.0%
Attendee Name Nanghaka Daniel Khauka	Sum 17	Sum 16	Avg 94.1%
Attendee Name Raymond Mamattah	Sum 11	Sum 11	Avg 100.0%
Attendee Name Steinar Grøtterød	Sum 17	Sum 15	Avg 88.2%
Primary Commercial Business Users Constituency (BC)	Sum 22	Sum 20	Avg 90.9%
Attendee Name Arinola Akinyemi	Sum 5	Sum 5	Avg 100.0%
Attendee Name Zak Muscovitch	Sum 17	Sum 15	Avg 88.2%
Primary GNSO Council	Sum 30	Sum 27	Avg 90.0%
Attendee Name Gregory DiBiase	Sum 13	Sum 10	Avg 76.9%
Attendee Name Roger Carney	Sum 17	Sum 17	Avg 100.0%
Primary Independent	Sum 17	Sum 9	Avg 52.9%
Attendee Name Steve Crocker	Sum 17	Sum 9	Avg 52.9%
Primary Intellectual Property Constituency (IPC)	Sum 34	Sum 16	Avg 47.1%
Attendee Name Mike Rodenbaugh	Sum 17	Sum 9	Avg 52.9%
Attendee Name Salvador Camacho Hernandez	Sum 17	Sum 7	Avg 41.2%
Primary Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Sum 17	Sum 14	Avg 82.4%
Attendee Name John Woodworth	Sum 17	Sum 14	Avg 82.4%
Primary Non-Commercial Stakeholder Group (NCSG)	Sum 31	Sum 25	Avg 80.6%
Attendee Name Akinremi Peter Taiwo	Sum 3	Sum 3	Avg 100.0%
Attendee Name Farzaneh Badiei	Sum 14	Sum 8	Avg 57.1%
Attendee Name Wisdom Donkor	Sum 14	Sum 14	Avg 100.0%
Primary Registrar Stakeholder Group (RrSG)	Sum 276	Sum 257	Avg 93.1%
Attendee Name Antonia Nan Chu	Sum 17	Sum 17	Avg 100.0%
Attendee Name Arnaud Wittersheim	Sum 12	Sum 12	Avg 100.0%
Attendee Name Catherine Merdinger	Sum 17	Sum 15	Avg 88.2%
Attendee Name Crystal Ondo	Sum 17	Sum 14	Avg 82.4%
Attendee Name Eric Rokobauer	Sum 16	Sum 16	Avg 100.0%
Attendee Name Essie Musailov	Sum 16	Sum 16	Avg 100.0%
Attendee Name Jacques Blanc	Sum 4	Sum 4	Avg 100.0%
Attendee Name Jody Kolker	Sum 15	Sum 15	Avg 100.0%
Attendee Name Jothan Frakes	Sum 17	Sum 17	Avg 100.0%
Attendee Name Keiron Tobin	Sum 13	Sum 11	Avg 84.6%
Attendee Name Kristian Ørmen	Sum 17	Sum 16	Avg 94.1%
Attendee Name Min Feng	Sum 2	Sum 2	Avg 100.0%
Attendee Name Owen Smigelski	Sum 17	Sum 16	Avg 94.1%
Attendee Name Prudence Malinki	Sum 17	Sum 17	Avg 100.0%
Attendee Name Richard Brown	Sum 11	Sum 11	Avg 100.0%
Attendee Name Richard Merdinger	Sum 4	Sum 4	Avg 100.0%
Attendee Name Sarah Wyld	Sum 17	Sum 15	Avg 88.2%
Attendee Name Theo Geurts	Sum 17	Sum 16	Avg 94.1%
Attendee Name Thomas Keller	Sum 16	Sum 9	Avg 56.3%
Attendee Name Volker Greimann	Sum 14	Sum 14	Avg 100.0%
Primary Registry Stakeholder Group (RySG)	Sum 48	Sum 46	Avg 95.8%
Attendee Name Barbara Knight	Sum 17	Sum 16	Avg 94.1%
Attendee Name Beth Bacon	Sum 14	Sum 14	Avg 100.0%
Attendee Name James Galvin	Sum 17	Sum 16	Avg 94.1%

Open source report to view more

Plenary - Alternates Replacing Members Log



<https://community.icann.org/x/V4aUCQ>

WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Q1			Q2			Q3			Q4			Q1			Q2			Q3														
								Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
	PDP: Transfer Policy Review - Phase 1	746d	02/18/21	12/28/23		25%	In Progress																																	
1	PROJECT CONTROL	746d	02/18/21	12/28/23		35%	In Progress																																	
1.1	Project start confirmed	0	02/18/21	02/18/21		100%	Complete																																	
1.2	Adopt/Confirm charter	25d	02/18/21	03/24/21	3	100%	Complete																																	
1.3	Confirmation of Team	50d	02/18/21	04/28/21	3	100%	Complete																																	
1.4	Appointment of Team Chair	50d	02/18/21	04/28/21	3	100%	Complete																																	
1.5	Appointment of Liaison to GNSO Council	50d	02/18/21	04/28/21	3	100%	Complete																																	
1.6	Chair / Staff preparations	10d	04/29/21	05/12/21	6	100%	Complete																																	
1.7	Project Management	696d	04/29/21	12/28/23		18%	In Progress																																	
1.7.1	Develop and confirm Project Plan	30d	04/29/21	06/09/21	6	100%	Complete																																	
1.7.2	Obtain project plan approval from GNSO Council	30d	06/10/21	07/21/21	10	100%	Complete																																	
1.7.3	Develop monthly Project Packages and deliver to Group & Council	540d	07/22/21	08/16/23	11	9%	In Progress																																	
1.7.4	Leadership Sub team	600d	04/29/21	08/16/23		18%	In Progress																																	
1.7.4.1	On-going preparation and planning of group activities	600d	04/29/21	08/16/23	6	18%	In Progress																																	
1.7.5	Close project and transition project to implementation	1d	12/28/23	12/28/23	14, 222																																			
2	GROUP DELIBERATIONS	465d	05/13/21	02/22/23		41%	In Progress																																	
2.1	First meeting of Team	1d	05/13/21	05/13/21	8	100%	Complete																																	
2.2	Understand Charter, organize materials and develop initial approach	10d	05/13/21	05/26/21	8	100%	Complete																																	
2.3	Overview & initial discussion of all Policy Topics	15d	05/13/21	06/02/21	8	100%	Complete																																	
2.4	Develop definitions and terminology	30d	05/13/21	06/23/21	8	100%	Complete																																	
2.5	Input from other SO/ACs & GNSO SG-Cs	91d	05/27/21	09/30/21		100%	Complete																																	
2.6	Phase 1A Policy Topics	245d	06/02/21	05/11/22		36%	In Progress																																	
2.6.1	Topic 1 Deliberations - Gaining FOA	40d	12/02/21	01/26/22		36%	In Progress																																	
2.6.2	Topic 2 Deliberations - Losing FOA	40d	10/07/21	12/01/21		71%	In Progress																																	
2.6.3	Topic 3 Deliberations - Additional Security Measures	40d	08/12/21	10/06/21			On Hold																																	
2.6.4	Topic 4 Deliberations - Auth-Info Code Management	180d	06/03/21	02/09/22		50%	In Progress																																	
2.6.5	Topic 5 Deliberations - Bulk Use of Auth-Info Codes	40d	02/10/22	04/06/22																																				
2.6.6	Topic 6 Deliberations - Wave 1, Recommendation 27	25d	04/07/22	05/11/22																																				
2.6.7	Unplanned Issues & Tasks	0	06/02/21	06/02/21																																				
2.7	Phase 1B Policy Topics	180d	06/15/22	02/22/23																																				
2.7.1	Topic 7 Deliberations - Change of Registrant / Overall Policy	40d	06/16/22	08/10/22																																				
2.7.2	Topic 8 Deliberations - Change of Registrant / 60-Day Lock	40d	08/11/22	10/05/22																																				
2.7.3	Topic 9 Deliberations - Change of Registrant / Privacy/Proxy Customers	35d	10/06/22	11/23/22																																				
2.7.4	Topic 10 Deliberations - Change of Registrant / Designated Agent	25d	11/24/22	12/28/22																																				
2.7.5	Topic 11 Deliberations - Change of Registrant / Additional Questions	20d	12/29/22	01/25/23																																				
2.7.6	Topic 12 Deliberations - Change of Registrant / Wave 1 - Recommendation 27	20d	01/26/23	02/22/23																																				
2.7.7	Unplanned Issues & Tasks	0	06/15/22	06/15/22																																				
3	INITIAL REPORT	495d	06/24/21	05/17/23		13%	In Progress																																	
3.1	Phase 1A Initial Report	290d	06/24/21	08/03/22		23%	In Progress																																	
3.1.1	Populate stable drafts as required	230d	06/24/21	05/11/22	20	30%	In Progress																																	
3.1.2	Discuss/approve findings and interim recommendations	10d	05/12/22	05/25/22	27, 40, 51, 60, 72, 83																																			
3.1.3	Consolidate interim recommendations and findings	10d	05/26/22	06/08/22	198																																			
3.1.4	Build Draft Report for public comment	10d	05/26/22	06/08/22	198																																			
3.1.5	Approve Draft Report for public comment	5d	06/09/22	06/15/22	200																																			
3.1.6	Publish Initial Report	0	06/15/22	06/15/22	201																																			
3.1.7	Communicate Initial Report	5d	06/16/22	06/22/22	201																																			
3.1.8	Public comment forum on the Initial Report (45 days)	35d	06/16/22	08/03/22	201																																			
3.2	Phase 1B Initial Report	240d	06/16/22	05/17/23																																				
3.2.1	Populate stable drafts as required	60d	06/16/22	09/07/22	202																																			
3.2.2	Discuss/approve findings and interim recommendations	10d	02/23/23	03/08/23	111, 122, 135, 146, 1																																			
3.2.3	Consolidate interim recommendations and findings	10d	03/09/23	03/22/23	207																																			
3.2.4	Build Draft Report for public comment	10d	03/09/23	03/22/23	207																																			
3.2.5	Approve Draft Report for public comment	5d	03/23/23	03/29/23	209																																			
3.2.6	Publish Initial Report	0	03/29/23	03/29/23	210																																			
3.2.7	Communicate Initial Report	5d	03/30/23	04/05/23	210																																			
3.2.8	Public comment forum on the Initial Report (45 days)	35d	03/30/23	05/17/23	210																																			
4	FINAL REPORT	270d	08/04/22	08/16/23			Not Started																																	
4.1	Review of public comments - Phase 1A	30d	08/04/22	09/14/22	204																																			
4.2	Review of public comments - Phase 1B	30d	05/18/23	06/28/23	213																																			
4.3	Continue deliberations of policy topics towards a Final Report	50d	05/18/23	07/26/23	204, 213																																			
4.4	Build Final Report & Final Deliberations	5d	07/27/23	08/02/23	217																																			
4.5	Determine consensus levels on interim recommendations	10d	08/03/23	08/16/23	218																																			
4.6	Adopt final recommendations and report	10d	08/03/23	08/16/23	218																																			
4.7	Submission of Final Report to the GNSO Council	0	08/16/23	08/16/23	220																																			
5	POST GROUP TASKS	95d	08/17/23	12/27/23			Not Started																																	
	PDP CHECKLIST	824d	08/20/20	08/16/23		0%																																		

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	AI	Leadership team to prepare for first meeting	—	TPR WG	04/30/21	04/30/21	Complete	
	WP	Meeting #01 Introductions, Discuss proposed approach and timing, review background docs, homework assignments	↓	TPR WG	05/14/21	05/14/21	Complete	
	WP	Meeting #02 Review of Charter Questions	↓	TPR WG	05/21/21	05/21/21	Complete	
	WP	Meeting #03 Review of Charter Questions	↓	TPR WG	05/25/21	05/25/21	Complete	
	WP	Meeting #04 Review of Charter Questions	↓	TPR WG	06/01/21	06/01/21	Complete	
	WP	Meeting #05 Begin Review of Topic #4 Auth Info Code Management	↓	TPR WG	06/08/21	06/08/21	Complete	
	AI	TPR WG members to review the draft outreach document for SO/AC/SG/Cs and propose additional questions or edits to the text by 24 June 2021.	—	TPR WG	06/24/21	06/24/21	Complete	
	WP	Meeting - ICANN71 Seek broad community input on TPR Policy Topics	↓	TPR WG	06/16/21	06/16/21	Complete	
	WP	Meeting #06 Continue Review of Topic #4 Auth Info Code Management	↓	TPR WG	06/29/21	06/29/21	Complete	
	AI	Support Staff to distribute outreach document for SO/AC/SG/Cs with a deadline to respond of 35 days..	—	Policy Support Staff	07/02/21	07/02/21	Complete	
	MS	Release Early Input to SOs/ACs	!	Policy Support Staff	07/09/21	07/09/21	Complete	
	WP	Meeting #07 Continue Review of Topic #4 Auth Info Code Management	↓	TPR WG	07/06/21	07/06/21	Complete	
	MS	Submit Workplan to GNSO Council	!	TPR Leadership	07/12/21	07/12/21	Complete	Project plan submitted to Council on 12 July and confirmed on 22 July.
	WP	Meeting #08 ---CANCELLED---	↓	TPR WG	07/13/21	07/13/21	Complete	
	WP	TPR Small Team Call #01 - Develop principles and strawman	↓	TPR WG	07/16/21	07/16/21	Complete	
	WP	Meeting #09 ---CANCELLED---	↓	TPR WG	07/20/21	07/20/21	Complete	
	WP	TPR Small Team Call #02 - Develop principles and strawman	↓	TPR WG	07/19/21	07/19/21	Complete	
	WP	TPR Small Team Call #03 - Review principles and strawman	↓	TPR WG	07/23/21	07/23/21	Complete	
	WP	TPR Small Team Call #04 - Review principles and strawman	↓	TPR WG	07/26/21	07/26/21	Complete	
	AI	Staff to move the cleaned up principles and the strawman list to the WG AuthInfo Code discussion document to send along with the agenda for the WG meeting, with links to the recording/notes for WG members to review.	—	Policy Support Staff	07/26/21	07/26/21	Complete	
	WP	Meeting #10 Continue Review of Topic #4 Auth Info Code Management	↓	TPR WG	07/27/21	07/27/21	Complete	
	AI	Homework for WG members – add comments and suggested edits to the principles and strawman list at: https://docs.google.com/document/d/1O9PAnxWfUuPofLQCWlQXz8IT7KEj1HgH3b_obh0AK00/edit?usp=sharing [docs.google.com] including anything that might be missing, clarifications/changes to terminology, impacts on use cases, etc.	—	TPR WG	08/03/21	08/03/21	Complete	
	WP	Meeting #11 Continue Review of Topic #4 Auth Info Code Management	↓	TPR WG	08/03/21	08/03/21	Complete	
	MS	Early Input Deadline	↓	TPR WG	08/04/21	08/04/21	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	08/06/21	08/06/21	Complete	Project Package sent to both the WG & the Council
	WP	Meeting #12 Begin Review of Topic #3 Losing FOA	↓	TPR WG	08/10/21	08/10/21	Complete	
	AI	Homework for WG members – add comments and suggested edits to the principles and strawman list at: https://docs.google.com/document/d/1O9PAnxWfUuPofLQCWlQXz8IT7KEj1HgH3b_obh0AK00/edit?usp=sharing [docs.google.com] including anything that might be missing, clarifications/changes to terminology, impacts on use cases, etc.	—	TPR WG	08/17/21	08/17/21	Complete	
	WP	Meeting #13 Continue review of Topic #2 Losing FOA	↓	TPR WG	08/17/21	08/17/21	Complete	
	AI	Homework for WG members – In preparation for the next meeting on 24 August WG members to provide suggested language for changes to the current losing FOA policy in the working document along with those provided on page 3 at: https://docs.google.com/document/d/1wCUMe9ii6g05kUZ558luUvJaS6K2t0GZJYvifOy-raY/edit?usp=sharing	—	TPR WG	08/17/21	08/24/21	Complete	
	WP	Meeting #14 Continue review of Topic #2 Losing FOA	↓	TPR WG	08/24/21	08/24/21	Complete	
	AI	Homework - Leadership and staff will lay out the three proposed notifications/communications concepts/proposals. WG members to review and comment in preparation for the meeting on 31 August. See the document at: https://docs.google.com/document/d/1wCUMe9ii6g05kUZ558luUvJaS6K2t0GZJYvifOy-raY/edit?usp=sharing	—	TPR WG	08/24/21	08/30/21	Complete	
	WP	Meeting #15 Continue review of Topic #2 Losing FOA	↓	TPR WG	08/31/21	08/31/21	Complete	
	AI	Homework - Sarah Wyld volunteered to create a flow chart. Staff will create a Google doc template for this.	—	Sarah Wyld	08/24/21	08/30/21	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	09/03/21	09/06/21	Complete	
	WP	Meeting #16 Continue review of Topic #2 Losing FOA; start overview of Gaining FOA	↓	TPR WG	09/07/21	09/07/21	Complete	
	AI	Homework: WG members should look at reasons for denial in the current policy and comment on whether or not we need to update those reason. Add lines or comments to the Transfer Steps and Notifications Chart: Transfer Steps and Notifications chart https://docs.google.com/spreadsheets/d/17ADMRTYxN5sA-e3WoEI96KxIH5YRALBsxgwOmpsCC0g/edit#gid=0	—	TPR WG	09/20/21	08/30/21	Complete	
	AI	Leadership and staff to clean up the document based on comments and determine where steps can be combined.	—	TPR Leadership	08/24/21	08/30/21	Complete	

