


# RPM IGO CRWT - Summary Timeline

30 Apr 2021

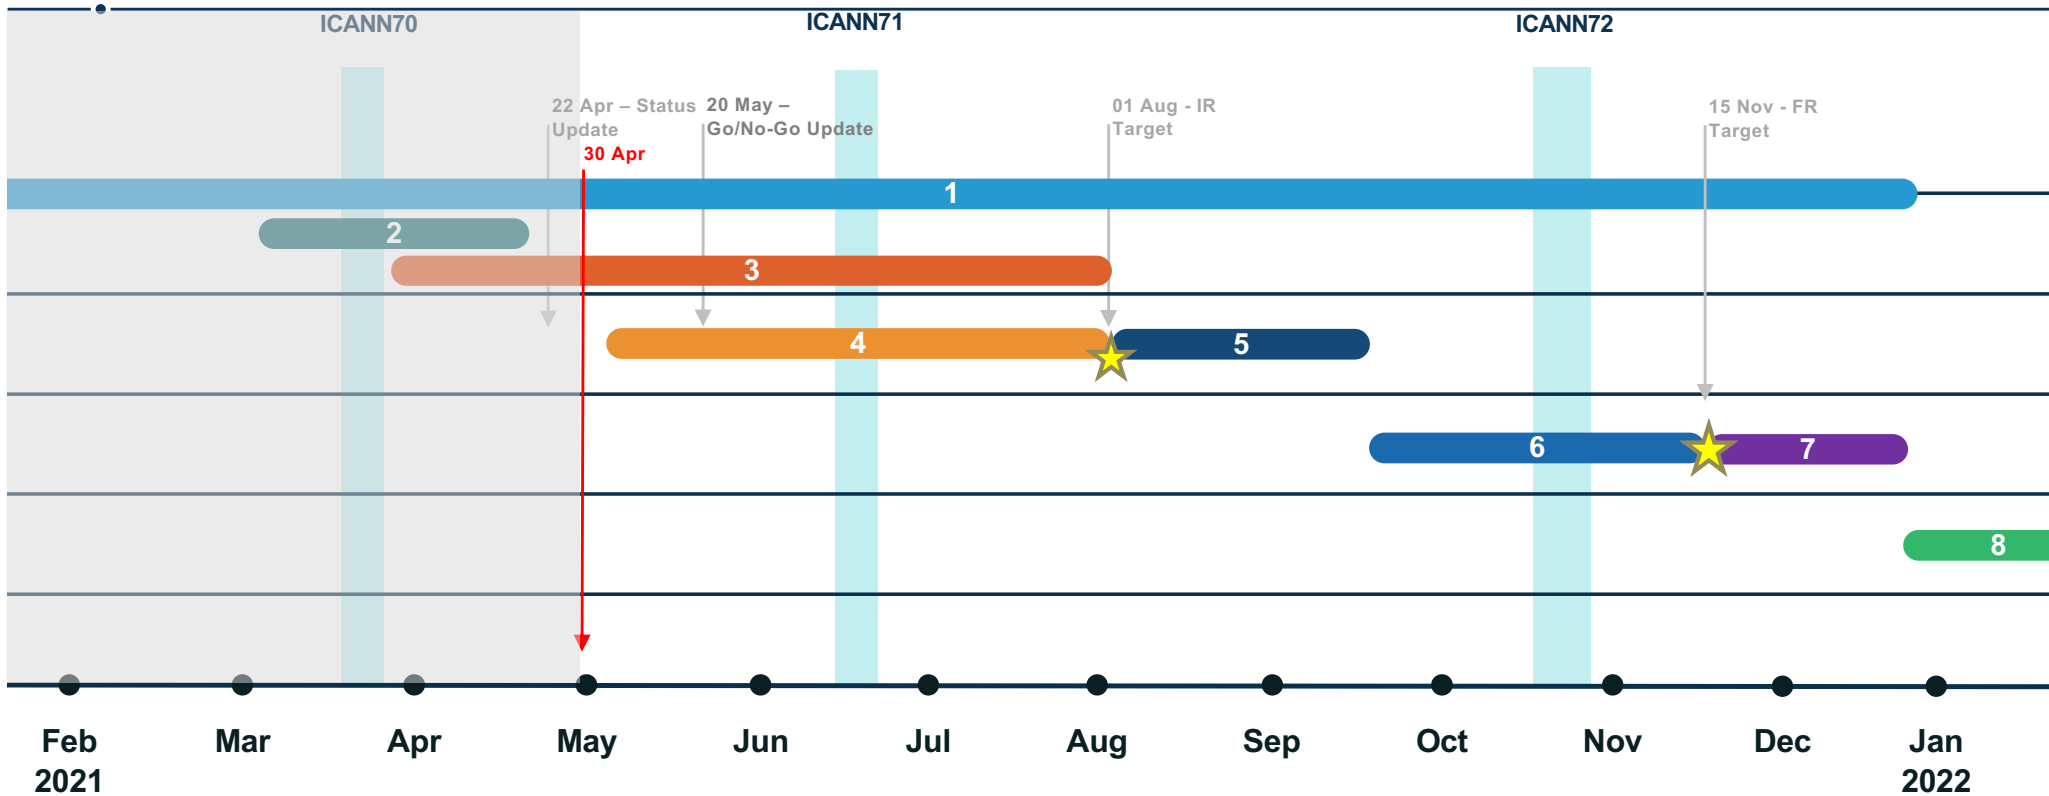

- 1 Project Management & Workplan
- 2 Review prior materials & define scope
- 3 Deliberate possible policy solutions
- 4 Construct Initial Report
- 5 Public Comment on Initial Report
- 6 Review of Public Comment & Submission of Final Report
- 7 Council Consideration of Final Report
- 8 Public Comment during Board Consideration
- 9 Board Consideration

Complete: 37%    Status: ●    Health: ■



## 4 - Working Group

**Title:** PDP: RPM - IGO Curative Rights Work Track (RPM\_IGO\_CRWT)

**Description & Scope:** The GNSO Council created a Work Track within the RPMs PDP WG, based on the Council referral of recommendation 5 from the IGO-INGO Curative Rights Protection Mechanisms PDP WG Final Report. The Addendum to the RPMs PDP Charter was adopted by the GNSO Council in January of 2020.



**Composition:**

<b>Chair(s):</b>	Chris Dispain
<b>Council Liaison:</b>	John McElwaine
<b>Staff:</b>	M. Wong, S. Chan, B. Cobb
<b># Participants:</b>	19 Participants ( <a href="#">link</a> )
<b># Observers:</b>	1
<b>Tools:</b>	<a href="#">Mailing List</a> / <a href="#">Meeting Schedule</a> / <a href="#">Wiki</a>
<b>Charter:</b>	<a href="#">Charter Addendum</a>

**Project Management:**

Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date
WG	31 Oct 2019	17 Dec 2020	483	15 Nov 2021	TBD

Progress	Status	Health
<b>37%</b>		

**STATUS:** ■ Planned ● On-schedule ● Revised schedule ▲ Behind schedule ◆ Target will be missed ■ On-hold  
**HEALTH:** ■ On-Target ■ At-Risk ■ In-Trouble

**Milestones/Work plan (link):**

Milestone/Task	Date	
Work Track Charter <a href="#">Adopted</a>	Jan-20	✓
Project Start	Dec-20	✓
1st WT Meeting	Feb-21	✓
Project Plan and Work plan	Apr-21	✓
Issue Deliberations	Oct-21	■
Assemble initial conclusions	Jul-21	■
Consolidate interim recommendations and findings	Jul-21	■
Build Draft Report for public comment	Jul-21	■
Issue report for public comment	Aug-21	■
Review public comment input	Oct-21	
Determine consensus levels on recommendations	Nov-21	
Finalize Report	Nov-21	
Adopt final recommendations and report	Nov-21	
Send final report to GNSO Council	Nov-21	
GNSO Council adoption of consensus recs.	Dec-21	
Issue public comment for Board consideration	Mar-22	
ICANN Board adoption of consensus recs.	Apr-22	
Prior period % Complete	30%	■

**Status/Health Rationale:**

- This project has recently started with a Status of “On-Schedule” and Health of “On-Target”.

**Current Activities:**

- Continued analysis of Dispute Resolution eligibility requirements (e.g., standing) for IGOs and secondary review options in the limited cases where an IGO successfully asserts jurisdictional immunity..

**Planned Activities:**

- Conclude deliberations on IGO eligibility requirements and jurisdictional immunity as it relates to the UDRP, and in the context of the IGO-INGO Curative Rights WG’s Recommendation #5.

**Open Issues, Risks & Mitigation Plan:**

- Scope of WT’s charter addendum may be too restrictive to develop a solution that is mutually agreeable to the WT. WT Leadership will consult with the GNSO Council if the addendum proves to be a hindrance to the WT achieving its desired outcomes.

**Completed in prior period(s):**

- Review of preliminary agreements and options on approach of the Work Track.
- Work Track’s project plan and Project Package accepted by GNSO Council on 22 April 2021.
- GNSO Council liaison to the WT provided an update to the GNSO Council, noting the WT is struggling with the scope of charter addendum.

## Roster - WG

As of 2021-05-01 21:45:22 Greenwich Mean Time/GMT • Generated by Berry Cobb

Filtered By

Show: All participants

Community Group: Group Name equals RPM - IGO Curative Rights Work Track


Participant Type equals Alternate,Member,Staff - Assigned

Participant Type ↑	Group Selected / Nominated By: Group Name ↑	Participant Contact Name: Full Name	Role	Participation Start Date	Participation End Date	SOI Link
Alternate	At-Large Advisory Committee (ALAC)	Justine Chew		17-12-2020		<a href="https://community.icann.org/x/bTefAg">https://community.icann.org/x/bTefAg</a>
		Vanda Scartezini		17-12-2020		<a href="https://community.icann.org/x/oAKAAw">https://community.icann.org/x/oAKAAw</a>
	Governmental Advisory Committee (GAC)	Jorge Cancio		17-12-2020		<a href="https://community.icann.org/x/lwUnAQ">https://community.icann.org/x/lwUnAQ</a>
		David Satola		17-12-2020		<a href="https://community.icann.org/x/AoUmCQ">https://community.icann.org/x/AoUmCQ</a>
		Matthew Coleman		17-12-2020		<a href="https://community.icann.org/x/BIUmCQ">https://community.icann.org/x/BIUmCQ</a>
Member	At-Large Advisory Committee (ALAC)	Yrjö Länsipuro		17-12-2020		<a href="https://community.icann.org/x/r59EB">https://community.icann.org/x/r59EB</a>
		Carlos Raúl Gutiérrez		17-12-2020		<a href="https://community.icann.org/x/LVp-Ag">https://community.icann.org/x/LVp-Ag</a>
		Jay Chapman		17-12-2020		<a href="https://community.icann.org/x/ULrhAg">https://community.icann.org/x/ULrhAg</a>
	Commercial Business Users Constituency (BC)	Chris Disspain	Chair	17-12-2020		<a href="https://community.icann.org/x/kQBpBQ">https://community.icann.org/x/kQBpBQ</a>
		Jeffrey Neuman	Liaison	08-01-2021		<a href="https://community.icann.org/x/qlBwAg">https://community.icann.org/x/qlBwAg</a>
	GNSO Council	John McElwaine	Liaison	08-01-2021		<a href="https://community.icann.org/x/lV9-Ag">https://community.icann.org/x/lV9-Ag</a>
		Susan Anthony		17-12-2020		<a href="https://community.icann.org/x/9gZyB">https://community.icann.org/x/9gZyB</a>
	Governmental Advisory Committee (GAC)	Kavouss Arasteh		17-12-2020		<a href="https://community.icann.org/x/ZC6AAw">https://community.icann.org/x/ZC6AAw</a>
		Alexandra Excoffier		17-12-2020		<a href="https://community.icann.org/x/-4QmCQ">https://community.icann.org/x/-4QmCQ</a>
		Brian Beckham		17-12-2020		<a href="https://community.icann.org/x/LK7bAQ">https://community.icann.org/x/LK7bAQ</a>
		Paul McGrady		11-01-2021		<a href="https://community.icann.org/x/CTCFag">https://community.icann.org/x/CTCFag</a>
	Intellectual Property Constituency (IPC)	Oswaldo Novoa		17-12-2020		<a href="https://community.icann.org/x/HgbPAQ">https://community.icann.org/x/HgbPAQ</a>
	Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Juan Manuel Rojas		17-12-2020		<a href="https://community.icann.org/x/E8PbAQ">https://community.icann.org/x/E8PbAQ</a>
	Non-Commercial Stakeholder Group (NCSG)	Krishna Seeburn		17-12-2020	03-03-2021	<a href="https://community.icann.org/x/ABrxAg">https://community.icann.org/x/ABrxAg</a>
		Ioana Florina Stupariu		17-12-2020		<a href="https://community.icann.org/x/rjxEb">https://community.icann.org/x/rjxEb</a>
	Staff - Assigned	Internet Corporation for Assigned Names & Numbers (ICANN)	Mary Wong		17-12-2020	
Steven Chan				17-12-2020		
Julie Bisland				17-12-2020		
Andrea Glandon				17-12-2020		
Terri Agnew				17-12-2020		
Berry Cobb				17-12-2020		
<b>Total</b>						26

**EPDP-P2A - Plenary**


<b>Represented Group / Member &amp; Alternate</b>	<b>Invited</b>	<b>Attended</b>	<b>% Attendance</b>
<b>At-Large Advisory Committee (ALAC)</b>	<b>8</b>	<b>8</b>	<b>78.4</b>
Carlos Raúl Gutiérrez	8	4	50.0
Justine Chew	6	5	83.0
Vanda Scartezini	6	5	83.0
Yrjö Länsipuro	8	8	100.0
<b>Commercial Business Users Constituency (BC)</b>	<b>8</b>	<b>8</b>	<b>100.0</b>
Jay Chapman	8	8	100.0
<b>GNSO Council</b>	<b>8</b>	<b>8</b>	<b>96.0</b>
Chris Disspain	8	8	100.0
Jeffrey Neuman	8	8	100.0
John McElwaine	8	7	88.0
<b>Governmental Advisory Committee (GAC)</b>	<b>8</b>	<b>8</b>	<b>89.5</b>
Alexandra Excoffier	8	7	88.0
Brian Beckham	8	7	88.0
David Satola	7	7	100.0
Jorge Cancio	1	0	0.0
Kavouss Arasteh	8	6	75.0
Matthew Coleman	7	7	100.0
Susan Anthony	8	8	100.0
<b>Intellectual Property Constituency (IPC)</b>	<b>8</b>	<b>7</b>	<b>88.0</b>
Paul McGrady	8	7	88.0
<b>Internet Service Providers and Connectivity Providers Constituency (ISPCP)</b>	<b>8</b>	<b>6</b>	<b>75.0</b>
Osvaldo Novoa	8	6	75.0
<b>Non-Commercial Stakeholder Group (NCSG)</b>	<b>8</b>	<b>7</b>	<b>78.2</b>
Ioana Florina Stupariu	8	7	88.0
Juan Manuel Rojas	8	5	63.0
Krishna Seeburn	2	2	100.0
<b>Grand Total</b>			<b>86.7</b>

### Meeting Activities

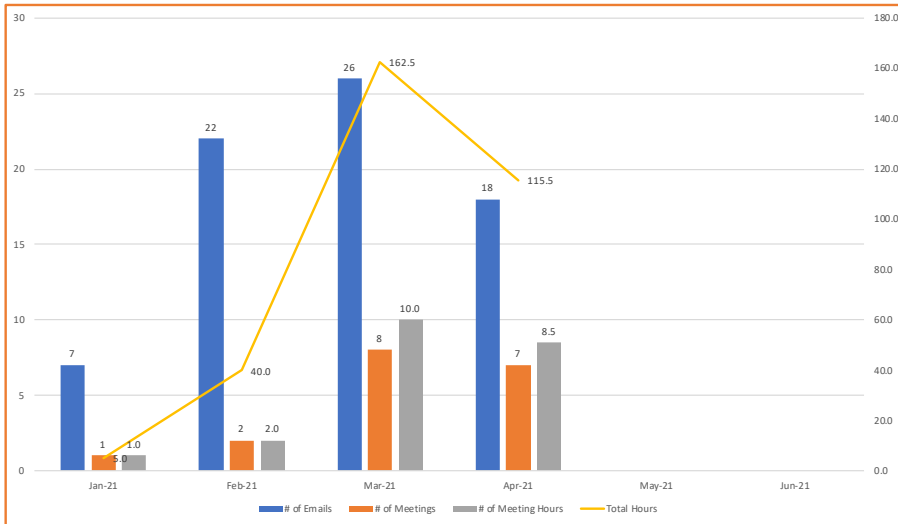


Date	# of Emails	# of Meetings	# of Meeting Hours	Total Hours
Jan-21	7	1	1.0	5.0
Feb-21	22	2	2.0	40.0
Mar-21	26	8	10.0	162.5
Apr-21	18	7	8.5	115.5
May-21				
Jun-21				323.0

### Work Based Metrics

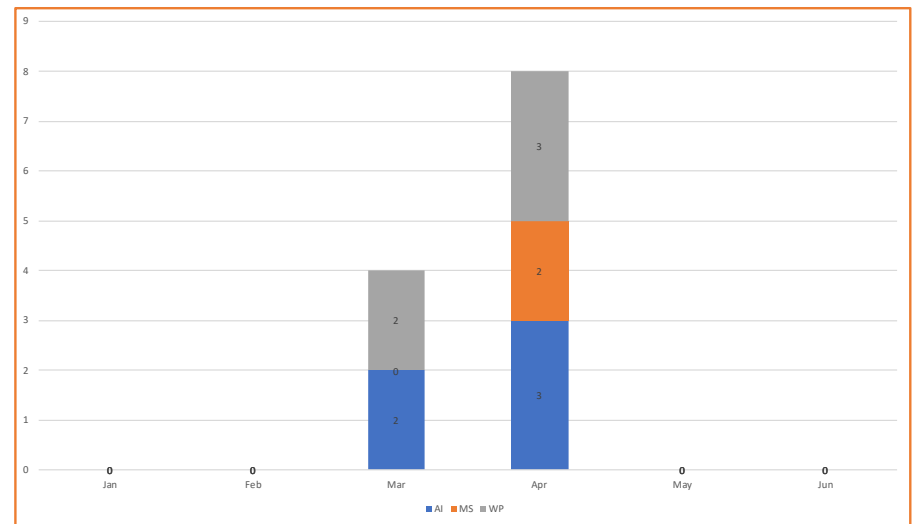

AI = Action Item  
 MS = Milestone  
 WP = Work Plan

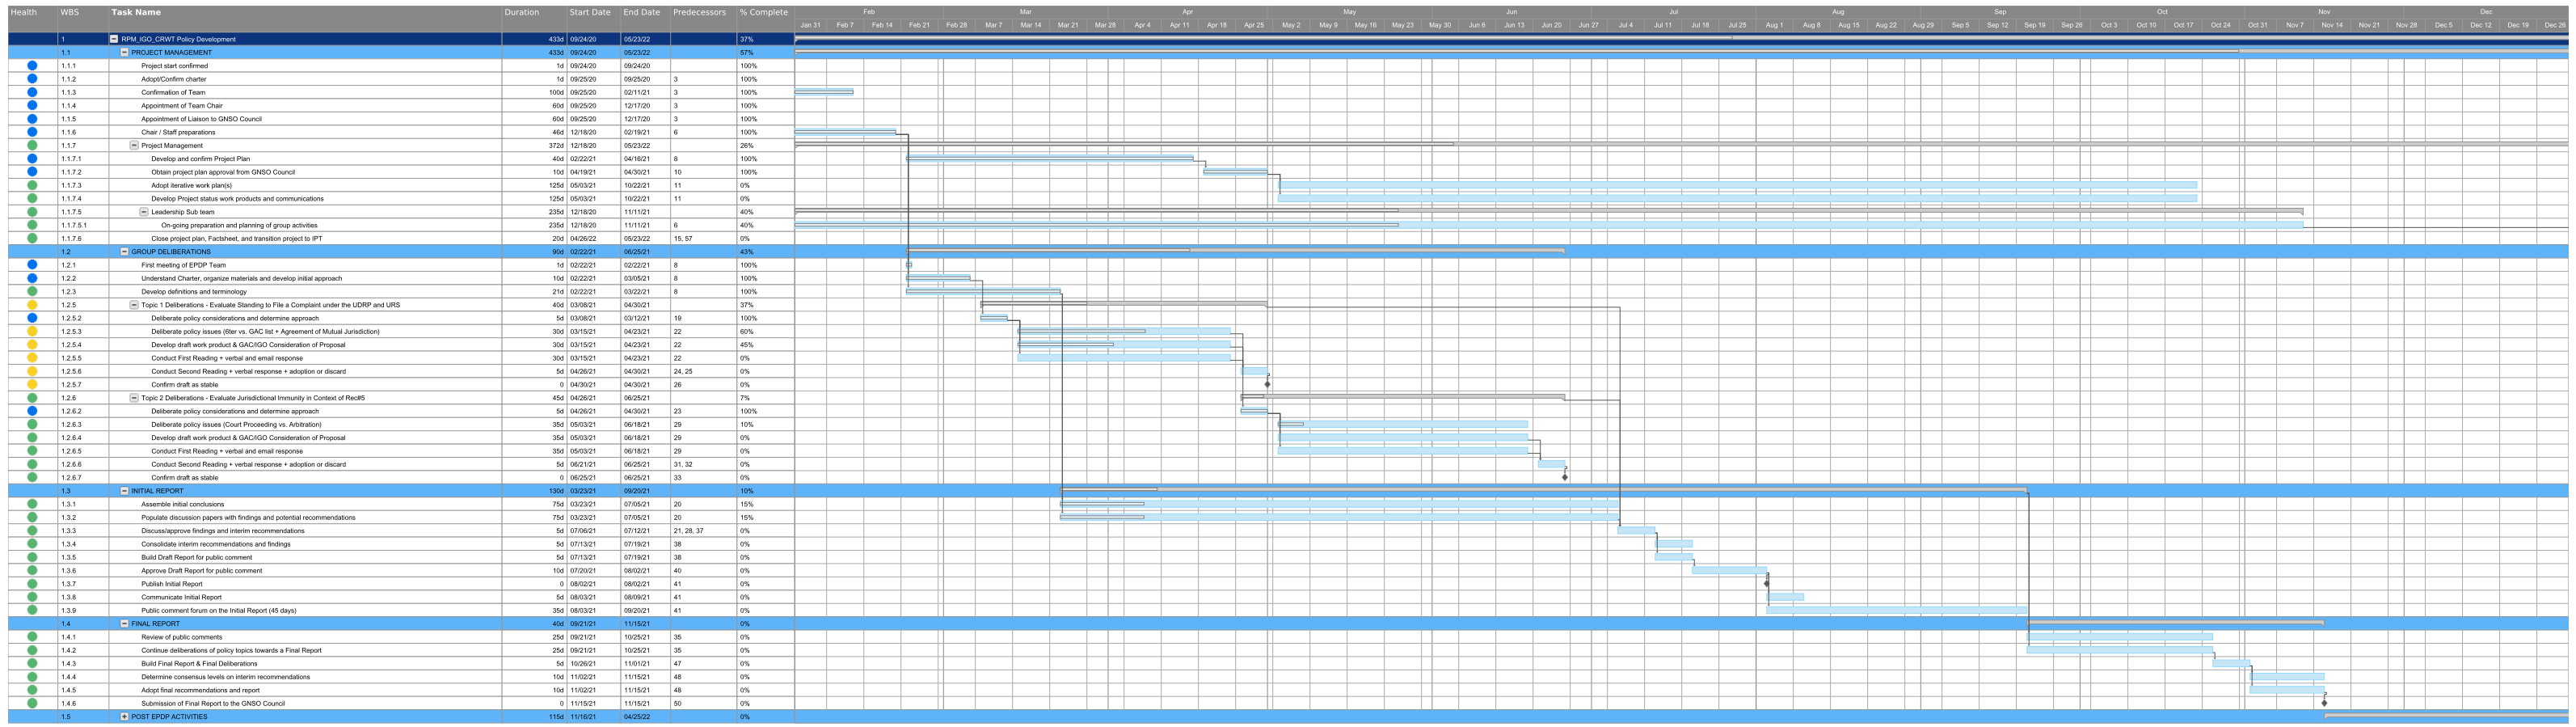

# RPM\_IGO\_CRWT - Action Items Log

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes	Requester	Created
1	AI	Develop General Agreements & Options Document per 8 March meeting	!	Mary Wong	03/11/21	03/11/21	Complete		berry.cobb@icann.org	03/10/21 6:00 PM
2	AI	Review Agreements & Options Document	—	IGO-WT Team	03/15/21	03/15/21	Complete		berry.cobb@icann.org	02/19/21 5:36 PM
3	WP	Meeting #05 - Review of Summary Agreements Doc	↓	IGO-WT Team	03/29/21	03/29/21	Complete		berry.cobb@icann.org	03/16/21 8:51 AM
4	WP	Meeting #06 - Cancelled	↓	IGO-WT Team	04/05/21	03/29/21	Complete		berry.cobb@icann.org	03/16/21 9:02 AM
5	WP	Meeting #07 - Review 4 Components of Solution	↓	IGO-WT Team	04/12/21	04/12/21	Complete		berry.cobb@icann.org	03/16/21 9:02 AM
6	MS	Deliver Project Package to Council	↓	Berry Cobb	04/12/21	04/12/21	Complete		berry.cobb@icann.org	03/16/21 9:02 AM
7	AI	WT to review draft of UDRP Rules/Procedures redline to promote further deliberations of possible options.	—	IGO-WT Team	04/27/21	04/23/21	Complete		berry.cobb@icann.org	04/30/21 1:59 PM
8	WP	Meeting #08 - Review Standing and Arbitration options to UDRP/URS	↓	IGO-WT Team	04/19/21	04/19/21	Complete		berry.cobb@icann.org	03/16/21 9:02 AM
9	MS	Provide update to Council and Work plan	!	John McElwaine	04/22/21	04/22/21	Complete		berry.cobb@icann.org	04/06/21 11:56 AM
10	WP	Meeting #09 - Review Standing and Arbitration options to UDRP/URS	↓	IGO-WT Team	04/26/21	04/26/21	Complete		berry.cobb@icann.org	03/16/21 9:02 AM
11	AI	Staff to develop simple process flow of UDRP	—	Steve Chan	04/27/21	04/27/21	Complete		berry.cobb@icann.org	04/30/21 1:59 PM
12	AI	Paul to develop outline of IGO Requirement to Scope to Progress	—	Paul McGrady	04/28/21	04/30/21	Complete		berry.cobb@icann.org	04/30/21 1:59 PM
13	WP	Meeting #10 - Align IGO Requirements to UDRP Process	↓	IGO-WT Team	05/03/21		In Progress		berry.cobb@icann.org	03/16/21 9:02 AM
14	MS	Deliver Project Package to Council	↓	Berry Cobb	05/06/21		In Progress		berry.cobb@icann.org	03/16/21 9:02 AM
15	WP	Meeting #11 - TBD	↓	IGO-WT Team	05/10/21		In Progress		berry.cobb@icann.org	03/16/21 9:02 AM
16	WP	Meeting #12 - TBD	↓	IGO-WT Team	05/17/21		In Progress		berry.cobb@icann.org	03/16/21 9:02 AM
17	MS	Provide update to Council and Work plan	!	John McElwaine	05/20/21		In Progress		berry.cobb@icann.org	04/30/21 2:00 PM
18	WP	Meeting #13 - TBD	↓	IGO-WT Team	05/24/21				berry.cobb@icann.org	03/16/21 9:02 AM
19	WP	Meeting #14 - TBD	↓	IGO-WT Team	05/31/21				berry.cobb@icann.org	03/16/21 9:02 AM
20	MS	Deliver Project Package to Council	↓	Berry Cobb	06/03/21				berry.cobb@icann.org	03/16/21 9:02 AM
21	WP	Meeting #15 - TBD	↓	IGO-WT Team	06/07/21				berry.cobb@icann.org	03/16/21 9:02 AM
22	WP	Meeting #16 - TBD	↓	IGO-WT Team	06/14/21				berry.cobb@icann.org	03/16/21 9:02 AM
23	WP	Meeting #17 - TBD	↓	IGO-WT Team	06/21/21				berry.cobb@icann.org	03/16/21 9:02 AM
24	WP	Meeting #18 - TBD	↓	IGO-WT Team	06/28/21				berry.cobb@icann.org	03/16/21 9:02 AM
25	MS	Deliver Project Package to Council	↓	Berry Cobb	07/01/21				berry.cobb@icann.org	03/16/21 9:02 AM
26	MS	Submit Initial Report for Public Comment	!	IGO-WT Team	07/01/21				berry.cobb@icann.org	03/16/21 9:26 AM
