

Project Tracking & Rollup DASHBOARD


Project Name EPDP: Internationalized Domain Names **Program** IDNs **Project Sponsor** GNSO Council

Project Information

05/20/21
Current Start

08/18/23
Current Finish

43%
% Complete

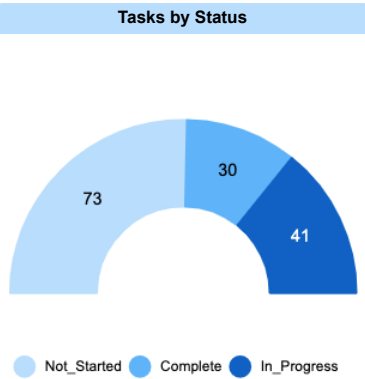

Project Contacts


Donna Austin
Chair

Justine Chew
Vice_Chair

Farell Folly
Liaison

Ariel Liang
Staff_Lead

Steve Chan
Project_Manager



Project Status & Health


Project_Status	Project_Health
On-Schedule	On-Target

Summary Gantt & Key Milestones


Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023								
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
	EPDP: Internationalized Domain Names	05/20/21	08/18/23	43%	In Progress	[Gantt bar]										
	PROJECT CONTROL	05/20/21	07/10/23	63%	In Progress	[Gantt bar]										
	GROUP DELIBERATIONS	08/11/21	03/16/23	48%	In Progress	[Gantt bar]										
●	Group 1	08/25/21	02/17/22	87%	In Progress	[Gantt bar]										
●	Group 2	02/04/22	03/31/22	65%	In Progress	[Gantt bar]										
●	Group 3	03/18/22	06/02/22	33%	In Progress	[Gantt bar]										
●	Group 4	05/20/22	08/04/22			[Gantt bar]										
●	Group 5	07/22/22	09/16/22			[Gantt bar]										
●	Group 6	09/05/22	10/24/22			[Gantt bar]										
●	Group 7	10/11/22	11/11/22			[Gantt bar]										
	INITIAL REPORT	09/20/21	02/03/23	24%	In Progress	[Gantt bar]										
	Publish Initial Report	12/16/22	12/16/22			[Milestone]										
	Public comment forum on the Initial Report (40 days)	12/19/22	02/03/23			[Milestone]										
	FINAL REPORT	02/06/23	04/07/23		Not Started	[Gantt bar]										
	Review of public comments	02/06/23	03/17/23			[Milestone]										
	Submission of Final Report to the GNSO Council	04/07/23	04/07/23			[Milestone]										

Project Tracking & Rollup DASHBOARD


Work-Plan Activity Metrics

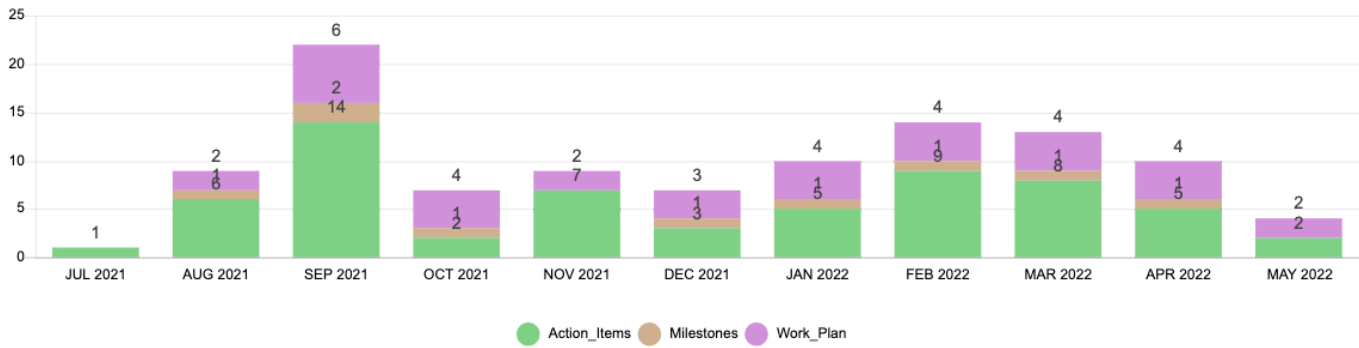

Mailman Activity



Meeting Activity

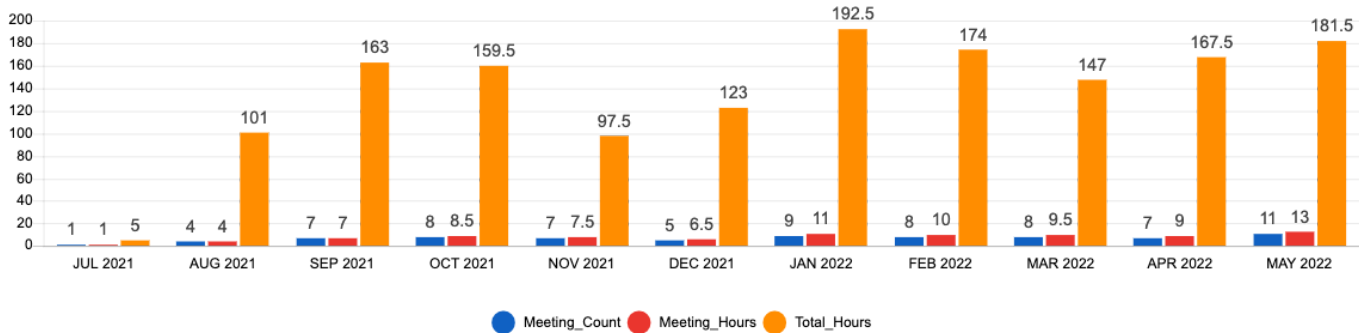

Plenary Attendance

Group Represented	Invited Qty	Attended Qty	Attendance
Total	Sum 1128	Sum 723	Avg 64.1%
Primary At-Large Advisory Committee (ALAC)	Sum 204	Sum 169	Avg 82.8%
Attendee Name Abdulkarim Oloyede	Sum 36	Sum 32	Avg 88.9%
Attendee Name Hadia Elminiawi	Sum 36	Sum 35	Avg 97.2%
Attendee Name Justine Chew	Sum 36	Sum 36	Avg 100.0%
Attendee Name Lianna Galstyan	Sum 36	Sum 26	Avg 72.2%
Attendee Name Satish Babu	Sum 36	Sum 34	Avg 94.4%
Attendee Name TV Gopal	Sum 24	Sum 6	Avg 25.0%
Primary Commercial Business Users Constituency (BC)	Sum 34	Sum 2	Avg 5.9%
Attendee Name Mark William Datysgeld	Sum 34	Sum 2	Avg 5.9%

Primary	Expedited Policy Development Process - IDNs	Sum	36	Sum	33	Avg	91.7%
Attendee Name	Donna Austin	Sum	36	Sum	33	Avg	91.7%
Primary	GNSO Council	Sum	36	Sum	27	Avg	75.0%
Attendee Name	Ekue Farell Folly	Sum	36	Sum	27	Avg	75.0%
Primary	Governmental Advisory Committee (GAC)	Sum	107	Sum	71	Avg	66.4%
Attendee Name	Hamza Onoruoiza Salami	Sum	35	Sum	27	Avg	77.1%
Attendee Name	Nigel Hickson	Sum	36	Sum	25	Avg	69.4%
Attendee Name	T. Santhosh	Sum	36	Sum	19	Avg	52.8%
Primary	ICANN Board	Sum	58	Sum	56	Avg	96.6%
Attendee Name	Akinori Maemura	Sum	22	Sum	21	Avg	95.5%
Attendee Name	Edmon Chung	Sum	36	Sum	35	Avg	97.2%
Primary	Independent	Sum	213	Sum	81	Avg	38.0%
Attendee Name	Abdalmonem Galila	Sum	35	Sum	2	Avg	5.7%
Attendee Name	ANIL JAIN	Sum	36	Sum	29	Avg	80.6%
Attendee Name	Gao Lei	Sum	34	Sum	1	Avg	2.9%
Attendee Name	Imran Hossen	Sum	4	Sum	1	Avg	25.0%
Attendee Name	Kenny Huang	Sum	1	Sum	1	Avg	100.0%
Attendee Name	Lisa Liang	Sum	36	Sum	35	Avg	97.2%
Attendee Name	Nabil Benamar	Sum	34	Sum	0	Avg	0.0%
Attendee Name	Quoc Pham	Sum	33	Sum	12	Avg	36.4%
Primary	Intellectual Property Constituency (IPC)	Sum	49	Sum	36	Avg	73.5%
Attendee Name	Brian King	Sum	13	Sum	10	Avg	76.9%
Attendee Name	Jeffrey Neuman	Sum	36	Sum	26	Avg	72.2%
Primary	Internet Service Providers and Connectivity Providers Constituency (ISPCP)	Sum	35	Sum	10	Avg	28.6%
Attendee Name	Christian Dawson	Sum	35	Sum	10	Avg	28.6%
Primary	Non-Commercial Stakeholder Group (NCSG)	Sum	72	Sum	17	Avg	23.6%
Attendee Name	Akinremi Peter Taiwo	Sum	36	Sum	8	Avg	22.2%
Attendee Name	Tomslin Samme-Nlar	Sum	36	Sum	9	Avg	25.0%
Primary	Registrar Stakeholder Group (RrSG)	Sum	65	Sum	56	Avg	86.2%
Attendee Name	Duwei Chen	Sum	16	Sum	11	Avg	68.8%
Attendee Name	Michael Bauland	Sum	36	Sum	32	Avg	88.9%
Attendee Name	Zhang Zuan	Sum	13	Sum	13	Avg	100.0%
Primary	Registry Stakeholder Group (RySG)	Sum	214	Sum	160	Avg	74.8%
Attendee Name	Dennis Tan Tanaka	Sum	36	Sum	34	Avg	94.4%
Attendee Name	Jennifer Chung	Sum	35	Sum	28	Avg	80.0%
Attendee Name	Jerry Sen	Sum	36	Sum	36	Avg	100.0%
Attendee Name	Joseph Chiu-Kit Yee	Sum	36	Sum	32	Avg	88.9%

Attendee Name Maxim Alzoba	Sum 36	Sum 27	Avg 75.0%
Attendee Name Wei (Wesley) Wang	Sum 35	Sum 3	Avg 8.6%
Primary Security and Stability Advisory Committee (SSAC)	Sum 5	Sum 5	Avg 100.0%
Attendee Name Jiankang Yao	Sum 1	Sum 1	Avg 100.0%
Attendee Name John R. Levine	Sum 1	Sum 1	Avg 100.0%
Attendee Name Lyman Chapin	Sum 1	Sum 1	Avg 100.0%
Attendee Name Patrik Fältström	Sum 1	Sum 1	Avg 100.0%
Attendee Name Ram Mohan	Sum 1	Sum 1	Avg 100.0%

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #33 E3, E1 (Part 1), E3a, E5	↓	EPDP_IDN	04/28/22	04/14/22	Complete	
	AI	Action Item 1: Staff to proceed with next steps on distributing questions to ROs that have new gTLDs in Chinese and Arabic scripts.	—	Policy Support Staff	05/12/22	06/03/22	Complete	
	AI	Action Item 2: Staff to request volunteers to join a small group tasked with developing examples related to Levels 1, 2, and 3. Staff to circulate a doodle to find a time for the small group to meet.	—	Policy Support Staff	05/06/22	05/06/22	Complete	
	WP	Meeting #34 E5, E2, E1 (Part 2), E4	↓	EPDP_IDN	05/05/22	05/05/22	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	05/06/22	05/06/22	Complete	
	WP	Meeting #35 E2, D2	↓	EPDP_IDN	05/12/22	05/12/22	Complete	
	AI	Examine what happens for intentional and planned retirement under EBERO, as opposed to emergency action.	—	Ariel Liang	05/12/22	05/19/22	Complete	
	WP	Meeting #36 D2, D3	↓	EPDP_IDN	05/19/22	05/19/22	Complete	
	AI	Leadership and staff to develop a proposal to scope further outreach to the three GPs with respect to additional work.	—	EPDP_IDN Leadership	06/13/22		In Progress	
	WP	Meeting #37 E5, E7	↓	EPDP_IDN	05/26/22	05/26/22	Complete	
	AI	Update process flow chart to include additional elements like 1) the new processes envisioned by SubPro 2) additional inputs to the New gTLD Program process (e.g., application comment, GAC EW, etc.) 3. numbering for boxes 4. upcoming charter questions to be discussed and 5. references to preliminary recommendations.	—	Policy Support Staff	07/28/22		In Progress	
	WP	Meeting #38 E7 (Parking Lot)	↓	EPDP_IDN	06/02/22	06/02/22	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	06/07/22		In Progress	
	WP	Meeting #39 TBD	↓	EPDP_IDN	06/09/22		Not Started	
	WP	Meeting ICANN74 TBD	↓	EPDP_IDN	06/14/22		Not Started	
	WP	Meeting #40 TBD	↓	EPDP_IDN	06/16/22		Not Started	
	MS	Submit project package to GNSO Council	!	Ariel Liang	07/08/22		Not Started	
	MS	Submit Initial Report for Public Comment	!	EPDP_IDN	12/19/22		Not Started	
