Project Tracking & Rollup DASHBOARD

ICANN GNSO Generic Names Supporting Organization

Project Name Program **Project Sponsor EPDP: Internationalized Domain Names GNSO** Council gTLD **Project Information** Tasks by Status **Project Contacts Participant Summary** Donna Austin 05/20/21 Chair 20 Current Start **Justine Chew** 61 08/18/23 Vice_Chair 6 98 **Farell Folly** 11 **Current Finish** 23 5 Liaison 29% Ariel Liang Ó 20 40 60 80 22 % Complete Staff_Lead Member 🛑 Participant_Count SC Steve Chan **Project Status & Health** Observer_Email_Only Staff_Assigned Project_Manager Project_Status Project_Health Not_Started Complete In_Progress Staff_Not_Assigned **On-Schedule On-Target**

			Su	mmary Gant	t & Key Mile	tones
Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021 2022 2023 Q1 Q2 Q3 Q4 Q1 <t< th=""></t<>
	EPDP: Internationalized Domain Names	05/20/21	08/18/23	29%	In Progress	EPDP: Internationalized Domain Names
	PROJECT CONTROL	05/20/21	07/10/23	48%	In Progress	PROJECT CONTROL
	GROUP DELIBERATIONS	08/11/21	03/16/23	26%	In Progress	GROUP DELIBERATIONS
٠	Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR	08/25/21	11/02/21	67%	In Progress	Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR
•	Topic B Deliberations: "Same entity" at the top-level	11/03/21	12/28/21			Topic B Deliberations: "Same entity" at the top-level
٠	Topic C Deliberations: "Same entity" at the second-level	12/29/21	02/22/22			Topic C Deliberations: "Same entity" at the second-level
	Topic D Deliberations: Adjustments in registry agreement, registry service, registry transition process, and other processes/procedures related to the domain name lifecycle	02/23/22	05/24/22			Topic D Deliberations: Adjustments in registry agreement, registry service, registry tra
	Topic E Deliberations: Adjustments to objection process, string similarity review, string contention resolution, reserved strings, and other policies and procedures	05/25/22	08/02/22			Topic E Deliberations: Adjustments to objection process, string similarity review, s
	Topic F Deliberations: Adjustments in registration dispute resolution procedures and trademark protection mechanisms	08/03/22	09/27/22			Topic F Deliberations: Adjustments in registration dispute resolution procedure
	Topic G Deliberations: Process to update the IDN Implementation Guidelines	09/28/22	11/04/22			Topic G Deliberations: Process to update the IDN Implementation Guideline
	INITIAL REPORT	09/20/21	02/03/23	16%	In Progress	INITIAL REPORT
	Publish Initial Report	12/16/22	12/16/22			Publish Initial Report
	FINAL REPORT	02/06/23	04/07/23		Not Started	FINAL REPORT
	Review of public comments	02/06/23	03/17/23			Review of public comments
	Submission of Final Report to the GNSO Council	04/07/23	04/07/23			Submission of Final Report to the GNSO Council

<u>Return to</u>	Project	Summary

4 - Working Group											
Title:	EPDP - Internationalized Domain Names (EPDP_IDN)										
Description & Scope:	e definition of gillus and the management of variant labels; and Z) now the IUN implementation Guidelines. Which Contracted Parties are										

Composition:	
Chair:	Donna Austin
Vice Chair:	Justine Chew
Council Liaison:	Farell Folly
Staff:	A. Liang, S. Chan, E. Barabas.
# Participants:	81 Participants (<u>link</u>)
# Observers:	9
Tools:	Mailing List / Meeting Schedule / Wiki
Charter:	<u>Charter</u>

Project Management:												
Token Holder	Planned Start Date	Actual Start Date	# of Days	Planned End Date	Actual End Date							
WG	20 May 2021	20 May 2021	273	09 Jun 2023	TBD							
Prog	ram	Progress		Status	Health							
gTl	D	29%										
STATUS: Planne	ed On-schedule	Revised schedule	At-Risk	hedule Target wil	I be missed Non-hold							

Milestones/Work plan (link):

Milestone/Task	Date		• This project was initiated on 20 May 2021 and continues with a <u>Status</u> of
Project Start	May-21	\checkmark	"On-Schedule" and <u>Health</u> of "On-Target".
Scoping Team Report	Jan-20	\checkmark	
Charter Approved	May-21	\checkmark	Current Activities:
EPDP Initiation Request Approved	May-21	\checkmark	 Complete the first pass of substantive deliberations on Topic A and review draft outcome language.
1st Plenary meeting	Aug-21	\checkmark	Update project plan to reflect the changed <u>sequencing</u> for tackling charter questions
SO/AC & SG/C Input to PDP	Nov-21	\checkmark	 Start deliberations on charter questions in Bundle 2: B1, B2, B3, D1, D1a, D1b, B4, B4, B5.
Project Plan and Work plan Adoption	Oct-21	\checkmark	
Issue Deliberations	Mar-23		Planned Activities:
Populate draft report w/ findings & potential recs.	Oct-22		Initiate deliberations on charter questions in Bundle 3: E1-E5, E7.
Assemble initial conclusions	Oct-22		Open Issues, Risks & Mitigation Plan:
Discuss/approve findings and interim recs.	Nov-22		Leadership proposed change to sequencing of tackling charter questions to ensure
Consolidate interim recommendations and findings	Nov-22		that a logical order is being followed and provide efficiencies to deliberations.
Issue report for public comment	Dec-22		Leadership also intends to revisit the project plan to assess whether the original
Review public comment input & prepare final report	Mar-23		planning assumptions were reasonable. Council will be informed if any changes are considered necessary.
Finalize Report	Apr-23		 At the time the Charter was developed, it was assumed that the SubPro
Determine consensus levels on recommendations	Apr-23		 At the time the Charter was developed, it was assumed that the sub-ro recommendations, particularly those relating to IDNs under Topic 25, would have
Adopt final recommendations and report	Apr-23		been approved by the ICANN Board. The IDN EPDP is conducting its work with the
Send final report to GNSO Council	Apr-23		expectation that the SubPro recommendations will be approved by the Board at son
GNSO Council adoption of consensus recs.	May-23		future date. However, it has been necessary for the EPDP Team to make assumption about the implementation of those recommendations in order to address the Charte
Issue public comment for Board consideration	Jun-23		questions. While these assumptions are believed to be sound, the Council should be
ICANN Board adoption of consensus recs.	Oct-23		aware of the possible ripple effect or potential risk to the EPDP Teamwork in the even that the Board does not adopt the related SubPro recommendations.
Prior period % Complete	28%		Completed in prior period(s):
			 Largely completed the first pass of deliberations on Topic A charter questions, with draft outcome language developed for seven out of ten questions. Conducted an engagement session with SSAC members to discuss their early input and ask SSAC members specific questions about Charter questions. Reviewed the proposed change to sequencing of tackling charter questions. Completed and distributed <u>Project Package</u> for January.

Status/Health Rationale:

[Return to Project Summary]

Project Tracking & Rollup



ticipant	Participant Type	Role	Participation Start Date	Participation End Date	Legacy SOI Link
Group Selected / Nominated By: Group Name At-Large Advisory Committee (ALAC)					
TV Gopal	Participant		05/25/21		https://community.ican
Hadia Elminiawi	Participant		07/14/21		https://community.ican
Satish Babu	Member		05/25/21		https://community.ican
Lianna Galstyan	Member		05/25/21		https://community.ican
Abdulkarim Oloyede	Member		05/25/21		https://community.ican
	Member	Vice choir			
Justine Chew Group Selected / Nominated By: Group Name Constitution Selected / Nominated By: Group Name Constitution Selected (Nominated By: Group Name Constitution Selected	Wember	Vice-chair	05/25/21		https://community.icar
Commercial Business Users Constituency (BC)					
Mark William Datysgeld Group Selected / Nominated By: Group Name	Member		05/25/21		https://community.icar
Expedited Policy Development Process - IDNs			00/10/01		
Donna Austin	Member	Chair	08/10/21		https://community.icar
Group Selected / Nominated By: Group Name GNSO Council					
Ekue Farell Folly	Member	Liaison	07/27/21		https://community.ica
Group Selected / Nominated By: Group Name Governmental Advisory Committee (GAC)					
Hamza Onoruoiza Salami	Participant		05/25/21		https://community.ica
T. Santhosh	Member		05/25/21		https://community.ica
Nigel Hickson	Member		07/12/21		https://community.ica
Group Selected / Nominated By: Group Name	1				
Edmon Chung	Member	Liaison	07/27/21		https://community.ica
Akinori Maemura	Member	Liaison	11/18/21	_	https://community.ica
Group Selected / Nominated By: Group Name Independent					
Abdalmonem Galila	Participant		05/25/21		https://community.ica
Gao Lei	Participant		05/25/21	_	https://community.ica
Nabil Benamar	Participant		05/25/21		https://community.ica
Lisa Liang	Participant		05/25/21		https://community.ica
Anil Jain	Participant		07/30/21		https://community.ica
					,
Quoc Pham	Participant		08/13/21	10/00/04	https://community.ica
Kenny Huang Group Selected / Nominated By: Group Name	Guest		10/26/21	10/26/21	
Intellectual Property Constituency (IPC)					
Brian King	Member		05/25/21	11/08/21	https://community.ica
Jeffrey Neuman Group Selected / Nominated By: Group Name Internet Corporation for Assigned Names & Numbers (ICANN)	Member		05/25/21		https://community.ica
Michael Karakash	Staff - Assigned	Liaison	05/25/21		
Michael Karakash Steve Chan	Staff - Assigned	Liaison	05/25/21		
Michael Karakash Steve Chan Emily Barabas	Staff - Assigned Staff - Assigned	Liaison	05/25/21 05/25/21		
Michael Karakash Steve Chan	Staff - Assigned	Liaison	05/25/21		
Michael Karakash Steve Chan Emily Barabas	Staff - Assigned Staff - Assigned	Liaison	05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew	Staff - Assigned Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain	Staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine	Staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana	Staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang	Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland	Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name	Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name	Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21		https://community.ica
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency Christian Dawson Group Selected / Nominated By: Group Name	Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21 12/02/21		https://community.ica
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency Christian Dawson Group Selected / Nominated By: Group Name	Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21 12/02/21		
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency Christian Dawson Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG) Tomslin Samme-Nlar Akinremi Peter Taiwo	Staff - Assigned Staff - Assigned		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21 12/02/21		https://community.ica
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency Christian Dawson Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG) Tomslin Samme-Nlar Akinremi Peter Taiwo Group Selected / Nominated By: Group Name	Staff - Assigned Staff - Assigned The staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned Member		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21 12/02/21		https://community.ica
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency Christian Dawson Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG)	Staff - Assigned Staff - Assigned The staff - Assigned Staff - Assigned Staff - Assigned Staff - Assigned Member		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21 12/02/21		https://community.icar https://community.icar
Michael Karakash Steve Chan Emily Barabas Terri Agnew Sarmad Hussain Nathalie Peregrine Pitinan Kooarmornpatana Ariel Liang Julie Bisland Michelle DeSmyter Devan Reed Group Selected / Nominated By: Group Name Internet Service Providers and Connectivity Providers Constituency Christian Dawson Group Selected / Nominated By: Group Name Non-Commercial Stakeholder Group (NCSG) Tomslin Samme-Nlar Akinremi Peter Taiwo Group Selected / Nominated By: Group Name Registrar Stakeholder Group (RrSG)	Staff - Assigned Staff - Assigned Participant		05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 05/25/21 08/18/21 12/02/21 07/12/21		https://community.icar https://community.icar https://community.icar https://community.icar


Jerry Sen	Participant	05/25/21	https://community.icann.or
Wei (Wesley) Wang	Participant	07/13/21	https://community.icann.or
Maxim Alzoba	Member	05/25/21	https://community.icann.or
Joseph Chiu-Kit Yee	Member	07/06/21	https://community.icann.or
Dennis Tan Tanaka	Member	05/25/21	https://community.icann.or
Group Selected / Nominated By: Group Name			

Security and Stability Advisory Committee (SSAC)

Project Tracking & Rollup DASHBOARD


ICANN GNSO

Work-Plan Activity Metrics



Action_Items Milestones Work_Plan





Meeting Activity






	Plenary Attendance			
Group Represented	Invited Qty		Attended Qty	Attendance
Total		Sum 656	Sum 447	
Primary At-Large Advisory Committee (ALAC)		Sum 124	Sum 100	
Attendee Name Abdulkarim Oloyede		Sum 21	Sum 18	
Attendee Name Hadia Elminiawi		Sum 21	Sum 20	Av 95.29
Attendee Name Justine Chew		Sum 21	Sum 21	100.09
Attendee Name Lianna Galstyan		Sum 21	Sum 16	
Attendee Name Satish Babu		Sum 21	Sum 19	90.5%
Attendee Name TV Gopal		Sum 19	Sum 6	
Primary Commercial Business Users Constituency (BC)		Sum 21	Sum 2	
Attendee Name Mark William Datysgeld		Sum 21	Sum 2	
Drimon		Ciim	Cim	٨٠

Expedited Policy Development Process - IDNs	21	20	95.2%
Attendee Name	Sum	Sum	^{Avg}
Donna Austin	21	20	95.2%
Primary	Sum	Sum	^{Avg}
GNSO Council	21	17	81.0%
Attendee Name	Sum	Sum	^{Avg}
Ekue Farell Folly	21	17	81.0%
Primary	Sum	Sum	^{Avg}
Governmental Advisory Committee (GAC)	62	44	71.0%
Attendee Name	Sum	Sum	Avg
Hamza Onoruoiza Salami	20	14	70.0%
Attendee Name	Sum	Sum	^{Avg}
Nigel Hickson	21	15	71.4%
Attendee Name	Sum	Sum	^{Avg}
T. Santhosh	21	15	71.4%
Primary	Sum	Sum	^{Avg}
ICANN Board	28	27	96.4%
Attendee Name	Sum	Sum	Avg
Akinori Maemura	7	7	100.0%
Attendee Name	Sum	Sum	^{Avg}
Edmon Chung	21	20	95.2%
Primary	Sum	Sum	45.4%
Independent	119	54	
Attendee Name	Sum	Sum	^{Avg}
Abdalmonem Galila	20	2	10.0%
Attendee Name ANIL JAIN	Sum	Sum	^{Avg}
	21	18	85.7%
Attendee Name	Sum	Sum	Avg
Gao Lei	19	1	5.3%
Attendee Name	Sum	Sum	Avg
Kenny Huang	1	1	100.0%
Attendee Name	Sum	Sum	Avg
Lisa Liang	21	20	95.2%
Attendee Name	Sum	Sum	Avg
Nabil Benamar	19	O	0.0%
Attendee Name	Sum	Sum	66.7%
Quoc Pham	18	12	
Primary	Sum	Sum 27	Avg
Intellectual Property Constituency (IPC)	34		79.4%
Attendee Name	Sum	Sum	76.9%
Brian King	13	10	
Attendee Name	Sum	Sum	81.0%
Jeffrey Neuman	21	17	
Primary	Sum	Sum	45.0%
Internet Service Providers and Connectivity Providers Constituency (ISPCP)	20	9	
Attendee Name	Sum	Sum	45.0%
Christian Dawson	20	9	
Primary	Sum	Sum	^{Avg}
Non-Commercial Stakeholder Group (NCSG)	42	15	35.7%
Attendee Name	Sum	Sum	^{Avg}
Akinremi Peter Taiwo	21	7	33.3%
Attendee Name	Sum	Sum	Avg
Tomslin Samme-Nlar	21	8	38.1%
Primary	Sum	Sum	Avg
Registrar Stakeholder Group (RrSG)	35	30	85.7%
Attendee Name	Sum	Sum	^{Avg}
Duowei Chen	14	11	78.6%
Attendee Name	Sum	Sum	Avg
Michael Bauland	21	19	90.5%
Primary	Sum	Sum	^{Avg}
Registry Stakeholder Group (RySG)	124	97	78.2%
Attendee Name	Sum	Sum	^{Avg}
Dennis Tan Tanaka	21	20	95.2%
Attendee Name	Sum	Sum	Avg
Jennifer Chung	20	17	85.0%
Attendee Name	Sum	Sum	Avg
Jerry Sen	21	21	100.0%
Attendee Name	Sum	Sum	Avg
Los op be Chiu Kit Xoo	21	20	95.2%
Joseph Chiu-Kit Yee Attendee Name	21	Sum	95.2% 76.2%
Maxim Alzoba	21	16	76.2%

Primary	Sum	Sum	Avg
Security and Stability Advisory Committee (SSAC)	5	5	100.0%
Attendee Name	Sum	Sum	100.0%
Jiankang Yao	1	1	

Health	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	Baseline Start	Baseline Finish	Q1 Jan Feb M	ar Anr	Q2 May	lun .lul	Q3	ien Oct	Q4	Q1 Feb Mar
1	EPDP: Internationalized Domain Names	587d	05/20/21	08/18/23		29%	In Progress	05/20/21	08/18/23		ai npi		our ou	, tag	.op 000	1101 200	
2	- PROJECT CONTROL		05/20/21	07/10/23		48%	In Progress	05/20/21	07/10/23								
3	Project start confirmed		05/20/21	05/20/21		100%	Complete	05/20/21	05/20/21	\		•					
4	Adopt/Confirm charter	0	05/20/21	05/20/21	3	100%	Complete	05/20/21	05/20/21								
5	Confirmation of Team		05/20/21	08/11/21	3	100%	Complete	05/20/21	08/11/21								
6	Appointment of Team Chair	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21								
7	Appointment of Liaison to GNSO Council	46d	05/20/21	07/22/21	3	100%	Complete	05/20/21	07/22/21								
8	Chair / Staff preparations	13d	07/23/21	08/10/21	6	100%	Complete	07/23/21	08/10/21				ġ	<u> </u>			
9	Project Management	512d	07/23/21	07/10/23		31%	In Progress	07/23/21	07/10/23				F				 <u> </u>
10	Develop and confirm Project Plan	50d	07/23/21	09/30/21	6	100%	Complete	07/23/21	09/30/21				i i				
11	Obtain project plan approval from GNSO Council	20d	10/01/21	10/28/21	10	100%	Complete	10/01/21	10/28/21								
12	Develop monthly Project Packages and deliver to Group & Council	370d	10/29/21	03/30/23	11	18%	In Progress	10/29/21	03/30/23							1	
13	Leadership Sub team	440d	07/23/21	03/30/23		31%	In Progress	07/23/21	03/30/23				F		_		
14	On-going preparation and planning of group activities	440d	07/23/21	03/30/23	6	31%	In Progress	07/23/21	03/30/23								
15	Close project and transition project to implementation	-	07/10/23	07/10/23	14, 165	0%		07/10/23	07/10/23								
16	- GROUP DELIBERATIONS		08/11/21	03/16/23		26%	In Progress	08/11/21	03/16/23								
17	First meeting of Team	1d	08/11/21	08/11/21	8	100%	Complete	08/11/21	08/11/21					6			
18	Understand Charter, organize materials and develop initial approach	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21								
19	Overview & initial discussion of all Policy Topics	10d	08/11/21	08/24/21	8	100%	Complete	08/11/21	08/24/21								
20	Develop definitions and terminology	28d	08/11/21	09/17/21	8	100%	Complete	08/11/21	09/17/21						2		
21	Input from other SO/ACs & GNSO SG/Cs	58d	09/09/21	11/29/21		100%	Complete	09/09/21	12/01/21					F			
26	Topic A Deliberations: Consistent definition and technical utilization of RZ-LGR	50d	08/25/21	11/02/21		67%	In Progress	08/25/21	11/02/21								
44	Topic B Deliberations: "Same entity" at the top-level	40d	11/03/21	12/28/21				11/03/21	12/28/21								
57	Topic C Deliberations: "Same entity" at the second-level	40d	12/29/21	02/22/22				12/29/21	02/22/22								
71	Topic D Deliberations: Adjustments in registry agreement, registry service, registry transition process, and other processes/procedures related to the domain name lifecycle	65d	02/23/22	05/24/22				02/23/22	05/24/22								
87	Topic E Deliberations: Adjustments to objection process, string similarity review, string contention resolution, reserved strings, and other policies and procedures	50d	05/25/22	08/02/22				05/25/22	08/02/22								
02	Topic F Deliberations: Adjustments in registration dispute resolution procedures and trademark protection mechanisms	40d	08/03/22	09/27/22				08/03/22	09/27/22								
12	Topic G Deliberations: Process to update the IDN Implementation Guidelines	28d	09/28/22	11/04/22				09/28/22	11/04/22								
21	Unplanned Issues & Tasks	0	08/24/21	08/24/21				08/24/21	08/24/21	\$							
38		364d	10/25/21	03/16/23		17%	In Progress	10/25/21	03/16/23						6	1	
45	- INITIAL REPORT	360d	09/20/21	02/03/23		16%	In Progress	09/20/21	02/03/23								
46	Populate stable drafts as required	300d	09/20/21	11/11/22	20	20%	In Progress	09/20/21	11/11/22								
47	Discuss/approve findings and interim recommendations	10d	11/14/22	11/25/22	146			11/14/22	11/25/22								
48	Consolidate interim recommendations and findings	10d	11/28/22	12/09/22	147			11/28/22	12/09/22								
49	Build Draft Report for public comment	10d	11/28/22	12/09/22	147			11/28/22	12/09/22								
50	Approve Draft Report for public comment	5d	12/12/22	12/16/22	149			12/12/22	12/16/22								
151	Publish Initial Report	0	12/16/22	12/16/22	150			12/16/22	12/16/22	\$							
52	Communicate Initial Report	5d	12/19/22	12/23/22	150			12/19/22	12/23/22								
53	Public comment forum on the Initial Report (40 days)	35d	12/19/22	02/03/23	150			12/19/22	02/03/23								
154	- FINAL REPORT	45d	02/06/23	04/07/23			Not Started	02/06/23	04/07/23								
55	Review of public comments	30d	02/06/23	03/17/23	153			02/06/23	03/17/23								
156	Continue deliberations of policy topics towards a Final Report	30d	02/06/23	03/17/23	153			02/06/23	03/17/23								
157	Build Final Report & Final Deliberations	5d	03/20/23	03/24/23	156			03/20/23	03/24/23								
58	Determine consensus levels on interim recommendations	10d	03/27/23	04/07/23	157			03/27/23	04/07/23								
159	Adopt final recommendations and report	10d	03/27/23	04/07/23	157			03/27/23	04/07/23								
60	Submission of Final Report to the GNSO Council	0	04/07/23	04/07/23	159			04/07/23	04/07/23	\							
61	+ POST GROUP TASKS	95d	04/10/23	08/18/23			Not Started	04/10/23	08/18/23								
66																	
67	PDP CHECKLIST	9 <u>9</u> d	01/01/21	05/20/21							_					· · · ·	

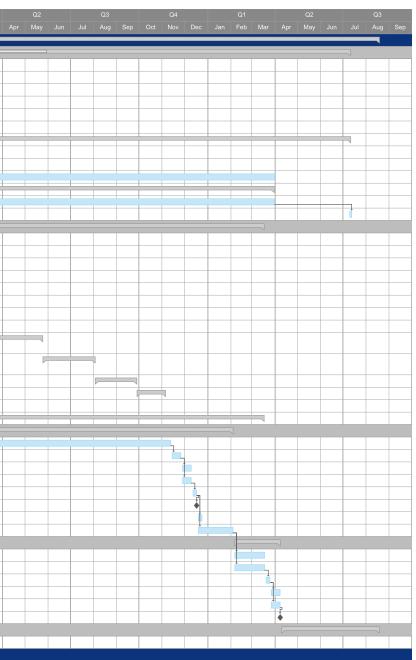

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Note
	WP	Meeting #18 Topic A/Questions A6, A7, A9, A10; SSAC engagement session prep	-	EPDP_IDN	01/06/22	01/06/22	Complete	
	AI	Action Item #1: EPDP Team members to frame specific questions for the SSAC members and share on the mailing list by Monday, 10 January.	-	EPDP_IDN	01/10/22	01/10/22	Complete	
	AI	Action Item #2: EPDP Members to give further thought to the possible paths for addressing charter question A7 and share additional input on the mailing list.	-	EPDP_IDN	01/20/22	01/27/22	Complete	
	MS	Submit project package to GNSO Council	!	Ariel Liang	01/07/22	01/05/22	Complete	
	WP	Meeting #19 SSAC engagement session	-	EPDP_IDN	01/13/22	01/13/22	Complete	
	AI	Action Item #1: EPDP Team members to provide input on draft text in response to charter question A6 and open items.	-	EPDP_IDN	01/20/22	01/20/22	Complete	
	WP	Meeting #20 A5, A6 (time permitting, A7, A9, A10)	-	EPDP_IDN	01/20/22	01/20/22	Complete	
	AI	Action Item #1: Leadership team will update the recommendations based on today's discussion and share with the EPDP Team for review.	-	EPDP_IDN	01/27/22	01/27/22	Complete	
	WP	Meeting #21 Change to Sequencing of Charter Questions; Recap A6, A7, A9 & A10	-	EPDP_IDN	01/27/22	01/27/22	Complete	
	AI	Action Item #1: Staff to send follow up message to the mailing list reminding members to provide any comments. Members to provide any input by 2 February 2022.		EPDP_IDN Policy Support Staff	02/02/22		In Progress	
	AI	Action Item #2: Leadership team to ensure that the recommendations in relation to A6 provide safeguards for the existing contracted parties. Be more explicit by what we mean by grandfathering. In recommendation 1.4, take out "to the extent feasible", include that the RZ-LGR MUST be updated. Add implementation guidance explaining specific expectations regarding the limited circumstances for exceptions to backwards compatibility.		EPDP_IDN Leadership	02/03/22		In Progress	
	AI	Action Item #3: Leadership team to add a recommendation reaffirming the principle of backward compatibility.		EPDP_IDN Leadership	02/03/22		In Progress	
	AI	Action Item #4: Leadership team to update recommendation 1.6 to be more specific in the definition of grandfathering and the circumstances throughout the TLD lifecycle where this applies.		EPDP_IDN Leadership	02/03/22		In Progress	
	AI	Action Item #5: Leadership team to draft implementation guidance in relation to recommendation 1.5 focused on who should provide that information as part of the public comment.		EPDP_IDN Leadership	02/03/22		In Progress	
	WP	Meeting #22 Recap A9 & A10; Start B1 & B2	-	EPDP_IDN	02/03/22		In Progress	
	MS	Submit project package to GNSO Council	1	Ariel Liang	02/04/22		In Progress	
	WP	Meeting #23 TBD	-	EPDP_IDN	02/10/22			
	WP	Meeting #24 TBD	-	EPDP_IDN	02/17/22			
	WP	Meeting #25 TBD	-	EPDP_IDN	02/24/22			
	WP	Meeting #26 TBD	-	EPDP_IDN	03/03/22			
	MS	Submit project package to GNSO Council	!	Ariel Liang	03/04/22			
	WP	Meeting ICANN73 TBD	-	EPDP_IDN	03/08/22			

Notes
