

Project Tracking & Rollup DASHBOARD


Project Name PDP: Transfer Policy Review **Program** Transfers **Project Sponsor** GNSO Council

Project Information

58%
% Complete

02/18/21
Actual Start

06/19/25
Planned Finish

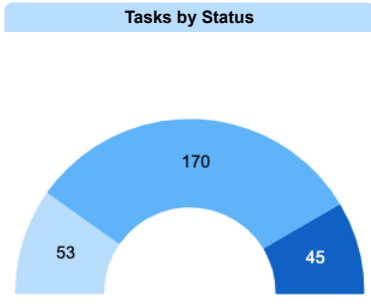

Project Contacts


Roger Carney
Chair

n/a
Vice_Chair

Oswaldo Novoa
Liaison

Caitlin Tubergen
Staff_Lead

Berry Cobb
Project_Manager



Project Status & Health

Project_Status: Revised Schedule
Project_Health: On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	Timeline (2021-2025)																							
						2021 Q1	2021 Q2	2021 Q3	2021 Q4	2022 Q1	2022 Q2	2022 Q3	2022 Q4	2023 Q1	2023 Q2	2023 Q3	2023 Q4	2024 Q1	2024 Q2	2024 Q3	2024 Q4	2025 Q1	2025 Q2	2025 Q3	2025 Q4				
	PDP: Transfer Policy Review	02/18/21	06/19/25	58%	In Progress	[Gantt Bar]																							
	PROJECT CONTROL	02/18/21	06/19/25	68%	In Progress	[Gantt Bar]																							
	GROUP DELIBERATIONS	05/13/21	11/14/24	72%	In Progress	[Gantt Bar]																							
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt Bar]																							
	Group 1B Policy Topics	09/28/23	06/05/24	26%	In Progress	[Gantt Bar]																							
	Group 2 Policy Topics	02/02/23	09/27/23	93%	In Progress	[Gantt Bar]																							
	INITIAL REPORT	06/24/21	11/06/24	63%	In Progress	[Gantt Bar]																							
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt Bar]																							
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	Not Started	Not Started	[Gantt Bar]																							
	FINAL REPORT	08/04/22	02/05/25	22%	In Progress	[Gantt Bar]																							
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt Bar]																							
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	Not Started	Not Started	[Gantt Bar]																							
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25	Not Started	Not Started	[Gantt Bar]																							

Project Description

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Mailing List](#)
[Meeting Schedule](#)
[Wiki](#)
[Charter](#)

Completed in Prior Period

- Completed substantive deliberations on the Transfer Emergency Action Contact (TEAC), reversal of a transfer, the Transfer Dispute Resolution Policy (TDRP), and Wave 1 - Rec #27 items related to TEAC and TDRP.
- Completed and distributed [Project Package](#).

Open Issues & Risks



- None at this time.

Current Activities & Tasks

- Continue deliberations on ICANN-Approved Transfers.

Planned Activities & Tasks

- Conduct a “where we’re at” materials & WG session regarding all topics from Groups 1A, 1B, and Group 2.
- Return to Group 1A deliberations on Change of Registrant.

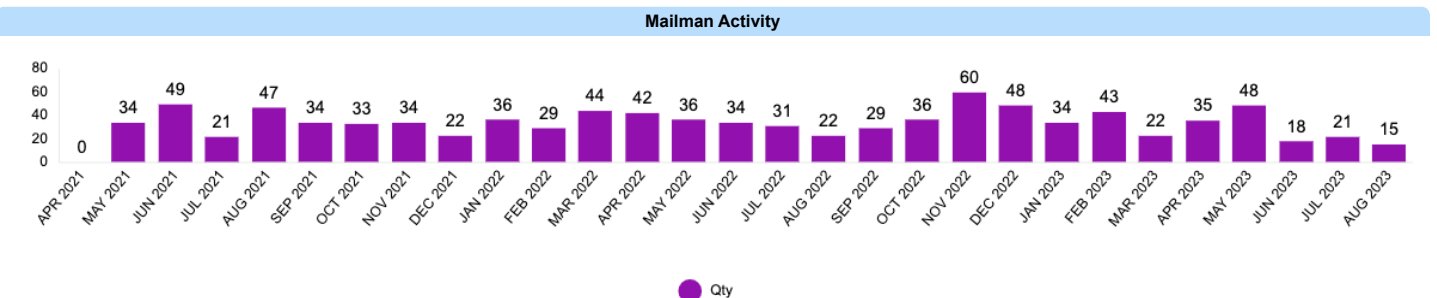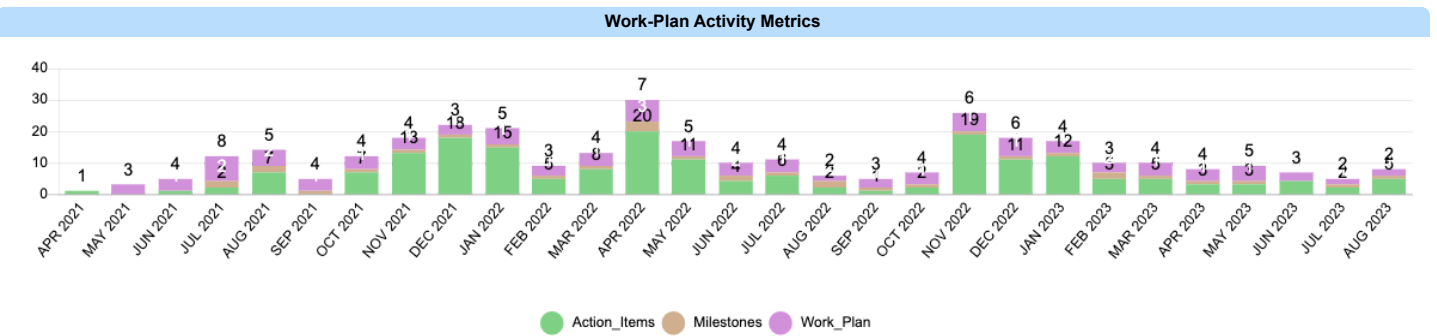

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting ICANN77 TEAC/TDRP	↓	TPR WG	06/12/23	06/12/23	Complete	
	AI	Charter question f5: WG to consider the feasibility of the recommendation of email to "start the clock" for the 24-hour response timeframe.	—	TPR WG	06/27/23	06/27/23	Complete	
	AI	Charter question g3: WG should consider the two types of disputes – inside and outside the policy – and provide additional rationale/comments.	—	TPR WG	06/27/23	06/27/23	Complete	
	WP	Meeting #95 Review draft responses to Charter Questions g3 - g5; ICANN Approved Transfers	↓	TPR WG	06/27/23	06/27/23	Complete	
	AI	Re: Recap Outcomes from ICANN77 Meeting on TEAC and TDRP -- charter questions f5, and g3, g4, and g5 -- See: https://docs.google.com/document/d/1zBYlaFTF5bRrUdhnGifP5CGHvuOoHqKPOhGnU46uGM/edit [docs.google.com] and https://docs.google.com/document/d/1I2DNZLXCKfmoSyffCIUL7lot3V3Zk96X5Q3eaTrEvp4/edit [docs.google.com]; WG members to review the text in the two documents and provide comments in advance of the next meeting on Tuesday, 11 July.	—	TPR WG	07/11/23	07/11/23	Complete	
	AI	Re: Bulk Transfers – WG to review charter questions in advance of the discussion at the next meeting: i1) In light of these challenges described in section 3.1.7.2 of the Final Issue Report, should the required fee in Section I.B.2 of the Transfer Policy be revisited or removed in certain circumstances i2) Should the scope of voluntary bulk transfers, including partial bulk transfers, be expanded and/or made uniform across all registry operators? If so, what types of rules and considerations should govern voluntary bulk transfers and partial bulk transfers	—	TPR WG	07/11/23	07/11/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	07/10/23	07/10/23	Complete	
	WP	Meeting #96 ICANN Approved Transfers - Charter Question i1	↓	TPR WG	07/11/23	07/11/23	Complete	
	WP	Meeting #97 ICANN Approved Transfers	↓	TPR WG	07/25/23	07/25/23	Complete	
	AI	Charter Question i1 ICANN-Approved Transfer (Bulk Transfers) -- Staff will create a working document in Google for WG members to provide comments/suggestions.	—	Policy Support Staff	08/01/23	08/01/23	Complete	
	AI	1.B proposed updates: Staff will create a working document in Google for WG members to provide comments/suggestions.	—	Policy Support Staff	08/01/23	08/01/23	Complete	
	WP	Meeting #98 ICANN Approved Transfers	↓	TPR WG	08/01/23	08/01/23	Complete	
	AI	Charter question i1 staff to create a working document with the preliminary agreements for WG members to review and suggest revisions.	—	Policy Support Staff	08/07/23	08/01/23	Complete	
	WP	Meeting #99 ICANN Approved Transfers	↓	TPR WG	08/08/23	08/08/23	Complete	
	AI	Any WG members who have comments or concerns regarding charter question i1 preliminary agreements please note them in the ICANN-Approved Transfers Working Document [docs.google.com] in advance of the next meeting.	—	TPR WG	08/14/23	08/14/23	Complete	
	AI	Continue today's discussion on the mailing list: Should there be locks, notices, and/or opt-out options for registrants?	—	TPR WG	08/14/23	08/14/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	08/14/23	08/14/23	Complete	
	WP	Meeting #100 ICANN Approved Transfers	↓	TPR WG	08/15/23		In Progress	
	WP	Meeting #101 ICANN Approved Transfers	↓	TPR WG	08/22/23		Not Started	
	WP	Meeting #102 ICANN Approved Transfers	↓	TPR WG	08/29/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	09/11/23		Not Started	
	WP	Meeting #103 "Where we're at" review across Groups 1A, 1B & 2	↓	TPR WG	09/12/23		Not Started	
	WP	Meeting #104 Change of Registrant	↓	TPR WG	09/19/23		Not Started	
	WP	Meeting #105 Change of Registrant	↓	TPR WG	09/26/23		Not Started	
	WP	Meeting #106 Change of Registrant	↓	TPR WG	10/03/23		Not Started	
	WP	Meeting #107 Change of Registrant	↓	TPR WG	10/10/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	10/15/23		Not Started	
	WP	ICANN78 Meeting TBD	↓	TPR WG	10/21/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	11/06/23		Not Started	
	MS	Submit Consolidated Initial Report to GNSO Council & Public Comment	!	TPR WG	08/21/24		Not Started	
