

Project Tracking & Rollup DASHBOARD




Project Name: PDP: Transfer Policy Review | **Program:** Transfers | **Project Sponsor:** GNSO Council

Project Information

52%
% Complete

02/18/21
Actual Start

06/19/25
Planned Finish

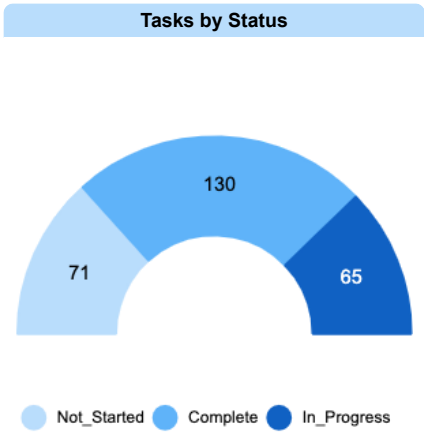

Project Contacts


Roger Carney
Chair

n/a
Vice_Chair

Oswaldo Novoa
Liaison

EB Emily Barabas
Staff_Lead

BC Berry Cobb
Project_Manager

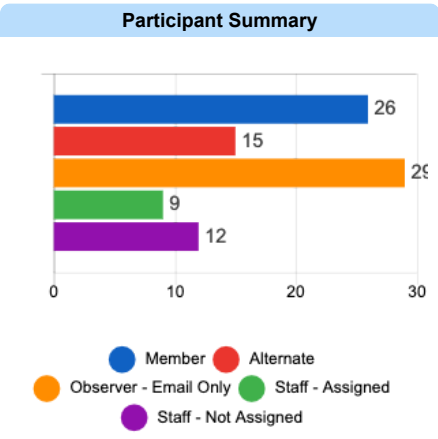

Project Status & Health

Project_Status	Project_Health
Revised Schedule	On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025					
						Q1 Q2 Q3 Q4	Q1 Q2 Q3 Q4	Q1 Q2 Q3 Q4	Q1 Q2 Q3 Q4	Q1 Q2 Q3 Q4 Q1					
	PDP: Transfer Policy Review	02/18/21	06/19/25	52%	In Progress	[Gantt bars for PDP: Transfer Policy Review]									
	PROJECT CONTROL	02/18/21	06/19/25	62%	In Progress	[Gantt bars for PROJECT CONTROL]									
	GROUP DELIBERATIONS	05/13/21	11/14/24	59%	In Progress	[Gantt bars for GROUP DELIBERATIONS]									
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt bars for Group 1A Policy Topics]									
	Group 1B Policy Topics	09/28/23	06/05/24	26%	In Progress	[Gantt bars for Group 1B Policy Topics]									
	Group 2 Policy Topics	02/02/23	09/27/23	55%	In Progress	[Gantt bars for Group 2 Policy Topics]									
	INITIAL REPORT	06/24/21	11/06/24	58%	In Progress	[Gantt bars for INITIAL REPORT]									
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt bars for Publish Initial Report - Group 1A]									
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	Not Started	Not Started	[Gantt bars for Publish Initial Report - Groups (1A, 1B & 2)]									
	FINAL REPORT	08/04/22	02/05/25	22%	In Progress	[Gantt bars for FINAL REPORT]									
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt bars for Review of public comments - Group 1A]									
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	Not Started	Not Started	[Gantt bars for Review of public comments - Groups (1A, 1B & 2)]									
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25	Not Started	Not Started	[Gantt bars for Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council]									

Project Description

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Mailing List](#)
[Meeting Schedule](#)
[Wiki](#)
[Charter](#)

Completed in Prior Period

- Early written input from SO/AC/SC/Cs obtained on the WG's Group 2 charter topics.
- Completed and distributed [Project Package](#).

Open Issues & Risks



- None at this time.

Current Activities & Tasks

- Substantive deliberations on Group 2 topics: Transfer Emergency Action Contact (TEAC), reversal of a transfer, the Transfer Dispute Resolution Policy (TDRP), and Wave 1 - Rec #27 items related to TEAC and TDRP.
- Review of early written input received from SO/AC/SG/Cs on Group 2 topics.
- Planning of agenda for ICANN77.

Planned Activities & Tasks

- Begin deliberation on ICANN Approved Transfers.

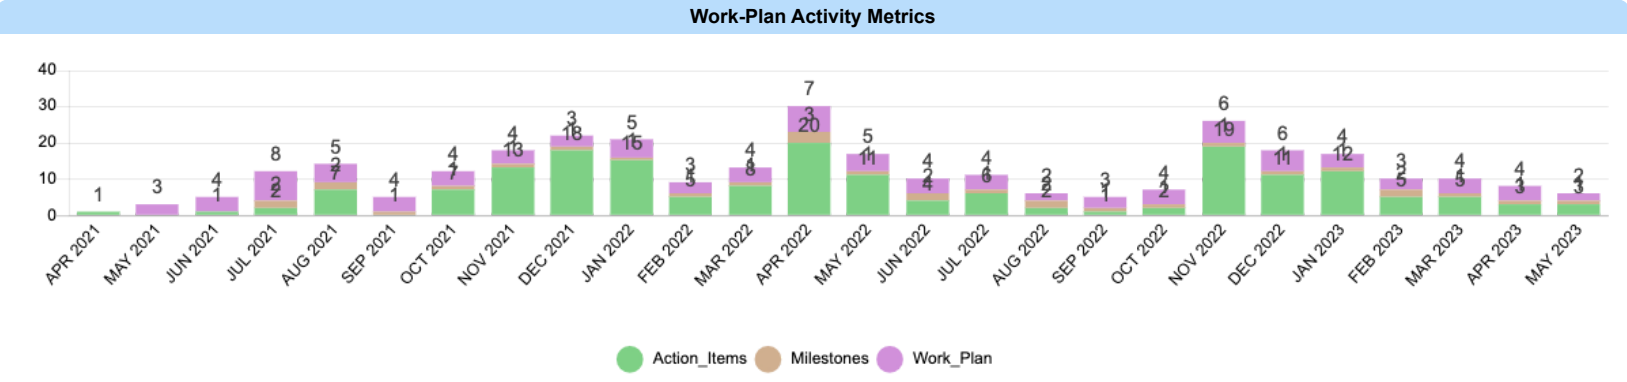

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #85 Gap Analysis Continued	↓	TPR WG	04/04/23	04/04/23	Complete	
	AI	WG members should share any observations/feedback from ICANN76 on the WG email distribution list.	—	TPR WG	04/04/23	04/04/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	04/10/23	04/10/23	Complete	
	WP	Meeting #86 Gap Analysis Continued	↓	TPR WG	04/11/23	04/11/23	Complete	
	AI	Staff to initiate a small team to develop a proposal/language to codify the informal transfer resolution process. Volunteers on the call: Jody Kolker, Rich Brown, Owen Smigelski Juan Manuel Rojas, Zak Muscovitch and Jothan Frakes.		Policy Support Staff	04/18/23	04/18/23	Complete	
	WP	Meeting #87 Gap Analysis Continued - Fast Undo	↓	TPR WG	04/18/23	04/18/23	Complete	
	AI	Interested supporting registrars should provide a proposal in writing for a fast/gap undo in between the informal process and the TDRP/courts by next Tuesday, 25 April.		TPR WG	04/25/23	04/25/23	Complete	
	AI	Ongoing -- Small Team to develop a proposal/language to codify the informal transfer resolution process is continuing its work. Volunteers: Jody Kolker, Rich Brown, Owen Smigelski Juan Manuel Rojas, Zak Muscovitch and Jothan Frakes.		TPR WG	05/01/23	05/01/23	Complete	
	WP	Meeting #88 Charter questions regarding Wave 1, Rec 27 Items	↓	TPR WG	04/25/23	04/25/23	Complete	
	AI	In the Recommendation 27, Wave 1 Working Document: Staff to revise the text based on the feedback from the WG members during the meeting on 25 April. See: https://docs.google.com/document/d/1GTtEPJvYNMW27UaJZAGQISb1BOYRHO7rSbFyb_9dhs/edit?usp=sharing [docs.google.com].		Policy Support Staff	05/02/23	05/02/23	Complete	
	WP	Meeting #89 Small Team proposal, Charter questions regarding Wave 1, Rec 27 Items	↓	TPR WG	05/02/23	05/02/23	Complete	
	AI	Re: Codification of informal dispute resolution process -- By COB Monday, 08 May: WG members should indicate as comments in the document (if any) those elements/details that should be specific policy requirements and whether they are Stakeholder Group positions. See: https://docs.google.com/document/d/1vP9Q-EyhroHlrurqrMWO13_6yAQX2_y7vzteOV3fQ/edit [docs.google.com].		TPR WG	05/08/23	05/08/23	Complete	
	WP	Meeting #90 TEAC Charter Questions F1-F7	↓	TPR WG	05/09/23	05/09/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	05/15/23	05/15/23	Complete	
	WP	Meeting #91 TEAC/TDRP	↓	TPR WG	05/16/23		In Progress	
	WP	Meeting #92 TEAC/TDRP	↓	TPR WG	05/23/23		Not Started	
	WP	Meeting #93 TEAC/TDRP	↓	TPR WG	05/30/23		Not Started	
	WP	Meeting #94 TEAC/TDRP	↓	TPR WG	06/06/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	06/05/23		Not Started	
	WP	Meeting ICANN77 Agenda TBD	↓	TPR WG	06/12/23		Not Started	
	WP	Meeting #95 Agenda TBD	↓	TPR WG	06/27/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	07/10/23		Not Started	
	WP	Meeting #96 Agenda TBD	↓	TPR WG	07/11/23		Not Started	
	WP	Meeting #97 Agenda TBD	↓	TPR WG	07/25/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	08/14/23		Not Started	
	MS	Submit Consolidated Initial Report to GNSO Council & Public Comment	!	TPR WG	08/21/24		Not Started	
