

Project Tracking & Rollup DASHBOARD

Project Name
PDP: Transfer Policy Review

Program
Transfers

Project Sponsor
GNSO Council


Project Information

61%
% Complete

02/18/21
Actual Start

06/19/25
Planned Finish

Tasks by Status



● Not Started ● Complete ● In Progress

Project Contacts

Roger Carney
Chair


n/a
Vice_Chair

Oswaldo Novoa
Liaison

Caitlin Tubergen
Staff_Lead

Berry Cobb
Project_Manager

Participant Summary



● Member ● Alternate
● Observer - Email Only ● Staff - Assigned
● Staff - Not Assigned

Project Status & Health

Project_Status	Project_Health
Revised Schedule	On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025					
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
	PDP: Transfer Policy Review	02/18/21	06/19/25	61%	In Progress	[Gantt Bar]									
	PROJECT CONTROL	02/18/21	06/19/25	72%	In Progress	[Gantt Bar]									
	GROUP DELIBERATIONS	05/13/21	11/14/24	73%	In Progress	[Gantt Bar]									
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt Bar]									
	Group 1B Policy Topics	09/28/23	06/05/24	26%	In Progress	[Gantt Bar]									
	Group 2 Policy Topics	02/02/23	09/27/23	100%	Complete	[Gantt Bar]									
	INITIAL REPORT	06/24/21	11/06/24	69%	In Progress	[Gantt Bar]									
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt Bar]									
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	Not Started	Not Started	[Gantt Bar]									
	FINAL REPORT	08/04/22	02/05/25	22%	In Progress	[Gantt Bar]									
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt Bar]									
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	Not Started	Not Started	[Gantt Bar]									
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25	Not Started	Not Started	[Gantt Bar]									

Project Description

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Mailing List](#)
[Meeting Schedule](#)
[Wiki](#)
[Charter](#)

Completed in Prior Period



- Completed deliberations on ICANN-Approved Transfers.
- Completed and distributed [Project Package](#).

Current Activities & Tasks

- Working session at ICANN78 in Hamburg focused on the last items for TDRP.
- Conduct a "where we're at" materials and WG session regarding all topics from Groups 1A, 1B, & Group 2.

Planned Activities & Tasks

- Conduct a "where we're at" materials & WG session regarding all topics from Groups 1A, 1B, and Group 2.

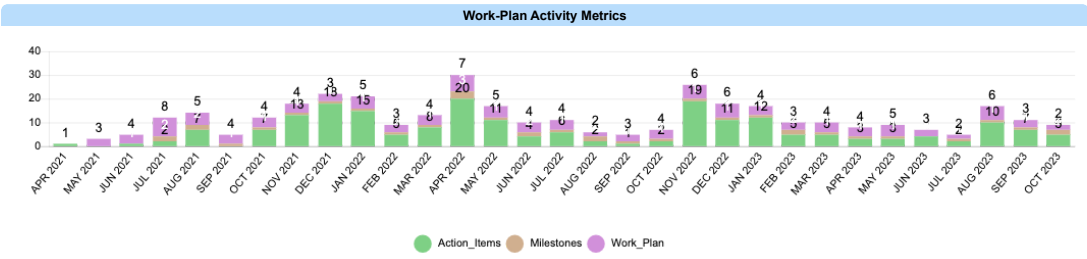

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #102 ICANN Approved Transfers	↓	TPR WG	08/29/23	08/29/23	Complete	
	AI	Staff to update the TPR Working Document [docs.google.com] based on today's discussion, including the 5 questions posed during the call (Re: Concepts 3 & 4).	—	Policy Support Staff	09/11/23	09/11/23	Complete	
	AI	Re: Charter Question i2) – WG members to provide their comments/suggestions in the Working Document [docs.google.com] regarding whether the scope of voluntary bulk transfers, including partial bulk transfers, should be expanded and/or made uniform across: 1. all registry operators (via an update to the Transfer Policy), or 2. all registry operators who offer the BTAPPA (via recommended updates to the BTAPPA)	—	TPR WG	09/11/23	09/11/23	Complete	
	AI	WG to specifically respond to the 6 questions from the 29 August call regarding bulk transfers.	—	TPR WG	09/11/23	09/11/23	Complete	
	WP	Meeting #XXX No meeting this week	↓	TPR WG	09/05/23	08/14/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	09/11/23	09/11/23	Complete	
	WP	Meeting #103 ICANN Approved Transfers	↓	TPR WG	09/12/23	09/12/23	Complete	
	AI	Staff to draft options for preliminary recommendation language for the Working Group to review and discuss on the next call.	—	Policy Support Staff	09/13/23	09/13/23	Complete	
	WP	Meeting #104 ICANN Approved Transfers	↓	TPR WG	09/19/23	09/19/23	Complete	
	AI	WG members to review the preliminary recommendations in the document at https://docs.google.com/document/d/1gX1N8d3qoktbnRmfGE4-8Un9dPavIKQ3IZYaoe9b0E/edit?usp=sharing [docs.google.com] beginning on page 4 and provide comments.	—	TPR WG	09/25/23	09/25/23	Complete	
	AI	WG members and RySG in particular to indicate which option(s) they favor in the document at https://docs.google.com/document/d/1gX1N8d3qoktbnRmfGE4-8Un9dPavIKQ3IZYaoe9b0E/edit?usp=sharing [docs.google.com] on page 11.	—	TPR WG	09/25/23	09/25/23	Complete	
	WP	Meeting #105 ICANN Approved Transfers	↓	TPR WG	09/26/23	09/26/23	Complete	
	AI	Staff to provide the data on the number of registries that offer BTAPPA services.	—	Policy Support Staff	09/28/23	09/28/23	Complete	
	AI	WG members to provide their feedback/preferences on the 4 options: https://docs.google.com/document/d/1b0KlvhRyyO5QSEI4DB4vP78muKvqHneaXOZTcvliBPQ/edit?usp=sharing [docs.google.com]	—	TPR WG	10/02/23	10/02/23	Complete	
	WP	Meeting #106 ICANN Approved Transfers	↓	TPR WG	10/03/23	10/03/23	Complete	
	AI	Staff to update the draft recommendations based on today's discussion	—	Policy Support Staff	10/06/23	10/06/23	Complete	
	AI	WG members to review the updates and provide feedback by COB Monday, 09 Oct	—	TPR WG	10/09/23	10/09/23	Complete	
	WP	Meeting #107 ICANN Approved Transfers / TDRP-Rec27	↓	TPR WG	10/10/23	10/10/23	Complete	
	AI	Staff to update the draft recommendations based on today's discussion	—	Policy Support Staff	10/12/23	10/12/23	Complete	
	AI	WG members to review the updated recommendations and provide any feedback by COB Tuesday, 17 Oct	—	TPR WG	10/17/23	10/17/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	10/15/23	10/15/23	Complete	
	WP	ICANN78 Meeting Remaining items on TDRP	↓	TPR WG	10/21/23		In Progress	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	11/06/23	10/15/23	Complete	No package created given short timing between Oct/Nov Council meetings.
	WP	Meeting #108 "Where we're at" review across Groups 1A, 1B & 2	↓	TPR WG	11/07/23		Not Started	
	WP	Meeting #109 Begin deliberations on Change of Registrant	↓	TPR WG	11/14/23		Not Started	
	WP	Meeting #110 Continue deliberations on Change of Registrant	↓	TPR WG	11/28/23		Not Started	
	WP	Meeting #111 Continue deliberations on Change of Registrant	↓	TPR WG	12/05/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	12/11/23		Not Started	
	WP	Meeting #112 Continue deliberations on Change of Registrant	↓	TPR WG	12/12/23		Not Started	
	WP	Meeting #113 Continue deliberations on Change of Registrant	↓	TPR WG	12/19/23		Not Started	
	WP	Meeting #114 Continue deliberations on Change of Registrant	↓	TPR WG	01/09/24		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	01/15/24		Not Started	
	MS	Submit Consolidated Initial Report to GNSO Council & Public Comment	!	TPR WG	08/21/24		Not Started	
