

Project Tracking & Rollup DASHBOARD

Project Name PDP: Transfer Policy Review **Program** Transfers **Project Sponsor** GNSO Council


Project Information

48%
% Complete

02/18/21
Actual Start

06/19/25
Planned Finish

Tasks by Status



● Not_Started ● Complete ● In_Progress

Project Contacts

Roger Carney
Chair


n/a
Vice_Chair

Osvaldo Novoa
Liaison

Emily Barabas
Staff_Lead

Berry Cobb
Project_Manager

Participant Summary



● Member ● Alternate
● Observer - Email Only ● Staff - Assigned
● Staff - Not Assigned

Project Status & Health

Project_Status	Project_Health
Revised Schedule	On-Target

Summary Gantt & Key Milestones

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021	2022	2023	2024	2025							
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	PDP: Transfer Policy Review	02/18/21	06/19/25	48%	In Progress	[Gantt Bar]											
	PROJECT CONTROL	02/18/21	06/19/25	59%	In Progress	[Gantt Bar]											
	GROUP DELIBERATIONS	05/13/21	11/14/24	57%	In Progress	[Gantt Bar]											
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt Bar]											
	Group 1B Policy Topics	09/28/23	06/05/24	26%	In Progress	[Gantt Bar]											
	Group 2 Policy Topics	02/02/23	09/27/23	29%	In Progress	[Gantt Bar]											
	INITIAL REPORT	06/24/21	11/06/24	51%	In Progress	[Gantt Bar]											
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt Bar]											
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	Not Started	Not Started	[Gantt Bar]											
	FINAL REPORT	08/04/22	02/05/25	22%	In Progress	[Gantt Bar]											
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt Bar]											
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	Not Started	Not Started	[Gantt Bar]											
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25	Not Started	Not Started	[Gantt Bar]											

Project Description **Completed in Prior Period**

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Mailing List](#)
[Meeting Schedule](#)
[Wiki](#)
[Charter](#)

- ICANN76 Cancun public sessions for the WG.
- Completed and distributed [Project Package](#).

Open Issues & Risks **Current Activities & Tasks**


• None at this time.

- Substantive deliberations on Group 2 topics: Transfer Emergency Action Contact (TEAC), reversal of a transfer, and the Transfer Dispute Resolution Policy (TDRP).
- Early Community Outreach to obtain input on the WG's Group 2 charter topics.


Planned Activities & Tasks

- Review of early input received from SO/AC/SG/Cs on Group 2 topics.
- Planning of agenda for ICANN77.

Work-Plan Activity Metrics

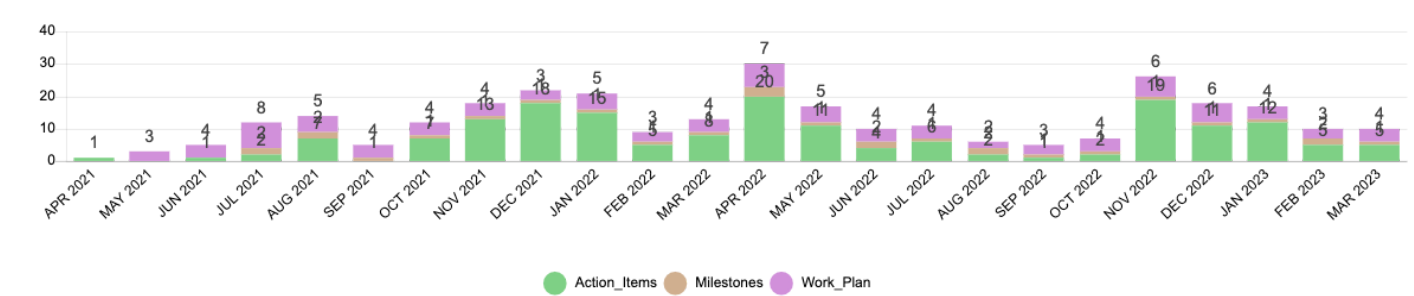

Mailman Activity



Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #81 TEAC	↓	TPR WG	02/21/23	02/21/23	Complete	
	AI	Re: Data from RADAR relating to TEAC -- Staff will check to see if there is any available data.	—	Policy Support Staff	03/08/23	02/23/23	Complete	
	AI	Re: The time frame (4 hours) for registrars to respond to communications via the TEAC channel – WG members should consider a provisional recommendation to change the time frame to 24 hours.	—	TPR WG	03/01/23	03/01/23	Complete	
	AI	Re: 07 March meeting -- If WG members cannot attend the 07 March meeting please let the Secretariat staff know at gns0-secs@icann.org so we can decide if we have enough attendance to hold the meeting.	—	TPR WG	03/06/23	03/06/23	Complete	
	WP	Meeting #82 TEAC	↓	TPR WG	02/28/23	02/28/23	Complete	
	AI	Re: 07 March meeting -- If WG members cannot attend the 07 March meeting please let the Secretariat staff know at gns0-secs@icann.org so we can decide if we have enough attendance to hold the meeting.	—	TPR WG	03/06/23	03/06/23	Complete	
	AI	Re: The time frame (4 hours) for registrars to respond to communications via the TEAC channel – WG members should consider a provisional recommendation to change the time frame to 24 hours.	—	TPR WG	03/06/23	03/06/23	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	03/04/23	03/06/23	Complete	
	WP	Meeting #83 TDRP	↓	TPR WG	03/07/23	03/07/23	Complete	
	AI	Re: TDRP -- Staff to research whether there are materials describing the goals of the TDRP.	—	Policy Support Staff	03/15/23	03/11/23	Complete	
	WP	Meeting ICANN76 - Part 1 TDRP	↓	TPR WG	03/11/23	03/11/23	Complete	
	WP	Meeting ICANN76 - Part 2 Transfer Reversal - Gap Analysis	↓	TPR WG	03/12/23	03/12/23	Complete	
	WP	Meeting #84 Gap Analysis Continued	↓	TPR WG	03/28/23	03/28/23	Complete	
	WP	Meeting #85 TEAC/TDRP	↓	TPR WG	04/04/23		In Progress	
	AI	WG members should share any observations/feedback from ICANN76 on the WG email distribution list.	—	TPR WG	04/04/23		In Progress	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	04/10/23		In Progress	
	WP	Meeting #86 TEAC/TDRP	↓	TPR WG	04/11/23		Not Started	
	WP	Meeting #87 TEAC/TDRP	↓	TPR WG	04/18/23		Not Started	
	WP	Meeting #88 TEAC/TDRP	↓	TPR WG	04/25/23		Not Started	
	WP	Meeting #89 TEAC/TDRP	↓	TPR WG	05/02/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	05/08/23		Not Started	
	WP	Meeting #90 TEAC/TDRP	↓	TPR WG	05/09/23		Not Started	
	WP	Meeting #91 TEAC/TDRP	↓	TPR WG	05/16/23		Not Started	
	WP	Meeting #92 TEAC/TDRP	↓	TPR WG	05/23/23		Not Started	
	WP	Meeting #93 TEAC/TDRP	↓	TPR WG	05/30/23		Not Started	
	WP	Meeting #94 TEAC/TDRP	↓	TPR WG	06/06/23		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	06/05/23		Not Started	
	WP	Meeting ICANN77 TBD	↓	TPR WG	06/12/23		Not Started	
	MS	Submit Consolidated Initial Report to GNSO Council & Public Comment	!	TPR WG	08/21/24		Not Started	
