

# Project Tracking & Rollup DASHBOARD

<b>Project Name</b> PDP: Transfer Policy Review	<b>Program</b> Transfers	<b>Project Sponsor</b> GNSO Council
--	-----------------------------	--

**Project Information**

**91%**  
% Complete

**02/18/21**  
Actual Start

**06/19/25**  
Planned Finish

**Tasks by Status**

● Not\_Started ● Complete ● In\_Progress

**Project Contacts**

**Roger Carney**  
Chair

**n/a**  
Vice\_Chair

**Osvaldo Novoa**  
Liaison

**Caitlin Tubergen**  
Staff\_Lead

**Christian Wheeler**  
Project\_Manager

**Participant Summary**

● Member ● Alternate  
● Observer - Email Only ● Staff - Assigned  
● Staff - Not Assigned

**Summary Gantt & Key Milestones**

Health	Primary Task	Current Start	Current Finish	% Complete	Status	2021 2022 2023 2024 2025											
						Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	<b>PDP: Transfer Policy Review</b>	02/18/21	06/19/25	91%	In Progress	[Gantt Bar]											
	<b>PROJECT CONTROL</b>	02/18/21	06/19/25	98%	In Progress	[Gantt Bar]											
●	<b>GROUP DELIBERATIONS</b>	05/13/21	03/13/25	95%	In Progress	[Gantt Bar]											
	Group 1A Policy Topics	06/03/21	05/11/22	100%	Complete	[Gantt Bar]											
	Group 1B Policy Topics	09/28/23	06/05/24	100%	Complete	[Gantt Bar]											
	Group 2 Policy Topics	02/02/23	09/27/23	100%	Complete	[Gantt Bar]											
	<b>INITIAL REPORT</b>	06/24/21	11/06/24	100%	Complete	[Gantt Bar]											
	Publish Initial Report - Group 1A	06/15/22	06/15/22	100%	Complete	[Gantt Bar]											
	Publish Initial Report - Groups (1A, 1B & 2)	08/21/24	08/21/24	100%	Complete	[Gantt Bar]											
	<b>FINAL REPORT</b>	08/04/22	02/05/25	75%	In Progress	[Gantt Bar]											
	Review of public comments - Group 1A	08/04/22	09/14/22	100%	Complete	[Gantt Bar]											
	Review of public comments - Groups (1A, 1B & 2)	11/07/24	12/18/24	100%	Complete	[Gantt Bar]											
	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	02/05/25	02/05/25		Not Started	[Gantt Bar]											

**Project Description**

On 18 February 2021, The GNSO Council passed a resolution to initiate a two-phased PDP to review the Transfer Policy. The PDP working group is tasked with determining if changes to the policy are needed to improve the ease, security, and efficacy of inter-registrar and inter-registrant transfers.

[Meeting Schedule](#)

[Wiki](#)

[Charter](#)



- Completed in Prior Period**
- Completed the report of [public comments](#).
  - Completed ICANN81 Session.
  - Completed the review of public comments.
  - Completed and distributed [Project Package](#).




**Open Issues & Risks**

None for this period.

- Current Activities & Tasks**
- The Working Group is reviewing and working towards its Final Report in January 2025.

- Planned Activities & Tasks**
- The Working Group to determine consensus levels on its final recommendations.

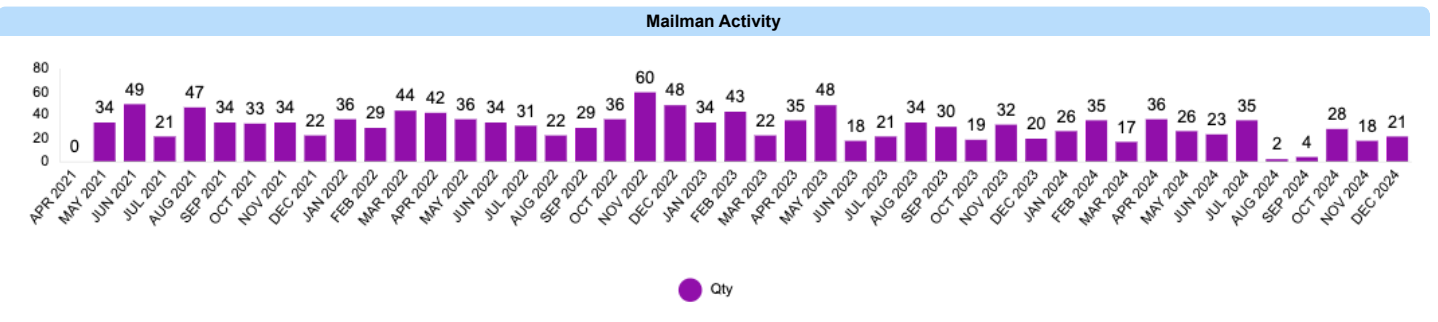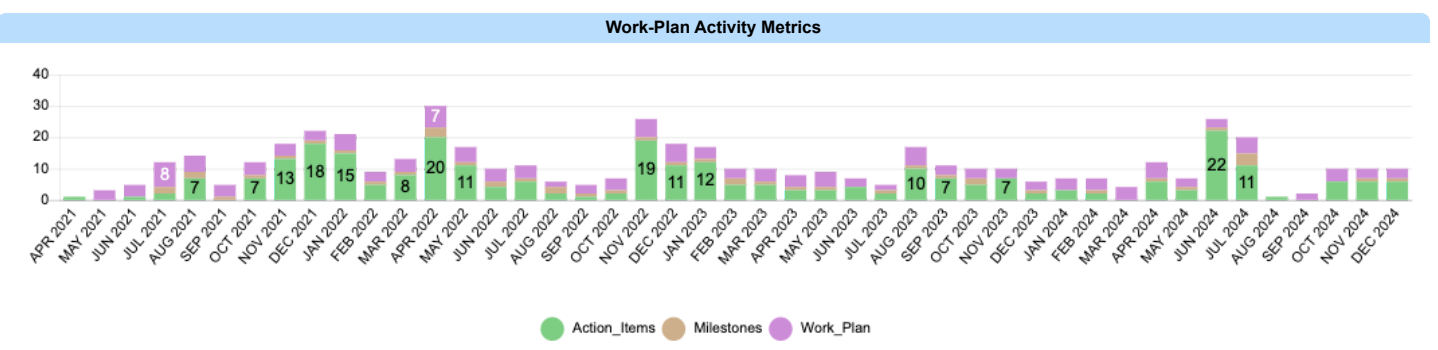

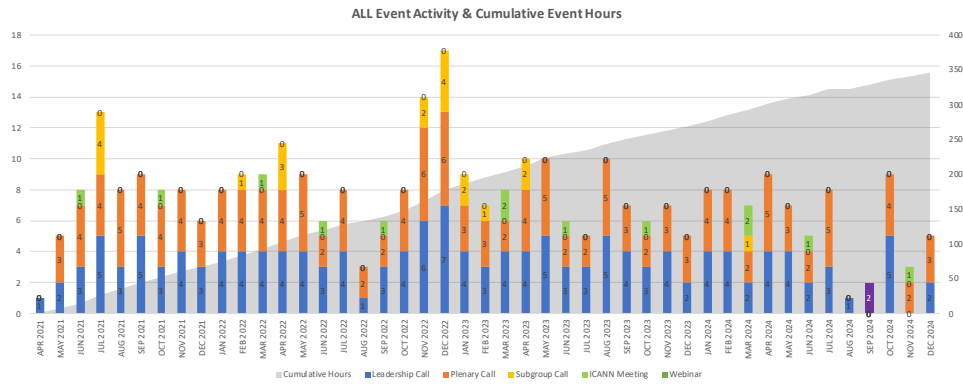

**Roster & Attendance - All Events**

Member	Row Labels	Invited	Attended	Percent	Role	SOI	Start Date	Depart Date
<b>AT-Large Advisory Committee (ALAC)</b>		<b>3424</b>	<b>2460</b>	<b>71.8%</b>				
At-Large Advisory Committee (ALAC)		281	161	57.3%				
Nanghika Daniel Khauka		140	41	29.3%		<a href="https://community.icann.org/x/ki9eAw">https://community.icann.org/x/ki9eAw</a>	04.05.2021	
Steinrik Grätterød		141	130	85.1%		<a href="https://community.icann.org/x/Lok1CQ">https://community.icann.org/x/Lok1CQ</a>	05.05.2021	
<b>Commercial Business Users Constituency (BC)</b>		<b>146</b>	<b>128</b>	<b>87.7%</b>				
Zak Muscovitch		146	128	87.7%		<a href="https://community.icann.org/x/UEmAAw">https://community.icann.org/x/UEmAAw</a>	23.04.2021	
<b>GNSO Council</b>		<b>541</b>	<b>425</b>	<b>78.6%</b>				
Gregory DiBlase		120	61	50.8%	Liaison	<a href="https://community.icann.org/x/jiCEnAw">https://community.icann.org/x/jiCEnAw</a>	04.06.2021	21.12.2022
Ovaldo Nova		128	74	57.8%	Liaison	<a href="https://community.icann.org/x/H8PpAQ">https://community.icann.org/x/H8PpAQ</a>	21.12.2022	
Roger Carney		293	290	99.0%	Chair	<a href="https://community.icann.org/x/COMdAw">https://community.icann.org/x/COMdAw</a>	23.04.2021	
<b>Intellectual Property Constituency (IPC)</b>		<b>280</b>	<b>54</b>	<b>19.3%</b>				
Mike Rodenbaugh		140	46	32.9%		<a href="https://community.icann.org/x/Ah9AAw">https://community.icann.org/x/Ah9AAw</a>	21.04.2021	
Salvador Camacho Hernandez		140	8	5.7%		<a href="https://community.icann.org/x/1AAw">https://community.icann.org/x/1AAw</a>	26.04.2021	
<b>Internet Service Providers and Connectivity Providers Constituency (ISPC)</b>		<b>145</b>	<b>116</b>	<b>80.0%</b>				
John Woodworth		145	116	80.0%		<a href="https://community.icann.org/x/Gw1CQ">https://community.icann.org/x/Gw1CQ</a>	14.04.2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>		<b>153</b>	<b>95</b>	<b>62.1%</b>				
Juan Manuel Rojas		71	43	60.6%		<a href="https://community.icann.org/x/E8PbAQ">https://community.icann.org/x/E8PbAQ</a>	22.06.2022	
Kenneth Herman		48	45	93.8%		<a href="https://community.icann.org/x/AlkXdg">https://community.icann.org/x/AlkXdg</a>	25.07.2023	
Raoul Plommer		34	7	20.6%		<a href="https://community.icann.org/x/K9abAw">https://community.icann.org/x/K9abAw</a>	12.07.2022	27.06.2023
<b>Registrar Stakeholder Group (RvSG)</b>		<b>1480</b>	<b>1270</b>	<b>85.8%</b>				
Catherine Paletta		142	103	72.5%		<a href="https://community.icann.org/x/RSW1CQ">https://community.icann.org/x/RSW1CQ</a>	27.04.2021	
Eric Rokobauer		140	127	90.7%		<a href="https://community.icann.org/x/CKK4Aw">https://community.icann.org/x/CKK4Aw</a>	26.04.2021	
Jody Kolker		144	134	93.1%		<a href="https://community.icann.org/x/KAkAAw">https://community.icann.org/x/KAkAAw</a>	07.05.2021	
Jothan Frakes		133	123	92.5%		<a href="https://community.icann.org/x/Gb-hAAw">https://community.icann.org/x/Gb-hAAw</a>	23.04.2021	
Karim Tobin		73	62	84.9%		<a href="https://community.icann.org/x/JPp1CQ">https://community.icann.org/x/JPp1CQ</a>	07.06.2021	10.02.2023
Nan Chow		125	113	89.6%		<a href="https://community.icann.org/x/DW1hAw">https://community.icann.org/x/DW1hAw</a>	06.05.2021	21.06.2024
Owen Smigelski		152	128	84.2%		<a href="https://community.icann.org/x/BalW8e">https://community.icann.org/x/BalW8e</a>	27.04.2021	
Prudence Malinski		141	113	80.1%		<a href="https://community.icann.org/x/NoC1CQ">https://community.icann.org/x/NoC1CQ</a>	27.04.2021	
Richard Merdinger		4	4	100.0%		<a href="https://community.icann.org/x/R8N8Aw">https://community.icann.org/x/R8N8Aw</a>	05.05.2021	07.06.2021
Sarah Wyld		3	3	100.0%		<a href="https://community.icann.org/x/JPw6Aw">https://community.icann.org/x/JPw6Aw</a>	23.04.2021	
Theo Geurts		141	125	88.7%		<a href="https://community.icann.org/x/jiyMAw">https://community.icann.org/x/jiyMAw</a>	23.04.2021	
Thomas Keller		16	9	56.3%		<a href="https://community.icann.org/x/jhEhAAw">https://community.icann.org/x/jhEhAAw</a>	26.04.2021	27.09.2021
Volker Greimann		138	99	71.7%		<a href="https://community.icann.org/x/foBwAw">https://community.icann.org/x/foBwAw</a>	24.04.2021	
Rich Brown		128	128	100.0%		<a href="https://community.icann.org/x/NAW1CQ">https://community.icann.org/x/NAW1CQ</a>	26.04.2021	
<b>Registry Stakeholder Group (RvSG)</b>		<b>258</b>	<b>198</b>	<b>76.7%</b>				
James Galvin		145	112	75.2%		<a href="https://community.icann.org/x/68F1Aw">https://community.icann.org/x/68F1Aw</a>	27.04.2021	
Richard Wilhelm		109	86	78.9%		<a href="https://community.icann.org/x/R8K1Cw">https://community.icann.org/x/R8K1Cw</a>	23.11.2022	
<b>Security and Stability Advisory Committee (SSAC)</b>		<b>140</b>	<b>13</b>	<b>9.3%</b>				
Stephen Crocker		140	13	9.3%	Subject Matter Expert	<a href="https://community.icann.org/x/L-RK88">https://community.icann.org/x/L-RK88</a>	26.04.2021	
<b>Alternate</b>		<b>887</b>	<b>758</b>	<b>85.5%</b>				
At-Large Advisory Committee (ALAC)		97	86	88.7%				
Lutz Donnerhacke		48	44	91.7%		<a href="https://community.icann.org/x/BAHQCG">https://community.icann.org/x/BAHQCG</a>	08.05.2021	
Raymond Selorm Mamattah		49	42	85.7%		<a href="https://community.icann.org/x/FatE8w">https://community.icann.org/x/FatE8w</a>	04.05.2021	
<b>Commercial Business Users Constituency (BC)</b>		<b>125</b>	<b>124</b>	<b>99.2%</b>				
Ariinola Akinyemi		125	124	99.2%		<a href="https://community.icann.org/x/vAE_Cg">https://community.icann.org/x/vAE_Cg</a>	12.08.2021	
<b>Non-Commercial Stakeholder Group (NCSG)</b>		<b>158</b>	<b>72</b>	<b>45.6%</b>				
Farzaneh Badiei		59	18	30.5%		<a href="https://community.icann.org/x/ljhrAAw">https://community.icann.org/x/ljhrAAw</a>	24.07.2023	
Wisdom Donker		99	64	64.5%		<a href="https://community.icann.org/x/ljz2Aw">https://community.icann.org/x/ljz2Aw</a>	01.06.2021	
<b>Registrar Stakeholder Group (RvSG)</b>		<b>480</b>	<b>449</b>	<b>93.5%</b>				
Andrew Beberry		5	4	80.0%		<a href="https://community.icann.org/x/BxFLCw">https://community.icann.org/x/BxFLCw</a>	23.04.2021	
Arnaud Wittersheim		100	99	99.0%		<a href="https://community.icann.org/x/CBQnAw">https://community.icann.org/x/CBQnAw</a>	05.05.2021	
Benny Samuelsen		30	30	100.0%		<a href="https://community.icann.org/x/NT5AAw">https://community.icann.org/x/NT5AAw</a>	23.04.2021	
Christopher Patterson		46	46	100.0%		<a href="https://community.icann.org/x/w4pXDG">https://community.icann.org/x/w4pXDG</a>	14.05.2021	
Essie Musallov		118	116	98.3%		<a href="https://community.icann.org/x/aQW1CQ">https://community.icann.org/x/aQW1CQ</a>	23.04.2021	
Heidi Revels		19	19	100.0%		<a href="https://community.icann.org/x/AlAKDw">https://community.icann.org/x/AlAKDw</a>	24.07.2023	
Jacques Blanc		7	4	57.1%		<a href="https://community.icann.org/x/6oK1CQ">https://community.icann.org/x/6oK1CQ</a>	29.04.2021	
Jothan Frakes		13	13	100.0%		<a href="https://community.icann.org/x/Gb-hAAw">https://community.icann.org/x/Gb-hAAw</a>	23.04.2021	
Min Feng		5	2	40.0%		<a href="https://community.icann.org/x/WIK1CQ">https://community.icann.org/x/WIK1CQ</a>	26.04.2021	
Pam Little		2	1	50.0%		<a href="https://community.icann.org/x/4eulAAw">https://community.icann.org/x/4eulAAw</a>	26.04.2021	30.05.2023
Sarah Wyld		133	113	85.0%		<a href="https://community.icann.org/x/JPw6Aw">https://community.icann.org/x/JPw6Aw</a>	23.04.2021	
Rich Brown		2	2	100.0%		<a href="https://community.icann.org/x/NAW1CQ">https://community.icann.org/x/NAW1CQ</a>	26.04.2021	
<b>Registry Stakeholder Group (RvSG)</b>		<b>22</b>	<b>22</b>	<b>100.0%</b>				
Carolyn Mitchell		22	22	100.0%		<a href="https://community.icann.org/x/8m4AAw">https://community.icann.org/x/8m4AAw</a>	07.03.2023	
<b>Not-for-Profit Organizations Constituency (NPOC)</b>		<b>5</b>	<b>5</b>	<b>100.0%</b>				
Bolufife Adisa		5	5	100.0%		<a href="https://community.icann.org/x/kiKCDa">https://community.icann.org/x/kiKCDa</a>	25.07.2023	
<b>Grand Total</b>		<b>4311</b>	<b>3218</b>	<b>74.6%</b>				

**Staff Support Roster**

Staff - Assigned	Row Labels	Start Date	Depart Date
<b>Internet Corporation for Assigned Names &amp; Numbers (ICANN)</b>			
Berry Cobb		18.02.2021	13.10.2024
Caitlin Tubergen		18.02.2021	
Christian Wheeler		27.07.2023	
Devan Reed		16.11.2021	
Emily Barabas		18.02.2021	17.07.2023
Feodora Hamza		22.02.2024	
Hollida Yanik	Liaison	30.04.2021	
Isabelle Coles	Liaison	10.06.2021	
Julia Bigland		18.02.2021	
Julie Hedlund		18.02.2021	
Leon Grundmann		15.11.2022	
Terri Agnew		18.02.2021	

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025			
									Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
		<b>PDP: Transfer Policy Review</b>	<b>1131d</b>	<b>02/18/21</b>	<b>06/19/25</b>		<b>91%</b>	<b>In Progress</b>																				
	<b>1</b>	<b>PROJECT CONTROL</b>	<b>1131d</b>	<b>02/18/21</b>	<b>06/19/25</b>		<b>98%</b>	<b>In Progress</b>																				
	1.1	Project start confirmed	0	02/18/21	02/18/21		100%	Complete																				
	1.2	Adopt/Confirm charter	25d	02/18/21	03/24/21	3	100%	Complete																				
	1.3	Confirmation of Team	50d	02/18/21	04/28/21	3	100%	Complete																				
	1.4	Appointment of Team Chair	50d	02/18/21	04/28/21	3	100%	Complete																				
	1.5	Appointment of Liaison to GNSO Council	50d	02/18/21	04/28/21	3	100%	Complete																				
	1.6	Chair / Staff preparations	10d	04/29/21	05/12/21	6	100%	Complete																				
	<b>1.7</b>	<b>Project Management</b>	<b>1081d</b>	<b>04/29/21</b>	<b>06/19/25</b>		<b>98%</b>	<b>In Progress</b>																				
	1.7.1	Develop and confirm Project Plan	30d	04/29/21	06/09/21	6	100%	Complete																				
	1.7.2	Obtain project plan approval from GNSO Council	30d	06/10/21	07/21/21	10	100%	Complete																				
	<b>1.7.3</b>	<b>Develop monthly Project Packages and deliver to Group &amp; Council</b>	<b>900d</b>	<b>07/22/21</b>	<b>01/01/25</b>	<b>11</b>	<b>99%</b>	<b>In Progress</b>																				
	<b>1.7.4</b>	<b>Leadership Sub team</b>	<b>970d</b>	<b>04/29/21</b>	<b>01/15/25</b>		<b>98%</b>	<b>In Progress</b>																				
	<b>1.7.4.1</b>	<b>On-going preparation and planning of group activities</b>	<b>970d</b>	<b>04/29/21</b>	<b>01/15/25</b>	<b>6</b>	<b>98%</b>	<b>In Progress</b>																				
	1.7.5	Close project and transition project to implementation	1d	06/19/25	06/19/25	14, 268		Not Started																				
<span style="color:red">●</span>	<b>2</b>	<b>GROUP DELIBERATIONS</b>	<b>1001d</b>	<b>05/13/21</b>	<b>03/13/25</b>		<b>95%</b>	<b>In Progress</b>																				
	2.1	First meeting of Team	1d	05/13/21	05/13/21	8	100%	Complete																				
	2.2	Understand Charter, organize materials and develop initial approach	10d	05/13/21	05/26/21	8	100%	Complete																				
	2.3	Overview & initial discussion of all Policy Topics	15d	05/13/21	06/02/21	8	100%	Complete																				
	2.4	Develop definitions and terminology	30d	05/13/21	06/23/21	8	100%	Complete																				
	2.5	+ Input from other SO/ACs & GNSO SG/Cs	91d	05/27/21	09/30/21		100%	Complete																				
	2.6	+ Group 1A Policy Topics	245d	06/03/21	05/11/22		100%	Complete																				
	2.7	Group 1B Policy Topics - Preliminary Discussions	165d	06/16/22	02/01/23	250SS	100%	Complete																				
	2.8	+ Group 1B Policy Topics	180d	09/28/23	06/05/24		100%	Complete																				
	2.9	+ Group 2 Policy Topics	170d	02/02/23	09/27/23		100%	Complete																				
	<b>2.10</b>	<b>Key Group Events</b>	<b>884d</b>	<b>10/25/21</b>	<b>03/13/25</b>		<b>90%</b>	<b>In Progress</b>																				
	<b>2.10.1</b>	<b>ICANN Meetings/WG Team F2F Meeting</b>	<b>884d</b>	<b>10/25/21</b>	<b>03/13/25</b>		<b>90%</b>	<b>In Progress</b>																				
	2.10.1.1	ICANN72	4d	10/25/21	10/28/21		100%	Complete																				
	2.10.1.2	ICANN73	5d	03/05/22	03/10/22		100%	Complete																				
	2.10.1.3	ICANN74	4d	06/13/22	06/16/22		100%	Complete																				
	2.10.1.4	ICANN75	5d	09/17/22	09/22/22		100%	Complete																				
	2.10.1.5	ICANN76	5d	03/11/23	03/16/23		100%	Complete																				
	2.10.1.6	ICANN77	4d	06/12/23	06/15/23		100%	Complete																				
	2.10.1.7	ICANN78	5d	10/21/23	10/26/23		100%	Complete																				
	2.10.1.8	ICANN79	5d	03/02/24	03/07/24		100%	Complete																				
	2.10.1.9	ICANN80	4d	06/10/24	06/13/24		100%	Complete																				
	2.10.1.10	ICANN81	5d	11/09/24	11/14/24		100%	Complete																				
	2.10.1.11	ICANN82	5d	03/08/25	03/13/25		0%	In Progress																				
	<b>3</b>	<b>INITIAL REPORT</b>	<b>880d</b>	<b>06/24/21</b>	<b>11/06/24</b>		<b>100%</b>	<b>Complete</b>																				
	3.1	+ Group 1A Initial Report	290d	06/24/21	08/03/22		100%	Complete																				
	3.2	- Groups (1A, 1B & 2) Initial Report	625d	06/16/22	11/06/24		100%	Complete																				
	3.2.1	Populate stable drafts as required	520d	06/16/22	06/12/24	248	100%	Complete																				
	3.2.2	Discuss/approve findings and interim recommendations	20d	06/13/24	07/10/24	104, 172, 252	100%	Complete																				
	3.2.3	Consolidate interim recommendations and findings	20d	07/11/24	08/07/24	253	100%	Complete																				
	3.2.4	Build Draft Report for public comment	20d	07/11/24	08/07/24	253	100%	Complete																				
	3.2.5	Approve Draft Report for public comment	10d	08/08/24	08/21/24	255	100%	Complete																				
	3.2.6	Publish Initial Report - Groups (1A, 1B & 2)	0	08/21/24	08/21/24	256	100%	Complete																				
	3.2.7	Communicate Initial Report	5d	08/22/24	08/28/24	256	100%	Complete																				
	3.2.8	Public comment forum on the Groups (1A, 1B & 2) Initial Report (60 days)	55d	08/22/24	11/06/24	256	100%	Complete																				
	<b>4</b>	<b>FINAL REPORT</b>	<b>655d</b>	<b>08/04/22</b>	<b>02/05/25</b>		<b>75%</b>	<b>In Progress</b>																				

Health	WBS	Task Name	Current Duration	Current Start	Current Finish	Predecessors	% Complete	Status	2021				2022				2023				2024				2025			
									Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	4.1	Review of public comments - Group 1A	30d	08/04/22	09/14/22	250	100%	Complete																				
	4.2	Review of public comments - Groups (1A, 1B & 2)	30d	11/07/24	12/18/24	259	100%	Complete																				
	4.3	Continue deliberations of policy topics towards a Final Report	50d	11/07/24	01/15/25	250, 259	80%	In Progress																				
	4.4	Build Final Report & Final Deliberations	5d	01/16/25	01/22/25	263	25%	In Progress																				
	4.5	Determine consensus levels on interim recommendations	10d	01/23/25	02/05/25	264		Not Started																				
	4.6	Adopt final recommendations and report	10d	01/23/25	02/05/25	264		Not Started																				
	4.7	Submission of Groups (1A, 1B & 2) Final Report to the GNSO Council	0	02/05/25	02/05/25	266		Not Started																				
	<b>5</b>	<b>- POST GROUP TASKS</b>	<b>95d</b>	<b>02/06/25</b>	<b>06/18/25</b>			<b>Not Started</b>																				
	5.1	Approval of Final Report and Recommendations by the GNSO Council	45d	02/06/25	04/09/25	267		Not Started																				
	5.2	Report to the Board	15d	04/10/25	04/30/25	269		Not Started																				
	5.3	Publish Recommendations for Public Comment	35d	05/01/25	06/18/25	270		Not Started																				
	5.4	Inform GAC if Recommendations affect public policy	5d	05/01/25	05/07/25	270		Not Started																				
		<b>+ PDP CHECKLIST</b>	<b>293d</b>	<b>06/20/20</b>	<b>08/04/21</b>		<b>0%</b>																					

Health	Category	Action Item	Priority	Assigned To	Baseline Finish	Current Finish	Status	Notes
	WP	Meeting #142 Review of public comments on draft Final Report	↓	TPR WG	10/29/24	10/29/24	Complete	
	AI	AI: Ken Herman to consult with his stakeholder group on the "reasonable basis" language in lifting the 30-day transfer lock and determine if there's a preferred middle ground.	—	TPR WG	11/04/24	11/04/24	Complete	
	AI	AI: Members to consider any additional language or criteria to clarify when and how the lock might be lifted, aiming to provide guidance while ensuring registrant security.	—	TPR WG	11/04/24	11/04/24	Complete	
	AI	AI: Members to assess whether specifying UTC as the primary time standard in transfer notifications is suitable and practical, with the option to include other time zones as a secondary reference.	—	TPR WG	11/04/24	11/04/24	Complete	
	AI	AI: Rich Brown to consider possible data-sharing limitations regarding providing identity and contact information of the transfer requester and report back if further clarification is needed.	—	TPR WG	11/04/24	11/04/24	Complete	
	AI	AI: Assignment 4 - Recs #29-33 (Group 2 TEAC + TDRP)	—	TPR WG	11/04/24	11/04/24	Complete	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	11/03/24	11/03/24	Complete	
	WP	Meeting #143 Review of public comments on draft Final Report	↓	TPR WG	11/05/24	11/05/24	Complete	
	WP	Meeting - ICANN81 Review of public comments on draft Final Report	↓	TPR WG	11/09/24	11/09/24	Complete	
	AI	Assignment 5 – Rec #34 – 47 (Group 2 ICANN-approved transfers + BTAPPA)	—	TPR WG	11/25/24	11/25/24	Complete	
	WP	Meeting #144 Review of public comments on draft Final Report	↓	TPR WG	11/26/24	11/26/24	Complete	
	AI	WG Members to consult teams on Rec. 17 feasibility.	—	TPR WG	12/02/24	12/02/24	Complete	
	AI	ICANN Org to refine language for Rec. 9, Rec. 17, and Rec. 18 based on discussions.	—	Policy Support Staff	12/02/24	12/02/24	Complete	
	WP	Meeting #145 Review of public comments on draft Final Report	↓	TPR WG	12/03/24	12/03/24	Complete	
	AI	WG members to gather further input from their stakeholder groups on Recommendation 18.	—	TPR WG	12/09/24	12/09/24	Complete	
	WP	Meeting #146 Review of public comments on draft Final Report	↓	TPR WG	12/10/24	12/10/24	Complete	
	AI	WG members to review the Q3 "Other Comments" [docs.google.com] in the Public Comment Review Tool (PCRT) and flag comments that require further discussion in the WG, i.e., comments, ideas, and issues the WG has not already discussed.	—	TPR WG	12/16/24	12/16/24	Complete	
	AI	WG members to flag recommendations where further discussion is needed, i.e., text that is better discussed during working group meeting time instead via the PCRT or on list.	—	TPR WG	12/16/24	12/16/24	Complete	
	AI	WG to consider ICANN org's comment on Rec. 35, i.e., - An alternative bulk transfer fee model where registries with fewer than 50,000 domains cannot charge fees, and registries with >50,000 domains share the \$50,000 cap.	—	TPR WG	12/16/24	12/16/24	Complete	
	WP	Meeting #147 Review of public comments on draft Final Report	↓	TPR WG	12/17/24	12/17/24	Complete	
	AI	WG group to review responses in the public comment review tool.	—	TPR WG	01/06/25		In Progress	
	AI	ICANN Org to draft revised language for Recommendations 34-36 regarding fee thresholds. Expand explanatory text and rationale for public comments in the final annex.	—	Policy Support Staff	01/06/25		In Progress	
	AI	ICANN Org to consolidate finalized recommendations into the "green box" section. Green Box indicates what would be included in the final report.	—	Policy Support Staff	01/06/25		In Progress	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	12/30/24	12/30/24	Complete	
	WP	Meeting #148 Review of public comments on draft Final Report	↓	TPR WG	01/07/25		In Progress	
	WP	Meeting #149 Review of public comments on draft Final Report	↓	TPR WG	01/14/25		Not Started	
	WP	Meeting #150 Review of public comments on draft Final Report	↓	TPR WG	01/21/25		Not Started	
	WP	Meeting #151 TBD	↓	TPR WG	01/28/25		Not Started	
	WP	Meeting #152 TBD	↓	TPR WG	02/04/25		Not Started	
	MS	Submit Final Report to GNSO Council	!	TPR WG	02/05/25		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	02/10/25		Not Started	
	WP	Meeting #153 TBD	↓	TPR WG	02/11/25		Not Started	
	WP	Meeting #154 TBD	↓	TPR WG	02/18/25		Not Started	
	WP	Meeting #155 TBD	↓	TPR WG	02/25/25		Not Started	
	MS	Submit Monthly Project Package to Council	—	TPR Leadership	03/02/25		Not Started	
	WP	Meeting #156 TBD	↓	TPR WG	03/04/25		Not Started	
	WP	Meeting - ICANN82 TBD	↓	TPR WG	03/08/25		Not Started	
